

# Aggregate Optimization Chart

## Production Gradation Report

**PLANT #:** **P-101**

Sample Date: 5/31/21

Concrete Grade: **DM**

Contractor: \_\_\_\_\_

Dates Test Represents: 6/1/2021 through 6/7/2021

MDOT No.: \_\_\_\_\_

Agg. Class	Pit #	Source	Weight (SSD)	ft <sup>3</sup>	Specific Gravity	% Contribution
6AA	71-47	Presque Isle	1560	9.54	2.62	53.6
26A	71-47	Presque Isle	200	1.22	2.62	6.9
2NS	75-051	Mid-Michigan	1150	6.93	2.66	39.5
<b>Total Wt</b>			<b>2910</b>	<b>17.69</b>		<b>100.0</b>

<----- Verify this number is 100%



**Superior Materials, LLC**  
 30701 W. 10 Mile Rd.  
 Suite 500  
 Farmington Hills, MI 48336

Sieve	6AA	26A	2NS	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	100.0	100.0	100.0	0.0	0.0
1.5"	100.0	100.0	100.0	100.0	0.0	0.0
1"	98.6	100.0	100.0	99.2	0.8	0.8
3/4"	82.7	100.0	100.0	90.7	8.5	9.3
1/2"	39.6	98.2	100.0	67.5	23.2	32.5
3/8"	21.9	89.6	100.0	57.4	10.1	42.6
#4	2.8	26.6	98.8	42.4	15.0	57.6
#8	1.8	8.0	82.2	34.0	8.4	66.0
#16	1.7	4.1	66.0	27.3	6.7	72.7
#30	1.6	2.8	49.6	20.7	6.6	79.3
#50	1.5	2.5	23.9	10.4	10.2	89.6
#100	1.4	2.3	5.4	3.0	7.4	97.0
LBW	1.3	2.0	0.7	1.1	1.9	98.9


\*Maximum % Retained must be above the 3/8" sieve.  
 \*Any two adjacent sieves must equal 10% except max., nom. max., #100 and #200 sieves.  
 \*% Retained must be at least 4% for each sieve except max., nom. max., #100 and #200 sieves.  
 \*% Retained must be at least 8% for the 1" sieve when a 2" max. size (nom. Max. 1.5") aggregate is used.

Production Gradation  Batch Plant Gradations  Aggregate Supplier Gradations

Adjusted WF Initial Production Sample (IPS)

<b>Coarseness Factor:</b>	<b>65</b>	<b>Workability Factor:</b>	<b>34</b>	<b>Adjusted WF</b>	<b>36.5</b>
---------------------------	-----------	----------------------------	-----------	--------------------	-------------

<b>Coarseness Factor:</b>	<b>62</b>
<b>Workability Factor:</b>	<b>35</b>

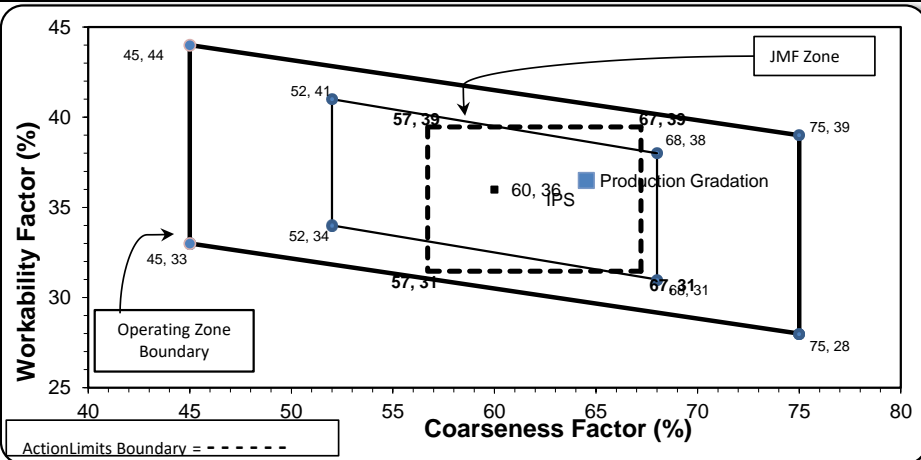

Sieve	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	0.0	0.0
1.5"	100.0	0.0	0.0
1"	100.0	0.0	0.0
3/4"	95.0	5.0	5.0
1/2"	70.5	24.5	29.5
3/8"	60.0	10.5	40.0
#4	44.4	15.6	55.6
#8	35.5	9.0	64.5
#16	28.5	7.0	71.5
#30	21.5	7.0	78.5
#50	10.2	11.3	89.8
#100	3.1	7.1	96.9
LBW	1.3	1.8	98.7

PREPARED BY:  
 SM, LLC Technical Service

Approved By:

# Aggregate Optimization Chart

**PLANT #:** **P-20**

Sample Date: 5/31/21

Concrete Grade: **DM**

Contractor: \_\_\_\_\_

Dates Test Represents: 6/1/2021 through 6/7/2021

MDOT No.: \_\_\_\_\_

Agg. Class	Pit #	Source	Weight (SSD)	ft <sup>3</sup>	Specific Gravity	% Contribution
6AA	71-47	Presque Isle	1605	9.82	2.62	55.2
26A	71-47	Presque Isle	200	1.22	2.62	6.9
2NS	63-92	Grange Hall	1100	6.65	2.65	37.9
<b>Total Wt</b>			<b>2905</b>	<b>17.69</b>		<b>100.0</b>

<----- Verify this number is 100%



**Superior Materials, LLC**  
 30701 W. 10 Mile Rd.  
 Suite 500  
 Farmington Hills, MI 48336

Sieve	6AA	26A	2NS	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	100.0	100.0	100.0	0.0	0.0
1.5"	100.0	100.0	100.0	100.0	0.0	0.0
1"	100.0	100.0	100.0	100.0	0.0	0.0
3/4"	87.7	100.0	100.0	93.2	6.8	6.8
1/2"	42.7	97.4	100.0	68.2	25.0	31.8
3/8"	23.1	90.6	100.0	56.9	11.3	43.1
#4	2.8	22.4	97.5	40.0	16.9	60.0
#8	1.7	4.4	83.4	32.8	7.2	67.2
#16	1.4	2.4	68.0	26.7	6.1	73.3
#30	1.3	2.1	48.4	19.2	7.5	80.8
#50	1.2	2.0	22.0	9.1	10.1	90.9
#100	1.0	1.9	3.2	1.9	7.2	98.1
LBW	0.9	1.7	0.7	0.9	1.0	99.1


\*Maximum % Retained must be above the 3/8" sieve.  
 \*Any two adjacent sieves must equal 10% except max., nom. max., #100 and #200 sieves.  
 \*% Retained must be at least 4% for each sieve except max., nom. max., #100 and #200 sieves.  
 \*% Retained must be at least 8% for the 1" sieve when a 2" max. size (nom. Max. 1.5") aggregate is used.

Production Gradation  Batch Plant Gradations  Aggregate Supplier Gradations

Adjusted WF Initial Production Sample (IPS)

<b>Coarseness Factor:</b>	<b>64</b>	<b>Workability Factor:</b>	<b>33</b>	<b>Adjusted WF</b>	<b>35.3</b>
---------------------------	-----------	----------------------------	-----------	--------------------	-------------

<b>Coarseness Factor:</b>	<b>63</b>
<b>Workability Factor:</b>	<b>36</b>

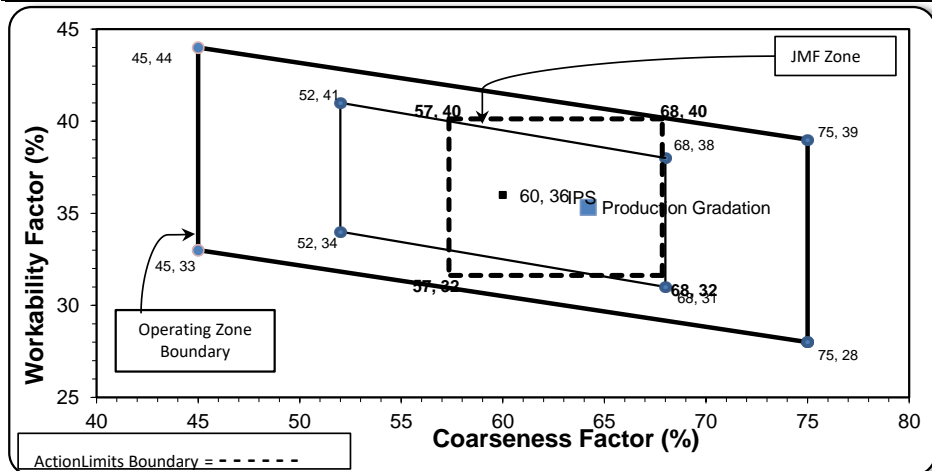

Sieve	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	0.0	0.0
1.5"	100.0	0.0	0.0
1"	100.0	0.0	0.0
3/4"	89.2	10.8	10.8
1/2"	68.4	20.8	31.6
3/8"	59.9	8.6	40.1
#4	43.0	16.9	57.0
#8	35.9	7.1	64.1
#16	29.0	6.8	71.0
#30	21.3	7.7	78.7
#50	9.9	11.4	90.1
#100	2.4	7.5	97.6
LBW	1.2	1.2	98.8

PREPARED BY:  
 SM, LLC Technical Service

Approved By:

# Aggregate Optimization Chart

**PLANT #:** **P-32**

Sample Date: 5/31/21

Concrete Grade: **DM**

Contractor: \_\_\_\_\_

Dates Test Represents: 6/1/2021 through 6/7/2021

MDOT No.: \_\_\_\_\_

Agg. Class	Pit #	Source	Weight (SSD)	ft <sup>3</sup>	Specific Gravity	% Contribution
6AA	71-47	Presque Isle	1450	8.87	2.62	49.9
26A	71-47	Presque Isle	305	1.87	2.62	10.5
2NS	95-013	Smelter Bay	1150	6.95	2.65	39.6
<b>Total Wt</b>			<b>2905</b>	<b>17.69</b>		<b>100.0</b>

<----- Verify this number is 100%



**Superior Materials, LLC**  
 30701 W. 10 Mile Rd.  
 Suite 500  
 Farmington Hills, MI 48336

Sieve	6AA	26A	2NS	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	100.0	100.0	100.0	0.0	0.0
1.5"	100.0	100.0	100.0	100.0	0.0	0.0
1"	96.9	100.0	100.0	98.5	1.5	1.5
3/4"	77.7	100.0	100.0	88.9	9.6	11.1
1/2"	41.1	96.5	100.0	70.2	18.6	29.8
3/8"	21.5	85.7	100.0	59.3	10.9	40.7
#4	3.1	28.6	96.7	42.8	16.5	57.2
#8	2.2	9.1	83.4	35.1	7.8	64.9
#16	2.1	4.7	67.0	28.1	7.0	71.9
#30	2.1	3.6	43.8	18.8	9.3	81.2
#50	2.0	3.1	19.0	8.8	9.9	91.2
#100	1.8	2.2	4.6	3.0	5.9	97.0
LBW	1.4	1.5	1.2	1.3	1.6	98.7


\*Maximum % Retained must be above the 3/8" sieve.  
 \*Any two adjacent sieves must equal 10% except max., nom. max., #100 and #200 sieves.  
 \*% Retained must be at least 4% for each sieve except max., nom. max., #100 and #200 sieves.  
 \*% Retained must be at least 8% for the 1" sieve when a 2" max. size (nom. Max. 1.5") aggregate is used.

Production Gradation  Batch Plant Gradations  Aggregate Supplier Gradations

Adjusted WF Initial Production Sample (IPS)

<b>Coarseness Factor:</b>	<b>63</b>	<b>Workability Factor:</b>	<b>35</b>	<b>37.6</b>
---------------------------	-----------	----------------------------	-----------	-------------

<b>Coarseness Factor:</b>	<b>62</b>
<b>Workability Factor:</b>	<b>36</b>

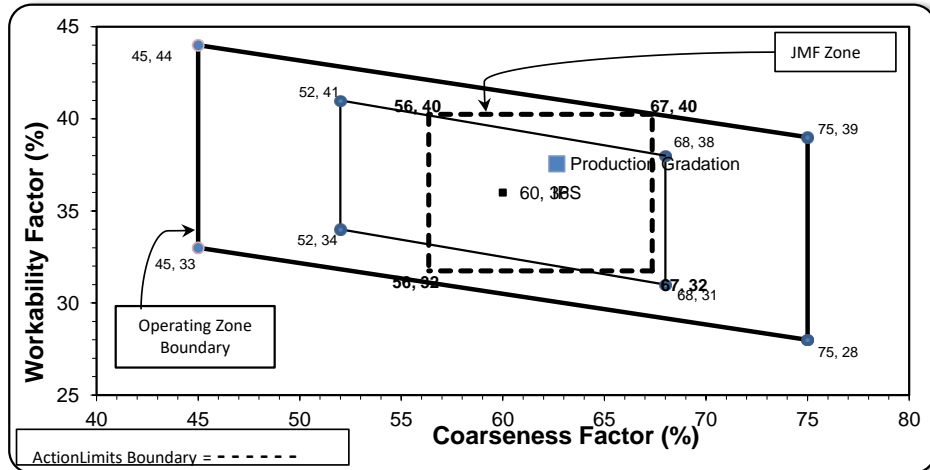

Sieve	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	0.0	0.0
1.5"	100.0	0.0	0.0
1"	100.0	0.0	0.0
3/4"	95.0	5.0	5.0
1/2"	72.3	22.8	27.7
3/8"	60.4	11.8	39.6
#4	42.6	17.8	57.4
#8	36.0	6.6	64.0
#16	29.5	6.5	70.5
#30	20.3	9.2	79.7
#50	9.5	10.8	90.5
#100	3.4	6.1	96.6
LBW	1.3	2.1	98.7

PREPARED BY:  
 SM, LLC Technical Service

Approved By:

# Aggregate Optimization Chart

**PLANT #:** **P-35**

Sample Date: 5/31/21

Concrete Grade: **DM**

Contractor: \_\_\_\_\_

Dates Test Represents: 6/1/2021 through 6/7/2021

MDOT No.: \_\_\_\_\_

Agg. Class	Pit #	Source	Weight (SSD)	ft <sup>3</sup>	Specific Gravity	% Contribution
6AA	58-003	Stoneco	1650	9.83	2.69	55.8
26A	58-003	Stoneco	205	1.22	2.69	6.9
2NS	81-093	Burmeister	1100	6.65	2.65	37.2
<b>Total Wt</b>			<b>2955</b>	<b>17.70</b>		<b>100.0</b>

<----- Verify this number is 100%



**Superior Materials, LLC**  
 30701 W. 10 Mile Rd.  
 Suite 500  
 Farmington Hills, MI 48336

Sieve	6AA	26A	2NS	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	100.0	100.0	100.0	0.0	0.0
1.5"	100.0	100.0	100.0	100.0	0.0	0.0
1"	100.0	100.0	100.0	100.0	0.0	0.0
3/4"	91.9	100.0	100.0	95.5	4.5	4.5
1/2"	54.3	99.5	100.0	74.4	21.0	25.6
3/8"	29.6	89.9	100.0	60.0	14.5	40.0
#4	4.6	12.0	98.0	39.9	20.1	60.1
#8	1.4	3.2	90.2	34.6	5.3	65.4
#16	1.1	2.0	72.5	27.7	6.8	72.3
#30	0.9	1.6	52.2	20.0	7.7	80.0
#50	0.8	1.5	16.6	6.7	13.3	93.3
#100	0.8	1.5	2.9	1.6	5.1	98.4
LBW	0.6	1.3	0.6	0.6	1.0	99.4


\*Maximum % Retained must be above the 3/8" sieve.  
 \*Any two adjacent sieves must equal 10% except max., nom. max., #100 and #200 sieves.  
 \*% Retained must be at least 4% for each sieve except max., nom. max., #100 and #200 sieves.  
 \*% Retained must be at least 8% for the 1" sieve when a 2" max. size (nom. Max. 1.5") aggregate is used.

Production Gradation  Batch Plant Gradations  Aggregate Supplier Gradations

Adjusted WF Initial Production Sample (IPS)

<b>Coarseness Factor:</b>	<b>61</b>	<b>Workability Factor:</b>	<b>35</b>	<b>37.1</b>
---------------------------	-----------	----------------------------	-----------	-------------

<b>Coarseness Factor:</b>	<b>61</b>
<b>Workability Factor:</b>	<b>36</b>

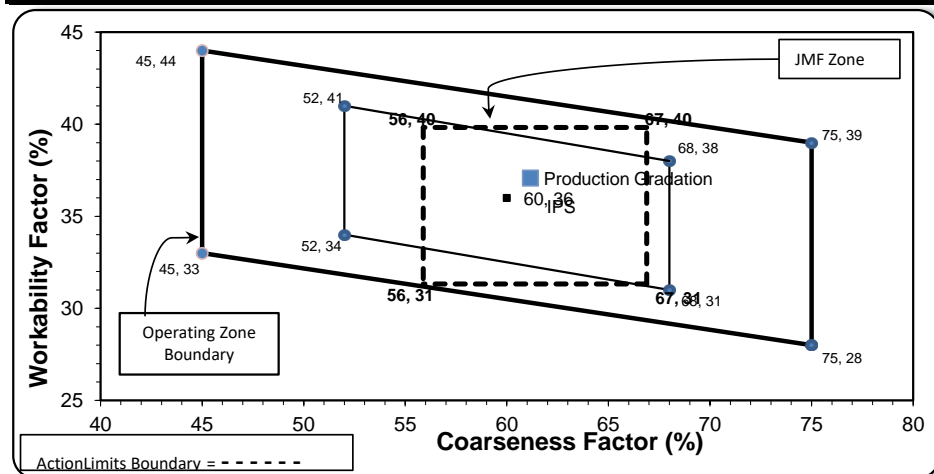

Sieve	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	0.0	0.0
1.5"	100.0	0.0	0.0
1"	99.3	0.7	0.7
3/4"	89.1	10.2	10.9
1/2"	70.5	18.6	29.5
3/8"	60.5	10.0	39.5
#4	44.1	16.4	55.9
#8	35.6	8.5	64.4
#16	27.7	7.9	72.3
#30	20.6	7.1	79.4
#50	8.7	11.8	91.3
#100	1.6	7.1	98.4
LBW	1.1	0.6	98.9

PREPARED BY:  
 SM, LLC Technical Service

Approved By:

# Aggregate Optimization Chart

**PLANT #:** **P-36**

Sample Date: 5/31/21

Concrete Grade: **DM**

Contractor: \_\_\_\_\_

Dates Test Represents: 6/1/2021 through 6/7/2021

MDOT No.: \_\_\_\_\_

Agg. Class	Pit #	Source	Weight (SSD)	ft <sup>3</sup>	Specific Gravity	% Contribution
6AA	71-47	Presque Isle	1405	8.59	2.62	48.4
26A	71-47	Presque Isle	400	2.45	2.62	13.8
2NS	63-92	Grange Hall	1100	6.65	2.65	37.9
<b>Total Wt</b>			<b>2905</b>	<b>17.69</b>		<b>100.0</b>

<----- Verify this number is 100%



**Superior Materials, LLC**  
 30701 W. 10 Mile Rd.  
 Suite 500  
 Farmington Hills, MI 48336

Sieve	6AA	26A	2NS	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	100.0	100.0	100.0	0.0	0.0
1.5"	100.0	100.0	100.0	100.0	0.0	0.0
1"	98.8	100.0	100.0	99.4	0.6	0.6
3/4"	78.8	100.0	100.0	89.7	9.7	10.3
1/2"	42.2	96.5	100.0	71.6	18.2	28.4
3/8"	22.7	85.7	100.0	60.6	10.9	39.4
#4	4.9	28.6	97.5	43.2	17.4	56.8
#8	3.0	9.1	83.4	34.3	8.9	65.7
#16	2.6	4.7	68.0	27.7	6.6	72.3
#30	2.4	3.6	48.4	20.0	7.7	80.0
#50	2.2	3.1	22.0	9.8	10.2	90.2
#100	2.0	2.2	3.2	2.5	7.3	97.5
LBW	1.6	1.5	0.7	1.2	1.2	98.8


\*Maximum % Retained must be above the 3/8" sieve.  
 \*Any two adjacent sieves must equal 10% except max., nom. max., #100 and #200 sieves.  
 \*% Retained must be at least 4% for each sieve except max., nom. max., #100 and #200 sieves.  
 \*% Retained must be at least 8% for the 1" sieve when a 2" max. size (nom. Max. 1.5") aggregate is used.

Production Gradation  Batch Plant Gradations  Aggregate Supplier Gradations

Adjusted WF Initial Production Sample (IPS)

<b>Coarseness Factor:</b>	<b>60</b>	<b>Workability Factor:</b>	<b>34</b>	<b>Adjusted WF</b>	<b>36.8</b>
---------------------------	-----------	----------------------------	-----------	--------------------	-------------

<b>Coarseness Factor:</b>	<b>63</b>
<b>Workability Factor:</b>	<b>35</b>

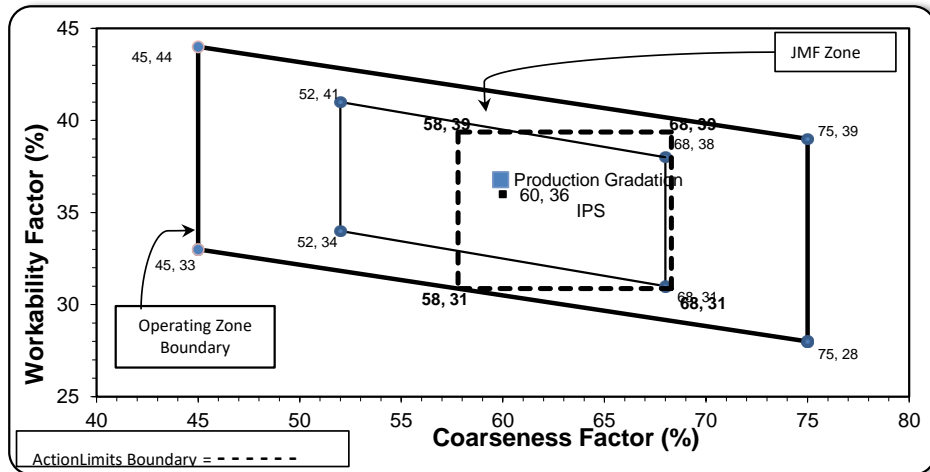

Sieve	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	0.0	0.0
1.5"	100.0	0.0	0.0
1"	99.1	0.9	0.9
3/4"	90.3	8.8	9.7
1/2"	69.2	21.1	30.8
3/8"	59.1	10.1	40.9
#4	41.8	17.3	58.2
#8	35.1	6.6	64.9
#16	28.5	6.6	71.5
#30	21.2	7.3	78.8
#50	8.7	12.5	91.3
#100	1.8	7.0	98.2
LBW	0.7	1.0	99.3

PREPARED BY:  
 SM, LLC Technical Service

Approved By:

# Aggregate Optimization Chart

**PLANT #:** **P-39**

Sample Date: 5/31/21 Concrete Grade: **DM**  
 Dates Test Represents: 6/1/2021 through 6/7/2021

Contractor: \_\_\_\_\_

MDOT No.: \_\_\_\_\_

Agg. Class	Pit #	Source	Weight (SSD)	ft <sup>3</sup>	Specific Gravity	% Contribution
6AA	71-47	Presque Isle	1605	9.82	2.62	55.2
26A	71-47	Presque Isle	200	1.22	2.62	6.9
2NS	44-051	Krake Willis Rd	1100	6.65	2.65	37.9
<b>Total Wt</b>			<b>2905</b>	<b>17.69</b>		<b>100.0</b>

<----- Verify this number is 100%

Sieve	6AA	26A	2NS	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	100.0	100.0	100.0	0.0	0.0
1.5"	100.0	100.0	100.0	100.0	0.0	0.0
1"	98.6	100.0	100.0	99.2	0.8	0.8
3/4"	82.7	100.0	100.0	90.4	8.8	9.6
1/2"	39.6	98.2	100.0	66.5	23.9	33.5
3/8"	21.9	89.6	100.0	56.1	10.4	43.9
#4	2.8	26.6	97.1	40.1	16.0	59.9
#8	1.8	8.0	79.2	31.5	8.6	68.5
#16	1.7	4.1	63.2	25.2	6.4	74.8
#30	1.6	2.8	48.5	19.4	5.7	80.6
#50	1.5	2.5	28.6	11.8	7.6	88.2
#100	1.4	2.3	9.0	4.3	7.5	95.7
LBW	1.3	2.0	1.2	1.3	3.0	98.7

\*Maximum % Retained must be above the 3/8" sieve.  
 \*Any two adjacent sieves must equal 10% except max., nom. max., #100 and #200 sieves.  
 \*% Retained must be at least 4% for each sieve except max., nom. max., #100 and #200 sieves.  
 \*% Retained must be at least 8% for the 1" sieve when a 2" max. size (nom. Max. 1.5") aggregate is used.




**Superior Materials, LLC**  
 30701 W. 10 Mile Rd.  
 Suite 500  
 Farmington Hills, MI 48336

Production Gradation  Batch Plant Gradations  Aggregate Supplier Gradations

Adjusted WF Initial Production Sample (IPS)

<b>Coarseness Factor:</b>	<b>64</b>	<b>Workability Factor:</b>	<b>32</b>	<b>34.0</b>
---------------------------	-----------	----------------------------	-----------	-------------

<b>Coarseness Factor:</b>	<b>63</b>
<b>Workability Factor:</b>	<b>36</b>

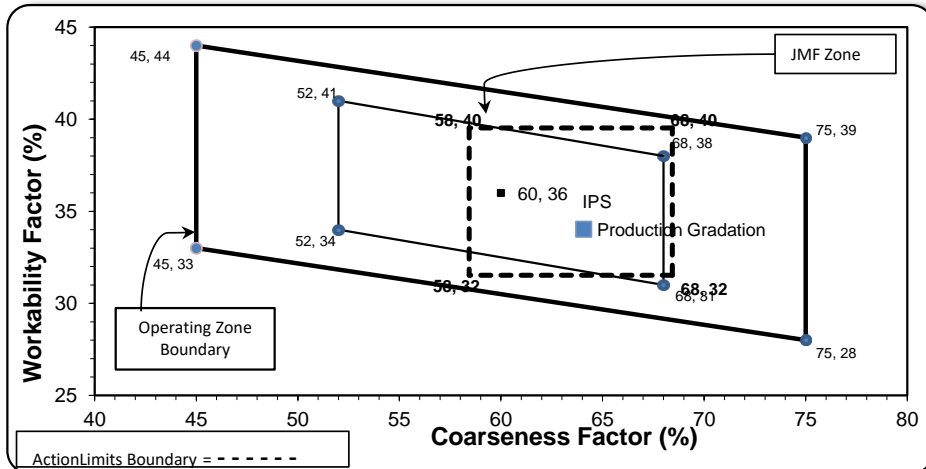

Sieve	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	0.0	0.0
1.5"	100.0	0.0	0.0
1"	100.0	0.0	0.0
3/4"	89.7	10.3	10.3
1/2"	70.3	19.4	29.7
3/8"	59.1	11.2	40.9
#4	42.8	16.3	57.2
#8	35.5	7.3	64.5
#16	29.0	6.5	71.0
#30	21.2	7.7	78.8
#50	9.8	11.5	90.2
#100	3.7	6.1	96.3
LBW	1.2	2.5	98.8

PREPARED BY:  
 SM, LLC Technical Service

Approved By:

# Aggregate Optimization Chart

**PLANT #:** P-02

Contractor: \_\_\_\_\_

Sample Date: 5/31/21

Concrete Grade: DM

Dates Test Represents: 6/1/2021 through 6/7/2021

MDOT No.: \_\_\_\_\_

Agg. Class	Pit #	Source	Weight (SSD)	ft <sup>3</sup>	Specific Gravity	% Contribution
6AA	71-47	Presque Isle	1450	8.87	2.62	49.9
26A	71-47	Presque Isle	355	2.17	2.62	12.2
2NS	63-115	Ray Rd	1100	6.65	2.65	37.9
<b>Total Wt</b>			<b>2905</b>	<b>17.69</b>		<b>100.0</b>

<----- Verify this number is 100%



**Superior Materials, LLC**  
 30701 W. 10 Mile Rd.  
 Suite 500  
 Farmington Hills, MI 48336

Sieve	6AA	26A	2NS	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	100.0	100.0	100.0	0.0	0.0
1.5"	100.0	100.0	100.0	100.0	0.0	0.0
1"	98.8	100.0	100.0	99.4	0.6	0.6
3/4"	78.8	100.0	100.0	89.4	10.0	10.6
1/2"	42.2	96.5	100.0	70.7	18.7	29.3
3/8"	22.7	85.7	100.0	59.7	11.1	40.3
#4	4.9	28.6	96.4	42.4	17.2	57.6
#8	3.0	9.1	79.7	32.8	9.7	67.2
#16	2.6	4.7	64.3	26.2	6.6	73.8
#30	2.4	3.6	48.1	19.9	6.4	80.1
#50	2.2	3.1	24.5	10.8	9.1	89.2
#100	2.0	2.2	5.2	3.2	7.5	96.8
LBW	1.6	1.5	0.6	1.2	2.0	98.8


\*Maximum % Retained must be above the 3/8" sieve.  
 \*Any two adjacent sieves must equal 10% except max., nom. max., #100 and #200 sieves.  
 \*% Retained must be at least 4% for each sieve except max., nom. max., #100 and #200 sieves.  
 \*% Retained must be at least 8% for the 1" sieve when a 2" max. size (nom. Max. 1.5") aggregate is used.

Production Gradation  Batch Plant Gradations  Aggregate Supplier Gradations

Adjusted WF Initial Production Sample (IPS)

<b>Coarseness Factor:</b>	<b>60</b>	<b>Workability Factor:</b>	<b>33</b>	<b>Adjusted WF</b>	<b>35.3</b>
---------------------------	-----------	----------------------------	-----------	--------------------	-------------

<b>Coarseness Factor:</b>	<b>63</b>
<b>Workability Factor:</b>	<b>35</b>

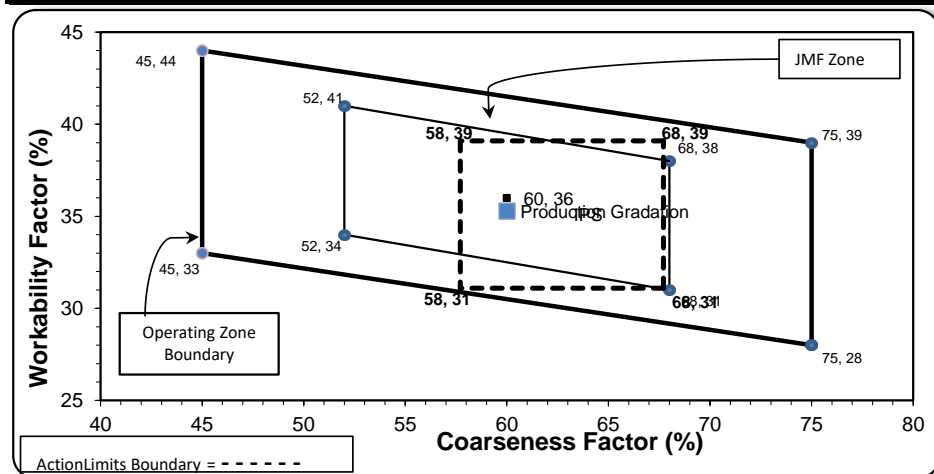

Sieve	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	0.0	0.0
1.5"	100.0	0.0	0.0
1"	100.0	0.0	0.0
3/4"	95.1	4.9	4.9
1/2"	74.6	20.5	25.4
3/8"	59.3	15.3	40.7
#4	42.1	17.2	57.9
#8	35.1	7.1	64.9
#16	29.2	5.9	70.8
#30	21.9	7.3	78.1
#50	9.6	12.4	90.4
#100	2.4	7.2	97.6
LBW	0.9	1.5	99.1

PREPARED BY:  
 SM, LLC Technical Service

Approved By:
