

Aggregate Optimization Chart

PLANT #: **P-32**

Sample Date: 2/22/21 Concrete Grade: **S2M**
 Dates Test Represents: 2/23/2021 through 3/1/2021

Contractor: _____

MDOT No.: _____

Agg. Class	Pit #	Source	Weight (SSD)	ft ³	Specific Gravity	% Contribution
6AA	71-47	Presque Isle	1470	8.99	2.62	48.2
26A	71-47	Presque Isle	350	2.14	2.62	11.5
2NS	95-013	Smelter Bay	1230	7.44	2.65	40.3
Total Wt			3050	18.57		100.0

<----- Verify this number is 100%




Superior Materials, LLC
 30701 W. 10 Mile Rd.
 Suite 500
 Farmington Hills, MI 48336

Sieve	6AA	26A	2NS	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	100.0	100.0	100.0	0.0	0.0
1.5"	100.0	100.0	100.0	100.0	0.0	0.0
1"	97.9	100.0	100.0	99.0	1.0	1.0
3/4"	74.9	100.0	100.0	87.9	11.1	12.1
1/2"	35.6	98.5	100.0	68.8	19.1	31.2
3/8"	19.8	87.7	100.0	59.9	8.9	40.1
#4	3.8	18.7	97.4	43.3	16.7	56.7
#8	2.1	5.4	82.8	35.0	8.2	65.0
#16	1.8	2.7	68.0	28.6	6.4	71.4
#30	1.6	2.1	49.2	20.9	7.7	79.1
#50	1.4	2.0	20.7	9.3	11.6	90.7
#100	1.3	1.8	4.6	2.7	6.6	97.3
LBW	1.0	1.6	1.3	1.2	1.5	98.8

*Maximum % Retained must be above the 3/8" sieve.
 *Any two adjacent sieves must equal 10% except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 4% for each sieve except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 8% for the 1" sieve when a 2" max. size (nom. Max. 1.5") aggregate is used.

Production Gradation Batch Plant Gradations Aggregate Supplier Gradations

Coarseness Factor: **62** **Workability Factor:** **35**

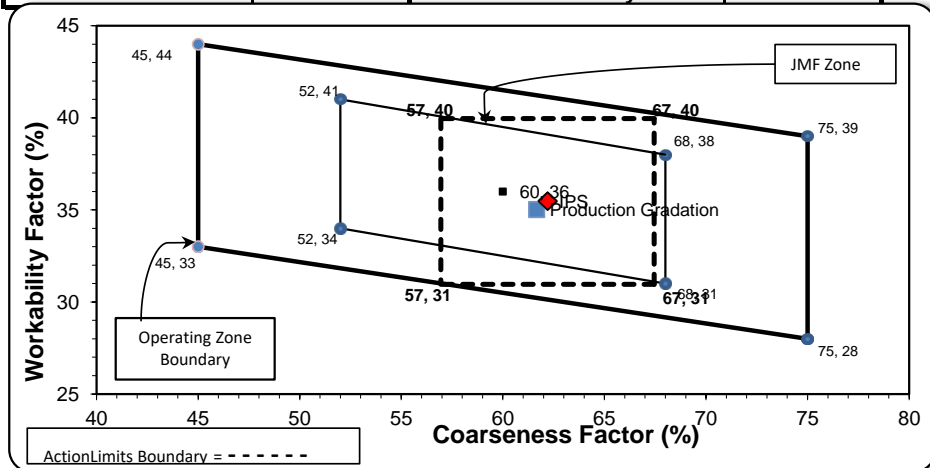

Initial Production Sample (IPS)

Coarseness Factor: 62		Workability Factor: 35	
Sieve	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	0.0	0.0
1.5"	100.0	0.0	0.0
1"	100.0	0.0	0.0
3/4"	94.0	6.0	6.0
1/2"	70.2	23.7	29.8
3/8"	59.9	10.4	40.1
#4	42.7	17.2	57.3
#8	35.5	7.2	64.5
#16	28.4	7.0	71.6
#30	19.2	9.2	80.8
#50	8.9	10.3	91.1
#100	3.1	5.9	96.9
LBW	1.4	1.7	98.6

PREPARED BY:
 SM, LLC Technical Service

Approved By:

Aggregate Optimization Chart

PLANT #: **P-02**

Sample Date: 2/22/21 Concrete Grade: **S2M**
 Dates Test Represents: 2/23/2021 through 3/1/2021

Contractor: _____

MDOT No.: _____

Agg. Class	Pit #	Source	Weight (SSD)	ft ³	Specific Gravity	% Contribution
6AA	71-47	Presque Isle	1450	8.87	2.62	47.5
26A	71-47	Presque Isle	300	1.83	2.62	9.8
2NS	63-115	Ray Rd	1300	7.86	2.65	42.6
Total Wt			3050	18.57		100.0

<----- Verify this number is 100%




Superior Materials, LLC
 30701 W. 10 Mile Rd.
 Suite 500
 Farmington Hills, MI 48336

Sieve	6AA	26A	2NS	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	100.0	100.0	100.0	0.0	0.0
1.5"	100.0	100.0	100.0	100.0	0.0	0.0
1"	98.1	100.0	100.0	99.1	0.9	0.9
3/4"	72.5	100.0	100.0	86.9	12.2	13.1
1/2"	31.8	98.5	100.0	67.4	19.5	32.6
3/8"	14.0	87.7	100.0	57.9	9.5	42.1
#4	1.9	18.7	97.2	44.2	13.7	55.8
#8	1.7	5.4	81.4	36.0	8.1	64.0
#16	1.7	2.7	65.4	28.9	7.1	71.1
#30	1.6	2.1	49.2	21.9	7.0	78.1
#50	1.6	2.0	23.2	10.8	11.1	89.2
#100	1.5	1.8	3.9	2.6	8.3	97.4
LBW	1.0	1.6	0.6	0.9	1.7	99.1

*Maximum % Retained must be above the 3/8" sieve.
 *Any two adjacent sieves must equal 10% except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 4% for each sieve except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 8% for the 1" sieve when a 2" max. size (nom. Max. 1.5") aggregate is used.

Production Gradation Batch Plant Gradations Aggregate Supplier Gradations

Coarseness Factor: **66** **Workability Factor:** **36**

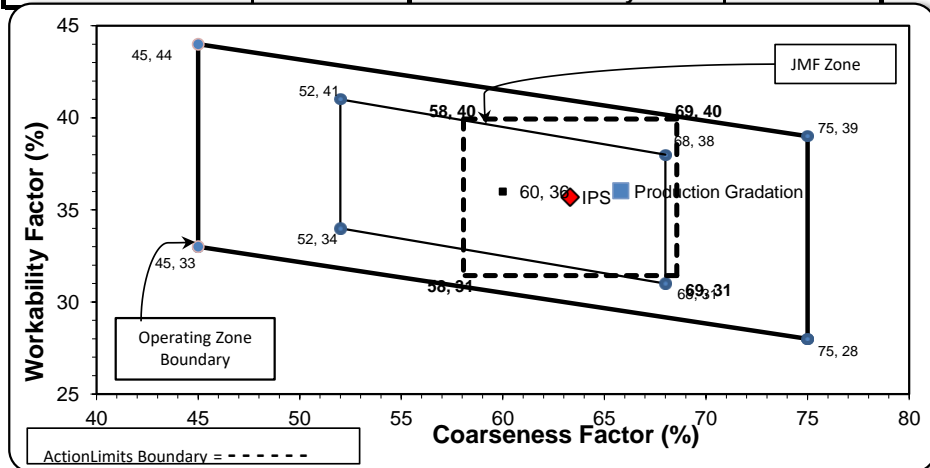

Initial Production Sample (IPS)

Coarseness Factor: **63**
Workability Factor: **36**

Sieve	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	0.0	0.0
1.5"	100.0	0.0	0.0
1"	100.0	0.0	0.0
3/4"	95.6	4.4	4.4
1/2"	73.1	22.6	26.9
3/8"	59.3	13.8	40.7
#4	42.8	16.5	57.2
#8	35.7	7.1	64.3
#16	28.9	6.8	71.1
#30	20.7	8.2	79.3
#50	9.9	10.8	90.1
#100	2.1	7.8	97.9
LBW	0.9	1.2	99.1

PREPARED BY:
 SM, LLC Technical Service

Approved By:
