

Aggregate Optimization Chart

PLANT #: **P-32**

Sample Date: 3/8/21 Concrete Grade: **S2M**
 Dates Test Represents: 3/9/2021 through 3/15/2021

Contractor: _____

MDOT No.: _____

Agg. Class	Pit #	Source	Weight (SSD)	ft ³	Specific Gravity	% Contribution
6AA	71-47	Presque Isle	1420	8.69	2.62	46.6
26A	71-47	Presque Isle	400	2.45	2.62	13.1
2NS	95-013	Smelter Bay	1230	7.44	2.65	40.3
Total Wt			3050	18.57		100.0

<----- Verify this number is 100%




Superior Materials, LLC
 30701 W. 10 Mile Rd.
 Suite 500
 Farmington Hills, MI 48336

Sieve	6AA	26A	2NS	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	100.0	100.0	100.0	0.0	0.0
1.5"	100.0	100.0	100.0	100.0	0.0	0.0
1"	97.2	100.0	100.0	98.7	1.3	1.3
3/4"	70.7	100.0	100.0	86.4	12.3	13.6
1/2"	30.1	97.3	100.0	67.1	19.3	32.9
3/8"	11.6	88.4	100.0	57.3	9.8	42.7
#4	2.4	14.7	96.2	41.8	15.5	58.2
#8	2.0	4.2	83.6	35.2	6.6	64.8
#16	1.9	2.1	67.4	28.3	6.9	71.7
#30	1.8	1.7	45.2	19.3	9.1	80.7
#50	1.7	1.5	18.3	8.4	10.9	91.6
#100	1.5	1.4	4.4	2.7	5.7	97.3
LBW	1.2	1.2	0.9	1.1	1.6	98.9

*Maximum % Retained must be above the 3/8" sieve.
 *Any two adjacent sieves must equal 10% except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 4% for each sieve except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 8% for the 1" sieve when a 2" max. size (nom. Max. 1.5") aggregate is used.

Production Gradation Batch Plant Gradations Aggregate Supplier Gradations

Coarseness Factor: **66** **Workability Factor:** **35**

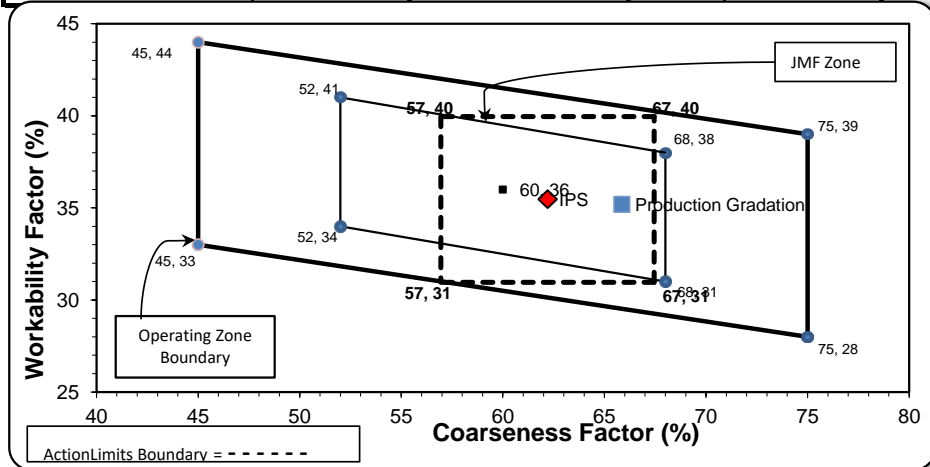

Initial Production Sample (IPS)

Coarseness Factor: **62**
Workability Factor: **35**

Sieve	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	0.0	0.0
1.5"	100.0	0.0	0.0
1"	100.0	0.0	0.0
3/4"	94.0	6.0	6.0
1/2"	70.2	23.7	29.8
3/8"	59.9	10.4	40.1
#4	42.7	17.2	57.3
#8	35.5	7.2	64.5
#16	28.4	7.0	71.6
#30	19.2	9.2	80.8
#50	8.9	10.3	91.1
#100	3.1	5.9	96.9
LBW	1.4	1.7	98.6

PREPARED BY:
 SM, LLC Technical Service

Approved By:

Aggregate Optimization Chart

PLANT #: **P-02**

Sample Date: 3/8/21 Concrete Grade: **S2M**
 Dates Test Represents: 3/9/2021 through 3/15/2021

Contractor: _____

MDOT No.: _____

Agg. Class	Pit #	Source	Weight (SSD)	ft ³	Specific Gravity	% Contribution
6AA	71-47	Presque Isle	1450	8.87	2.62	47.5
26A	71-47	Presque Isle	300	1.83	2.62	9.8
2NS	63-115	Ray Rd	1300	7.86	2.65	42.6
Total Wt			3050	18.57		100.0

<----- Verify this number is 100%




Superior Materials, LLC
 30701 W. 10 Mile Rd.
 Suite 500
 Farmington Hills, MI 48336

Sieve	6AA	26A	2NS	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	100.0	100.0	100.0	0.0	0.0
1.5"	100.0	100.0	100.0	100.0	0.0	0.0
1"	99.2	100.0	100.0	99.6	0.4	0.4
3/4"	75.5	100.0	100.0	88.4	11.3	11.6
1/2"	33.2	97.3	100.0	68.0	20.4	32.0
3/8"	16.9	88.4	100.0	59.4	8.6	40.6
#4	2.9	14.7	97.5	44.4	15.0	55.6
#8	1.8	4.2	79.8	35.3	9.1	64.7
#16	1.7	2.1	61.4	27.2	8.1	72.8
#30	1.6	1.7	44.5	19.9	7.3	80.1
#50	1.5	1.5	19.8	9.3	10.6	90.7
#100	1.4	1.4	3.4	2.3	7.0	97.7
LBW	1.1	1.2	0.5	0.9	1.4	99.1

*Maximum % Retained must be above the 3/8" sieve.
 *Any two adjacent sieves must equal 10% except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 4% for each sieve except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 8% for the 1" sieve when a 2" max. size (nom. Max. 1.5") aggregate is used.

Production Gradation Batch Plant Gradations Aggregate Supplier Gradations

Coarseness Factor: **63** **Workability Factor:** **35**

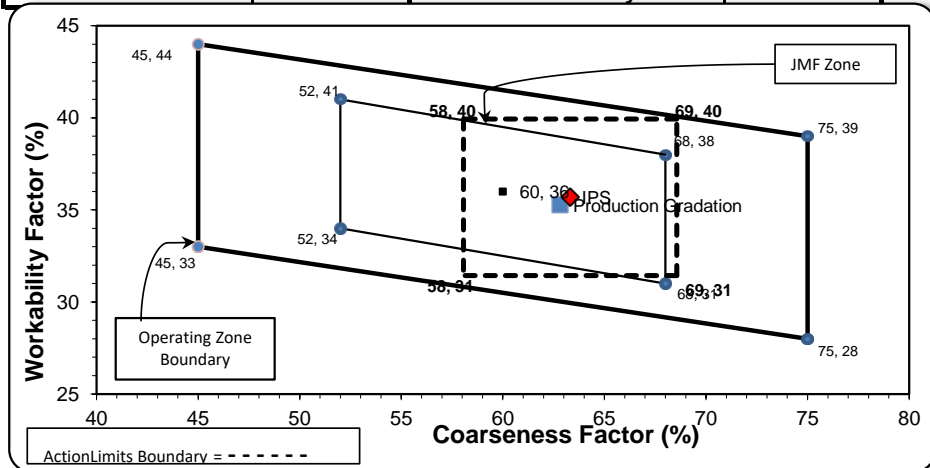

Initial Production Sample (IPS)

Coarseness Factor: **63**
Workability Factor: **36**

Sieve	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	0.0	0.0
1.5"	100.0	0.0	0.0
1"	100.0	0.0	0.0
3/4"	95.6	4.4	4.4
1/2"	73.1	22.6	26.9
3/8"	59.3	13.8	40.7
#4	42.8	16.5	57.2
#8	35.7	7.1	64.3
#16	28.9	6.8	71.1
#30	20.7	8.2	79.3
#50	9.9	10.8	90.1
#100	2.1	7.8	97.9
LBW	0.9	1.2	99.1

PREPARED BY:
 SM, LLC Technical Service

Approved By:
