

Aggregate Optimization Chart

PLANT #: **P-101**

Sample Date: 10/12/20

Concrete Grade: **S2M**

Contractor: _____

Dates Test Represents: 10/13/2020 through 10/19/2020

MDOT No.: _____

Agg. Class	Pit #	Source	Weight (SSD)	ft ³	Specific Gravity	% Contribution
6AA	71-47	Presque Isle	1675	10.25	2.62	54.8
26A	71-47	Presque Isle	150	0.92	2.62	4.9
2NS	75-051	Mid-Michigan	1230	7.41	2.66	40.3
Total Wt			3055	18.57		100.0

<----- Verify this number is 100%



Superior Materials, LLC
 30701 W. 10 Mile Rd.
 Suite 500
 Farmington Hills, MI 48336

Sieve	6AA	26A	2NS	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	100.0	100.0	100.0	0.0	0.0
1.5"	100.0	100.0	100.0	100.0	0.0	0.0
1"	99.5	100.0	100.0	99.7	0.3	0.3
3/4"	88.6	100.0	100.0	93.7	6.0	6.3
1/2"	50.7	97.9	100.0	72.9	20.9	27.1
3/8"	28.4	88.4	100.0	60.2	12.7	39.8
#4	3.7	23.9	98.2	42.7	17.4	57.3
#8	1.9	6.8	82.4	34.6	8.2	65.4
#16	1.7	3.0	67.1	28.1	6.5	71.9
#30	1.6	2.2	51.9	21.9	6.2	78.1
#50	1.5	2.0	27.2	11.9	10.0	88.1
#100	1.5	1.9	4.7	2.8	9.1	97.2
LBW	1.4	1.7	0.7	1.1	1.7	98.9

*Maximum % Retained must be above the 3/8" sieve.
 *Any two adjacent sieves must equal 10% except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 4% for each sieve except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 8% for the 1" sieve when a 2" max. size (nom. Max. 1.5") aggregate is used.

Production Gradation Batch Plant Gradations Aggregate Supplier Gradations


Coarseness Factor:	61	Workability Factor:	35
---------------------------	-----------	----------------------------	-----------

Initial Production Sample (IPS)

Coarseness Factor:	64
---------------------------	-----------

Workability Factor:	35
----------------------------	-----------

Sieve	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	0.0	0.0
1.5"	100.0	0.0	0.0
1"	100.0	0.0	0.0
3/4"	93.9	6.1	6.1
1/2"	71.4	22.5	28.6
3/8"	59.0	12.4	41.0
#4	45.1	13.9	54.9
#8	35.5	9.6	64.5
#16	28.3	7.2	71.7
#30	21.3	6.9	78.7
#50	11.0	10.3	89.0
#100	3.4	7.6	96.6
LBW	1.1	2.3	98.9

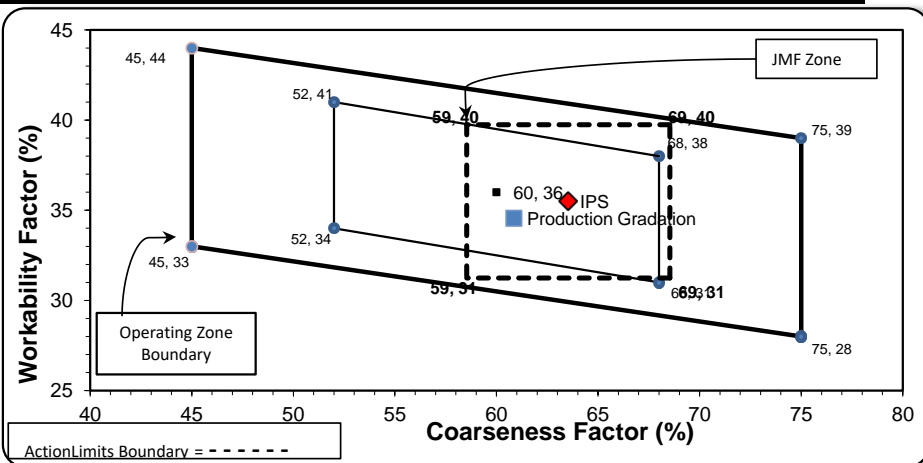

PREPARED BY:
 SM, LLC Technical Service

Approved By:

Aggregate Optimization Chart

PLANT #: **P-102**

Sample Date: 10/12/20

Concrete Grade: **S2M**

Contractor: _____

Dates Test Represents: 10/13/2020 through 10/19/2020

MDOT No.: _____

Agg. Class	Pit #	Source	Weight (SSD)	ft ³	Specific Gravity	% Contribution
6AA	58-003	Stoneco	1550	9.23	2.69	50.0
26A	58-003	Stoneco	340	2.03	2.69	11.0
2NS	63-114	Highland	1210	7.32	2.65	39.0
Total Wt			3100	18.58		100.0

<----- Verify this number is 100%




Superior Materials, LLC
 30701 W. 10 Mile Rd.
 Suite 500
 Farmington Hills, MI 48336

Sieve	6AA	26A	2NS	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	100.0	100.0	100.0	0.0	0.0
1.5"	100.0	100.0	100.0	100.0	0.0	0.0
1"	99.4	100.0	100.0	99.7	0.3	0.3
3/4"	81.4	100.0	100.0	90.7	9.0	9.3
1/2"	49.6	99.0	100.0	74.7	16.0	25.3
3/8"	23.8	74.7	100.0	59.1	15.6	40.9
#4	6.2	27.0	99.1	44.7	14.4	55.3
#8	1.8	9.1	83.7	34.6	10.2	65.4
#16	1.2	3.3	65.7	26.6	8.0	73.4
#30	1.0	2.4	46.5	18.9	7.7	81.1
#50	0.8	2.3	18.2	7.8	11.2	92.2
#100	0.8	2.1	3.9	2.2	5.6	97.8
LBW	0.8	1.7	0.4	0.7	1.4	99.3

*Maximum % Retained must be above the 3/8" sieve.
 *Any two adjacent sieves must equal 10% except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 4% for each sieve except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 8% for the 1" sieve when a 2" max. size (nom. Max. 1.5") aggregate is used.

Production Gradation Batch Plant Gradations Aggregate Supplier Gradations

Coarseness Factor:	62	Workability Factor:	35
---------------------------	-----------	----------------------------	-----------

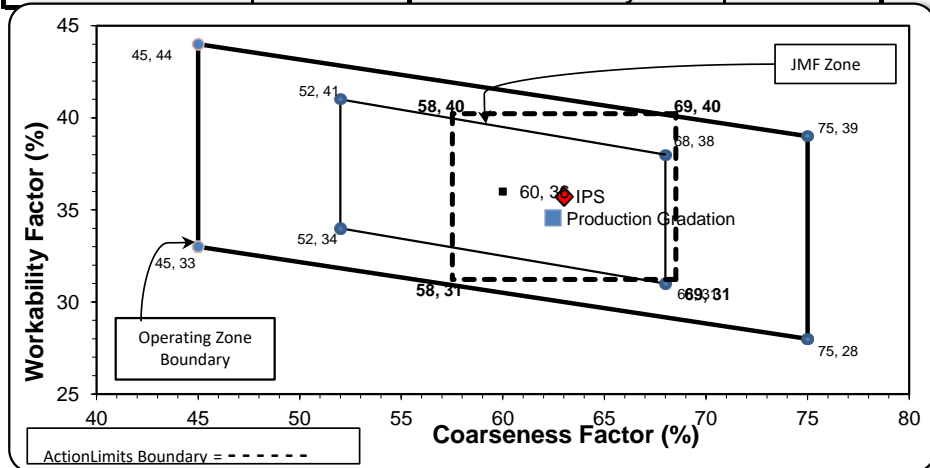

Initial Production Sample (IPS)

Coarseness Factor:	63		
Workability Factor:	36		
Sieve	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	0.0	0.0
1.5"	100.0	0.0	0.0
1"	99.2	0.8	0.8
3/4"	90.9	8.3	9.1
1/2"	71.3	19.6	28.7
3/8"	59.5	11.8	40.5
#4	43.8	15.7	56.2
#8	35.7	8.1	64.3
#16	27.0	8.7	73.0
#30	18.6	8.4	81.4
#50	6.8	11.8	93.2
#100	1.4	5.4	98.6
LBW	0.6	0.8	99.4

PREPARED BY:
 SM, LLC Technical Service

Approved By:

Aggregate Optimization Chart

PLANT #: **P-103**

Sample Date: 10/12/20

Concrete Grade: **S2M**

Contractor: _____

Dates Test Represents: 10/13/2020 through 10/19/2020

MDOT No.: _____

Agg. Class	Pit #	Source	Weight (SSD)	ft ³	Specific Gravity	% Contribution
6AA	58-003	Stoneco	1550	9.23	2.69	50.0
26A	58-003	Stoneco	340	2.03	2.69	11.0
2NS	63-114	Highland	1210	7.32	2.65	39.0
Total Wt			3100	18.58		100.0

<----- Verify this number is 100%




Superior Materials, LLC
 30701 W. 10 Mile Rd.
 Suite 500
 Farmington Hills, MI 48336

Sieve	6AA	26A	2NS	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	100.0	100.0	100.0	0.0	0.0
1.5"	100.0	100.0	100.0	100.0	0.0	0.0
1"	99.4	100.0	100.0	99.7	0.3	0.3
3/4"	81.4	100.0	100.0	90.7	9.0	9.3
1/2"	49.6	99.0	100.0	74.7	16.0	25.3
3/8"	23.8	74.7	100.0	59.1	15.6	40.9
#4	6.2	27.0	99.1	44.7	14.4	55.3
#8	1.8	9.1	83.7	34.6	10.2	65.4
#16	1.2	3.3	65.7	26.6	8.0	73.4
#30	1.0	2.4	46.5	18.9	7.7	81.1
#50	0.8	2.3	18.2	7.8	11.2	92.2
#100	0.8	2.1	3.9	2.2	5.6	97.8
LBW	0.8	1.7	0.4	0.7	1.4	99.3

*Maximum % Retained must be above the 3/8" sieve.
 *Any two adjacent sieves must equal 10% except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 4% for each sieve except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 8% for the 1" sieve when a 2" max. size (nom. Max. 1.5") aggregate is used.

Production Gradation Batch Plant Gradations Aggregate Supplier Gradations

Coarseness Factor:	62	Workability Factor:	35
---------------------------	-----------	----------------------------	-----------

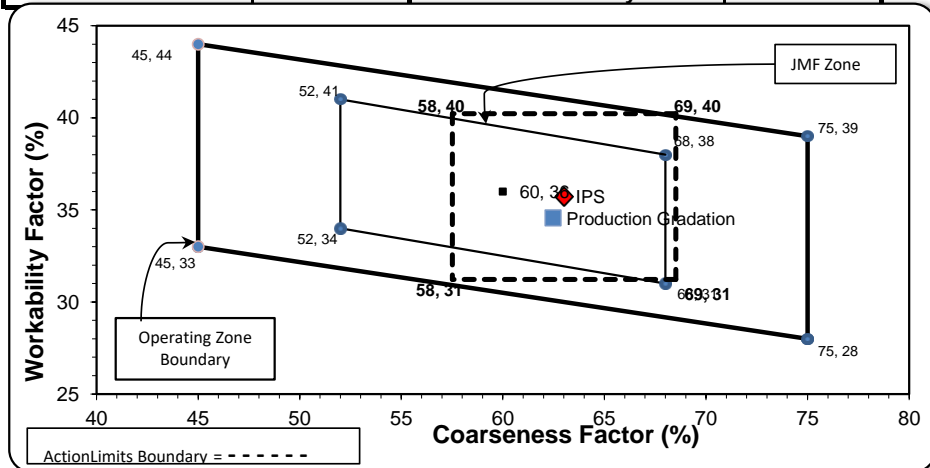

Initial Production Sample (IPS)

Coarseness Factor:	63		
Workability Factor:	36		
Sieve	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	0.0	0.0
1.5"	100.0	0.0	0.0
1"	99.2	0.8	0.8
3/4"	90.9	8.3	9.1
1/2"	71.3	19.6	28.7
3/8"	59.5	11.8	40.5
#4	43.8	15.7	56.2
#8	35.7	8.1	64.3
#16	27.0	8.7	73.0
#30	18.6	8.4	81.4
#50	6.8	11.8	93.2
#100	1.4	5.4	98.6
LBW	0.6	0.8	99.4

PREPARED BY:
 SM, LLC Technical Service

Approved BY:

Aggregate Optimization Chart

PLANT #: **P-12**

Sample Date: 10/12/20

Concrete Grade: **S2M**

Contractor: _____

Dates Test Represents: 10/13/2020 through 10/19/2020

MDOT No.: _____

Agg. Class	Pit #	Source	Weight (SSD)	ft ³	Specific Gravity	% Contribution
6AA	71-47	Presque Isle	1700	10.40	2.62	55.7
26A	71-47	Presque Isle	120	0.73	2.62	3.9
2NS	63-115	Ray Rd	1230	7.44	2.65	40.3
Total Wt			3050	18.57		100.0

<----- Verify this number is 100%




Superior Materials, LLC
 30701 W. 10 Mile Rd.
 Suite 500
 Farmington Hills, MI 48336

Sieve	6AA	26A	2NS	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	100.0	100.0	100.0	0.0	0.0
1.5"	100.0	100.0	100.0	100.0	0.0	0.0
1"	97.9	100.0	100.0	98.8	1.2	1.2
3/4"	85.2	100.0	100.0	91.8	7.1	8.2
1/2"	51.9	98.6	100.0	73.1	18.6	26.9
3/8"	30.5	88.7	100.0	60.8	12.3	39.2
#4	5.2	18.7	97.7	43.0	17.8	57.0
#8	2.3	5.1	79.2	33.4	9.6	66.6
#16	1.8	2.5	61.7	26.0	7.4	74.0
#30	1.7	2.1	45.3	19.3	6.7	80.7
#50	1.6	1.9	20.0	9.0	10.3	91.0
#100	1.5	1.7	3.5	2.3	6.7	97.7
LBW	1.2	1.4	0.7	1.0	1.3	99.0

*Maximum % Retained must be above the 3/8" sieve.
 *Any two adjacent sieves must equal 10% except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 4% for each sieve except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 8% for the 1" sieve when a 2" max. size (nom. Max. 1.5") aggregate is used.

Production Gradation Batch Plant Gradations Aggregate Supplier Gradations

Coarseness Factor:	59	Workability Factor:	33
---------------------------	-----------	----------------------------	-----------

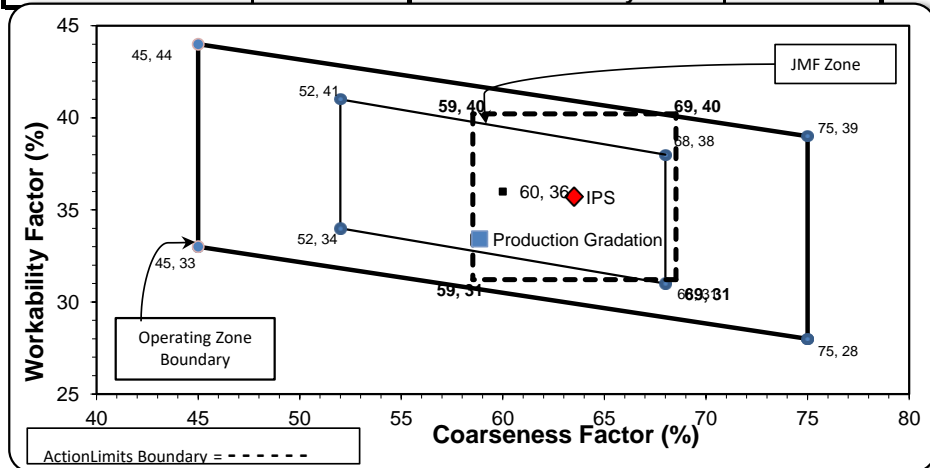

Initial Production Sample (IPS)

Coarseness Factor:	64		
Workability Factor:	36		
Sieve	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	0.0	0.0
1.5"	100.0	0.0	0.0
1"	99.2	0.8	0.8
3/4"	90.9	8.3	9.1
1/2"	71.3	19.6	28.7
3/8"	59.2	12.1	40.8
#4	41.5	17.7	58.5
#8	35.7	5.8	64.3
#16	27.9	7.9	72.1
#30	18.3	9.5	81.7
#50	7.3	11.0	92.7
#100	2.0	5.3	98.0
LBW	0.9	1.1	99.1

PREPARED BY:
 SM, LLC Technical Service

Approved By:

Aggregate Optimization Chart

PLANT #: **P-32**

Sample Date: 10/12/20

Concrete Grade: **S2M**

Contractor: _____

Dates Test Represents: 10/13/2020 through 10/19/2020

MDOT No.: _____

Agg. Class	Pit #	Source	Weight (SSD)	ft ³	Specific Gravity	% Contribution
6AA	71-47	Presque Isle	1520	9.30	2.62	49.8
26A	71-47	Presque Isle	300	1.83	2.62	9.8
2NS	95-013	Smelter Bay	1230	7.44	2.65	40.3
Total Wt			3050	18.57		100.0

<----- Verify this number is 100%




Superior Materials, LLC
 30701 W. 10 Mile Rd.
 Suite 500
 Farmington Hills, MI 48336

Sieve	6AA	26A	2NS	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	100.0	100.0	100.0	0.0	0.0
1.5"	100.0	100.0	100.0	100.0	0.0	0.0
1"	96.8	100.0	100.0	98.4	1.6	1.6
3/4"	75.0	100.0	100.0	87.5	10.9	12.5
1/2"	37.3	98.6	100.0	68.6	18.9	31.4
3/8"	21.2	88.7	100.0	59.6	9.0	40.4
#4	4.3	18.7	95.0	42.3	17.3	57.7
#8	2.5	5.1	82.0	34.8	7.5	65.2
#16	2.2	2.5	64.5	27.4	7.5	72.6
#30	2.1	2.1	44.6	19.2	8.1	80.8
#50	2.0	1.9	20.2	9.3	9.9	90.7
#100	1.8	1.7	9.4	4.9	4.5	95.1
LBW	1.5	1.4	1.4	1.4	3.4	98.6

*Maximum % Retained must be above the 3/8" sieve.
 *Any two adjacent sieves must equal 10% except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 4% for each sieve except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 8% for the 1" sieve when a 2" max. size (nom. Max. 1.5") aggregate is used.

Production Gradation Batch Plant Gradations Aggregate Supplier Gradations

Coarseness Factor:	62	Workability Factor:	35
---------------------------	-----------	----------------------------	-----------

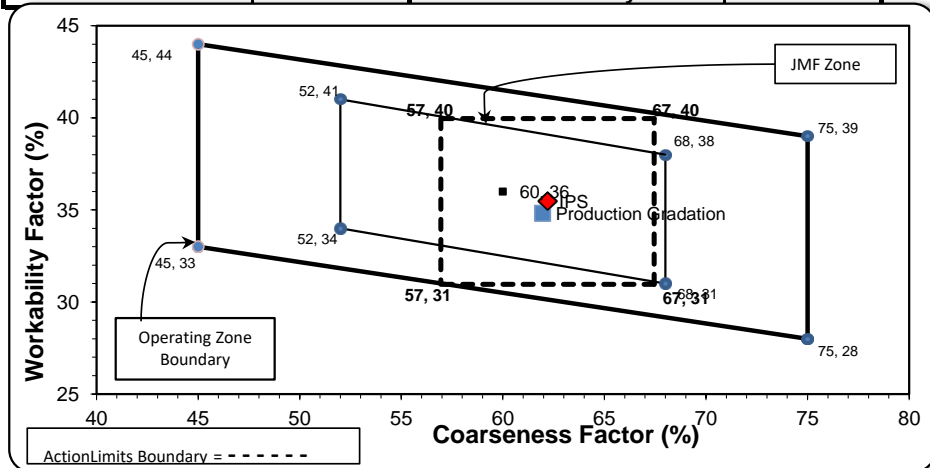

Initial Production Sample (IPS)

Coarseness Factor:	62		
Workability Factor:	35		
Sieve	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	0.0	0.0
1.5"	100.0	0.0	0.0
1"	100.0	0.0	0.0
3/4"	94.0	6.0	6.0
1/2"	70.2	23.7	29.8
3/8"	59.9	10.4	40.1
#4	42.7	17.2	57.3
#8	35.5	7.2	64.5
#16	28.4	7.0	71.6
#30	19.2	9.2	80.8
#50	8.9	10.3	91.1
#100	3.1	5.9	96.9
LBW	1.4	1.7	98.6

PREPARED BY:
 SM, LLC Technical Service

Approved By:

Aggregate Optimization Chart

PLANT #: **P-36**

Sample Date: 10/12/20

Concrete Grade: **S2M**

Contractor: _____

Dates Test Represents: 10/13/2020 through 10/19/2020

MDOT No.: _____

Agg. Class	Pit #	Source	Weight (SSD)	ft ³	Specific Gravity	% Contribution
6AA	71-47	Presque Isle	1700	10.40	2.62	55.7
26A	71-47	Presque Isle	150	0.92	2.62	4.9
2NS	63-92	Grange Hall	1200	7.26	2.65	39.3
Total Wt			3050	18.57		100.0

<----- Verify this number is 100%




Superior Materials, LLC
 30701 W. 10 Mile Rd.
 Suite 500
 Farmington Hills, MI 48336

Sieve	6AA	26A	2NS	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	100.0	100.0	100.0	0.0	0.0
1.5"	100.0	100.0	100.0	100.0	0.0	0.0
1"	97.9	100.0	100.0	98.8	1.2	1.2
3/4"	85.2	100.0	100.0	91.8	7.1	8.2
1/2"	51.9	98.6	100.0	73.1	18.6	26.9
3/8"	30.5	88.7	100.0	60.7	12.4	39.3
#4	5.2	18.7	97.5	42.2	18.5	57.8
#8	2.3	5.1	85.6	35.2	7.0	64.8
#16	1.8	2.5	70.8	29.0	6.2	71.0
#30	1.7	2.1	48.6	20.2	8.8	79.8
#50	1.6	1.9	17.4	7.8	12.3	92.2
#100	1.5	1.7	2.1	1.7	6.1	98.3
LBW	1.2	1.4	0.4	0.9	0.9	99.1

*Maximum % Retained must be above the 3/8" sieve.
 *Any two adjacent sieves must equal 10% except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 4% for each sieve except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 8% for the 1" sieve when a 2" max. size (nom. Max. 1.5") aggregate is used.

Production Gradation Batch Plant Gradations Aggregate Supplier Gradations

Coarseness Factor:	61	Workability Factor:	35
---------------------------	-----------	----------------------------	-----------

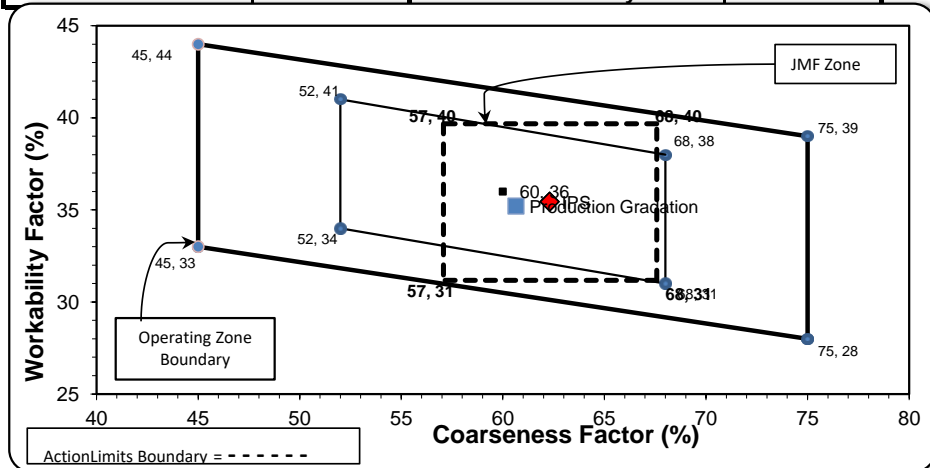

Initial Production Sample (IPS)

Coarseness Factor:	62
Workability Factor:	35

Sieve	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	0.0	0.0
1.5"	100.0	0.0	0.0
1"	99.1	0.9	0.9
3/4"	90.5	8.6	9.5
1/2"	69.8	20.7	30.2
3/8"	59.8	10.0	40.2
#4	42.2	17.6	57.8
#8	35.4	6.7	64.6
#16	28.8	6.7	71.2
#30	21.4	7.4	78.6
#50	8.8	12.6	91.2
#100	1.8	7.0	98.2
LBW	0.7	1.0	99.3

PREPARED BY:
 SM, LLC Technical Service

Approved By:

Aggregate Optimization Chart

PLANT #: **P-39**

Sample Date: 10/12/20

Concrete Grade: **S2M**

Contractor: _____

Dates Test Represents: 10/13/2020 through 10/19/2020

MDOT No.: _____

Agg. Class	Pit #	Source	Weight (SSD)	ft ³	Specific Gravity	% Contribution
6AA	71-47	Presque Isle	1650	10.09	2.62	54.1
26A	71-47	Presque Isle	150	0.92	2.62	4.9
2NS	44-051	Krake Willis Rd	1250	7.56	2.65	41.0
Total Wt			3050	18.57		100.0

<----- Verify this number is 100%




Superior Materials, LLC
 30701 W. 10 Mile Rd.
 Suite 500
 Farmington Hills, MI 48336

Sieve	6AA	26A	2NS	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	100.0	100.0	100.0	0.0	0.0
1.5"	100.0	100.0	100.0	100.0	0.0	0.0
1"	99.5	100.0	100.0	99.7	0.3	0.3
3/4"	88.6	100.0	100.0	93.8	5.9	6.2
1/2"	50.7	97.9	100.0	73.2	20.6	26.8
3/8"	28.4	88.4	100.0	60.7	12.5	39.3
#4	3.7	23.9	95.8	42.4	18.3	57.6
#8	1.9	6.8	80.7	34.4	8.0	65.6
#16	1.7	3.0	64.9	27.7	6.8	72.3
#30	1.6	2.2	50.0	21.5	6.2	78.5
#50	1.5	2.0	24.9	11.1	10.4	88.9
#100	1.5	1.9	6.7	3.7	7.5	96.3
LBW	1.4	1.7	0.8	1.2	2.5	98.8

*Maximum % Retained must be above the 3/8" sieve.
 *Any two adjacent sieves must equal 10% except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 4% for each sieve except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 8% for the 1" sieve when a 2" max. size (nom. Max. 1.5") aggregate is used.

Production Gradation Batch Plant Gradations Aggregate Supplier Gradations

Coarseness Factor:	60	Workability Factor:	34
---------------------------	-----------	----------------------------	-----------

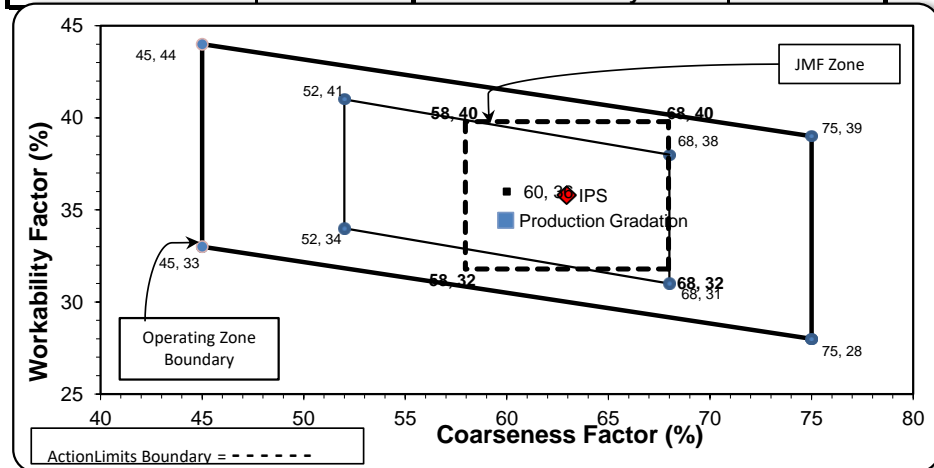

Initial Production Sample (IPS)

Coarseness Factor:	63
Workability Factor:	36

Sieve	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	0.0	0.0
1.5"	100.0	0.0	0.0
1"	100.0	0.0	0.0
3/4"	89.8	10.2	10.2
1/2"	70.7	19.1	29.3
3/8"	59.6	11.1	40.4
#4	43.2	16.4	56.8
#8	35.8	7.4	64.2
#16	29.2	6.6	70.8
#30	21.4	7.8	78.6
#50	9.8	11.6	90.2
#100	3.7	6.1	96.3
LBW	1.2	2.5	98.8

PREPARED BY:
 SM, LLC Technical Service

Approved By:

Aggregate Optimization Chart

PLANT #: **P-02**

Sample Date: 10/12/20

Concrete Grade: **S2M**

Contractor: _____

Dates Test Represents: 10/13/2020 through 10/19/2020

MDOT No.: _____

Agg. Class	Pit #	Source	Weight (SSD)	ft ³	Specific Gravity	% Contribution
6AA	71-47	Presque Isle	1650	10.09	2.62	54.1
26A	71-47	Presque Isle	100	0.61	2.62	3.3
2NS	63-115	Ray Rd	1300	7.86	2.65	42.6
Total Wt			3050	18.57		100.0

<----- Verify this number is 100%




Superior Materials, LLC
 30701 W. 10 Mile Rd.
 Suite 500
 Farmington Hills, MI 48336

Sieve	6AA	26A	2NS	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	100.0	100.0	100.0	0.0	0.0
1.5"	100.0	100.0	100.0	100.0	0.0	0.0
1"	97.9	100.0	100.0	98.9	1.1	1.1
3/4"	85.2	100.0	100.0	92.0	6.9	8.0
1/2"	51.9	98.6	100.0	73.9	18.1	26.1
3/8"	30.5	88.7	100.0	62.0	11.9	38.0
#4	5.2	18.7	97.7	45.1	17.0	54.9
#8	2.3	5.1	79.2	35.2	9.9	64.8
#16	1.8	2.5	61.7	27.4	7.8	72.6
#30	1.7	2.1	45.3	20.3	7.1	79.7
#50	1.6	1.9	20.0	9.5	10.8	90.5
#100	1.5	1.7	3.5	2.4	7.1	97.6
LBW	1.2	1.4	0.7	1.0	1.4	99.0

*Maximum % Retained must be above the 3/8" sieve.
 *Any two adjacent sieves must equal 10% except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 4% for each sieve except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 8% for the 1" sieve when a 2" max. size (nom. Max. 1.5") aggregate is used.

Production Gradation Batch Plant Gradations Aggregate Supplier Gradations

Coarseness Factor:	59	Workability Factor:	35
---------------------------	-----------	----------------------------	-----------

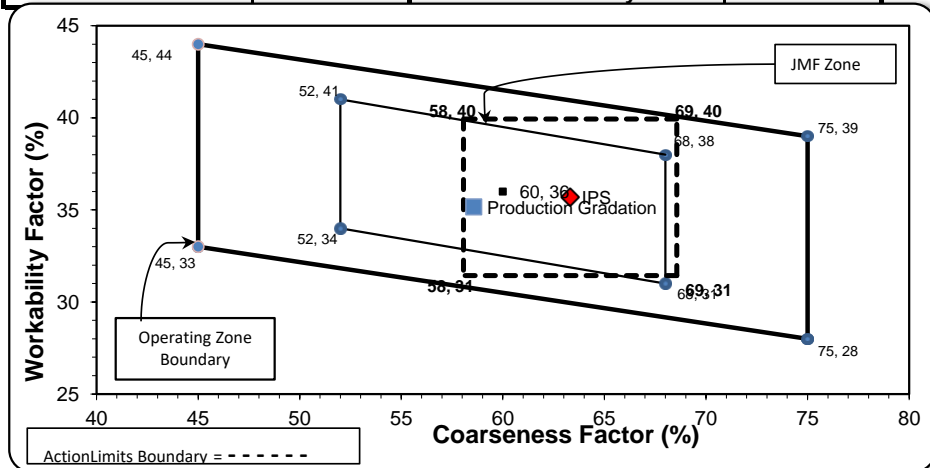

Initial Production Sample (IPS)

Coarseness Factor:	63		
Workability Factor:	36		
Sieve	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	0.0	0.0
1.5"	100.0	0.0	0.0
1"	100.0	0.0	0.0
3/4"	95.6	4.4	4.4
1/2"	73.1	22.6	26.9
3/8"	59.3	13.8	40.7
#4	42.8	16.5	57.2
#8	35.7	7.1	64.3
#16	28.9	6.8	71.1
#30	20.7	8.2	79.3
#50	9.9	10.8	90.1
#100	2.1	7.8	97.9
LBW	0.9	1.2	99.1

PREPARED BY:
 SM, LLC Technical Service

Approved By:
