

Aggregate Optimization Chart

PLANT #: **P-101**

Sample Date: 10/5/20

Concrete Grade: **S2M**

Contractor: _____

Dates Test Represents: 10/6/2020 through 10/12/2020

MDOT No.: _____

Agg. Class	Pit #	Source	Weight (SSD)	ft ³	Specific Gravity	% Contribution
6AA	71-47	Presque Isle	1675	10.25	2.62	54.8
26A	71-47	Presque Isle	150	0.92	2.62	4.9
2NS	75-051	Mid-Michigan	1230	7.41	2.66	40.3
Total Wt			3055	18.57		100.0

<---- Verify this number is 100%



Superior Materials, LLC
 30701 W. 10 Mile Rd.
 Suite 500
 Farmington Hills, MI 48336

Sieve	6AA	26A	2NS	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	100.0	100.0	100.0	0.0	0.0
1.5"	100.0	100.0	100.0	100.0	0.0	0.0
1"	97.1	100.0	100.0	98.4	1.6	1.6
3/4"	84.7	100.0	100.0	91.6	6.8	8.4
1/2"	37.6	98.2	100.0	65.7	25.9	34.3
3/8"	19.3	88.6	100.0	55.2	10.5	44.8
#4	2.0	19.3	98.1	41.5	13.7	58.5
#8	1.1	4.9	81.4	33.6	7.9	66.4
#16	1.0	2.4	64.9	26.8	6.8	73.2
#30	0.9	2.0	49.0	20.3	6.5	79.7
#50	0.9	1.9	25.1	10.7	9.6	89.3
#100	0.9	1.8	5.3	2.7	8.0	97.3
LBW	0.8	1.6	0.6	0.8	2.0	99.2


*Maximum % Retained must be above the 3/8" sieve.
 *Any two adjacent sieves must equal 10% except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 4% for each sieve except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 8% for the 1" sieve when a 2" max. size (nom. Max. 1.5") aggregate is used.

Production Gradation Batch Plant Gradations Aggregate Supplier Gradations

Coarseness Factor:	67	Workability Factor:	34
---------------------------	-----------	----------------------------	-----------

Initial Production Sample (IPS)

Coarseness Factor:	64
Workability Factor:	35

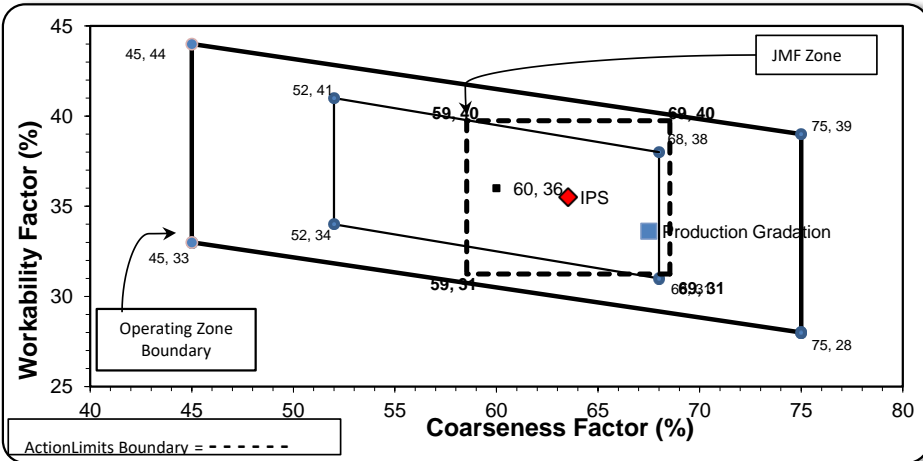

Sieve	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	0.0	0.0
1.5"	100.0	0.0	0.0
1"	100.0	0.0	0.0
3/4"	93.9	6.1	6.1
1/2"	71.4	22.5	28.6
3/8"	59.0	12.4	41.0
#4	45.1	13.9	54.9
#8	35.5	9.6	64.5
#16	28.3	7.2	71.7
#30	21.3	6.9	78.7
#50	11.0	10.3	89.0
#100	3.4	7.6	96.6
LBW	1.1	2.3	98.9

PREPARED BY:
 SM, LLC Technical Service

Approved By:

Aggregate Optimization Chart

PLANT #: **P-102**

Sample Date: 10/5/20

Concrete Grade: **S2M**

Contractor: _____

Dates Test Represents: 10/6/2020 through 10/12/2020

MDOT No.: _____

Agg. Class	Pit #	Source	Weight (SSD)	ft ³	Specific Gravity	% Contribution
6AA	58-003	Stoneco	1550	9.23	2.69	50.0
26A	58-003	Stoneco	340	2.03	2.69	11.0
2NS	63-114	Highland	1210	7.32	2.65	39.0
Total Wt			3100	18.58		100.0

<----- Verify this number is 100%




Superior Materials, LLC
 30701 W. 10 Mile Rd.
 Suite 500
 Farmington Hills, MI 48336

Sieve	6AA	26A	2NS	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	100.0	100.0	100.0	0.0	0.0
1.5"	100.0	100.0	100.0	100.0	0.0	0.0
1"	100.0	100.0	100.0	100.0	0.0	0.0
3/4"	78.5	100.0	100.0	89.3	10.8	10.8
1/2"	37.1	99.7	100.0	68.5	20.7	31.5
3/8"	16.5	82.2	100.0	56.3	12.2	43.7
#4	2.8	24.1	99.2	42.8	13.5	57.2
#8	1.6	7.1	85.9	35.1	7.7	64.9
#16	1.3	3.2	69.6	28.2	6.9	71.8
#30	1.2	2.5	48.8	19.9	8.2	80.1
#50	1.1	2.2	17.6	7.7	12.3	92.3
#100	1.0	2.1	4.2	2.4	5.3	97.6
LBW	0.6	1.8	0.3	0.6	1.8	99.4

*Maximum % Retained must be above the 3/8" sieve.
 *Any two adjacent sieves must equal 10% except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 4% for each sieve except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 8% for the 1" sieve when a 2" max. size (nom. Max. 1.5") aggregate is used.

Production Gradation Batch Plant Gradations Aggregate Supplier Gradations

Coarseness Factor: **67** **Workability Factor:** **35**

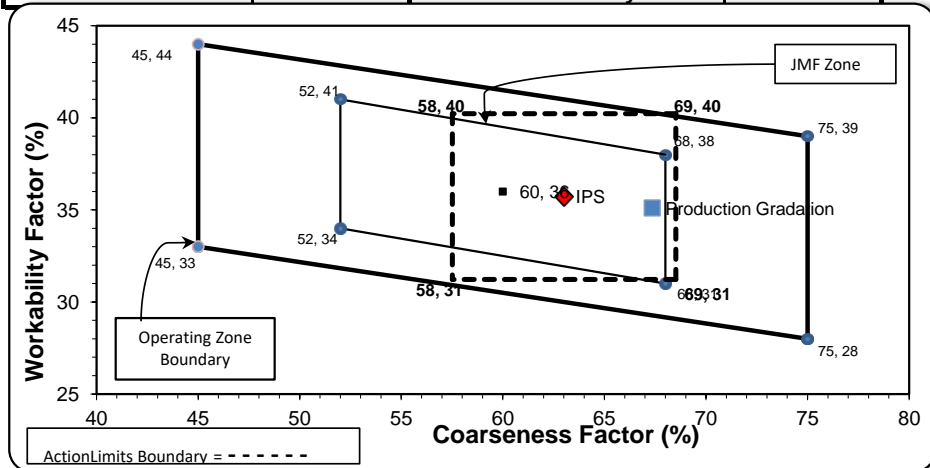

Initial Production Sample (IPS)

Coarseness Factor: **63**
Workability Factor: **36**

Sieve	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	0.0	0.0
1.5"	100.0	0.0	0.0
1"	99.2	0.8	0.8
3/4"	90.9	8.3	9.1
1/2"	71.3	19.6	28.7
3/8"	59.5	11.8	40.5
#4	43.8	15.7	56.2
#8	35.7	8.1	64.3
#16	27.0	8.7	73.0
#30	18.6	8.4	81.4
#50	6.8	11.8	93.2
#100	1.4	5.4	98.6
LBW	0.6	0.8	99.4

PREPARED BY:
 SM, LLC Technical Service

Approved By:

Aggregate Optimization Chart

PLANT #: **P-103**

Sample Date: 10/5/20

Concrete Grade: **S2M**

Contractor: _____

Dates Test Represents: 10/6/2020 through 10/12/2020

MDOT No.: _____

Agg. Class	Pit #	Source	Weight (SSD)	ft ³	Specific Gravity	% Contribution
6AA	58-003	Stoneco	1550	9.23	2.69	50.0
26A	58-003	Stoneco	340	2.03	2.69	11.0
2NS	63-114	Highland	1210	7.32	2.65	39.0
Total Wt			3100	18.58		100.0

<----- Verify this number is 100%




Superior Materials, LLC
 30701 W. 10 Mile Rd.
 Suite 500
 Farmington Hills, MI 48336

Sieve	6AA	26A	2NS	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	100.0	100.0	100.0	0.0	0.0
1.5"	100.0	100.0	100.0	100.0	0.0	0.0
1"	100.0	100.0	100.0	100.0	0.0	0.0
3/4"	78.5	100.0	100.0	89.3	10.8	10.8
1/2"	37.1	99.7	100.0	68.5	20.7	31.5
3/8"	16.5	82.2	100.0	56.3	12.2	43.7
#4	2.8	24.1	99.2	42.8	13.5	57.2
#8	1.6	7.1	85.9	35.1	7.7	64.9
#16	1.3	3.2	69.6	28.2	6.9	71.8
#30	1.2	2.5	48.8	19.9	8.2	80.1
#50	1.1	2.2	17.6	7.7	12.3	92.3
#100	1.0	2.1	4.2	2.4	5.3	97.6
LBW	0.6	1.8	0.3	0.6	1.8	99.4

*Maximum % Retained must be above the 3/8" sieve.
 *Any two adjacent sieves must equal 10% except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 4% for each sieve except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 8% for the 1" sieve when a 2" max. size (nom. Max. 1.5") aggregate is used.

Production Gradation Batch Plant Gradations Aggregate Supplier Gradations

Coarseness Factor:	67	Workability Factor:	35
---------------------------	-----------	----------------------------	-----------

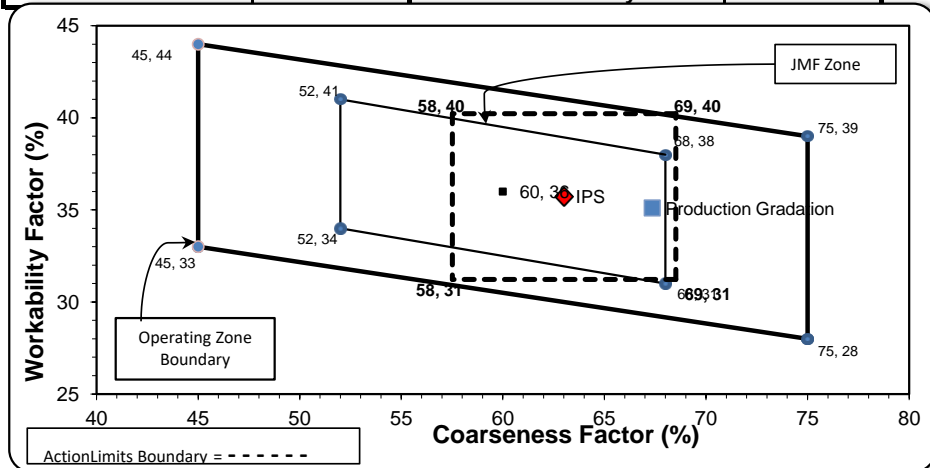

Initial Production Sample (IPS)

Coarseness Factor:	63		
Workability Factor:	36		
Sieve	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	0.0	0.0
1.5"	100.0	0.0	0.0
1"	99.2	0.8	0.8
3/4"	90.9	8.3	9.1
1/2"	71.3	19.6	28.7
3/8"	59.5	11.8	40.5
#4	43.8	15.7	56.2
#8	35.7	8.1	64.3
#16	27.0	8.7	73.0
#30	18.6	8.4	81.4
#50	6.8	11.8	93.2
#100	1.4	5.4	98.6
LBW	0.6	0.8	99.4

PREPARED BY:
 SM, LLC Technical Service

Approved BY:

Aggregate Optimization Chart

PLANT #: **P-12**

Sample Date: 10/5/20

Concrete Grade: **S2M**

Contractor: _____

Dates Test Represents: 10/6/2020 through 10/12/2020

MDOT No.: _____

Agg. Class	Pit #	Source	Weight (SSD)	ft ³	Specific Gravity	% Contribution
6AA	71-47	Presque Isle	1600	9.79	2.62	52.5
26A	71-47	Presque Isle	220	1.35	2.62	7.2
2NS	63-115	Ray Rd	1230	7.44	2.65	40.3
Total Wt			3050	18.57		100.0

<----- Verify this number is 100%




Superior Materials, LLC
 30701 W. 10 Mile Rd.
 Suite 500
 Farmington Hills, MI 48336

Sieve	6AA	26A	2NS	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	100.0	100.0	100.0	0.0	0.0
1.5"	100.0	100.0	100.0	100.0	0.0	0.0
1"	97.8	100.0	100.0	98.8	1.2	1.2
3/4"	75.1	100.0	100.0	86.9	11.9	13.1
1/2"	39.8	96.9	100.0	68.2	18.7	31.8
3/8"	23.1	76.1	100.0	57.9	10.3	42.1
#4	5.2	15.5	97.8	43.3	14.6	56.7
#8	3.0	5.9	78.9	33.8	9.5	66.2
#16	2.6	3.9	61.2	26.3	7.5	73.7
#30	2.4	3.4	44.9	19.6	6.7	80.4
#50	2.3	3.2	19.8	9.4	10.2	90.6
#100	2.2	3.0	3.1	2.6	6.8	97.4
LBW	1.6	2.5	0.3	1.1	1.5	98.9

*Maximum % Retained must be above the 3/8" sieve.
 *Any two adjacent sieves must equal 10% except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 4% for each sieve except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 8% for the 1" sieve when a 2" max. size (nom. Max. 1.5") aggregate is used.

Production Gradation Batch Plant Gradations Aggregate Supplier Gradations

Coarseness Factor:	64	Workability Factor:	34
---------------------------	-----------	----------------------------	-----------

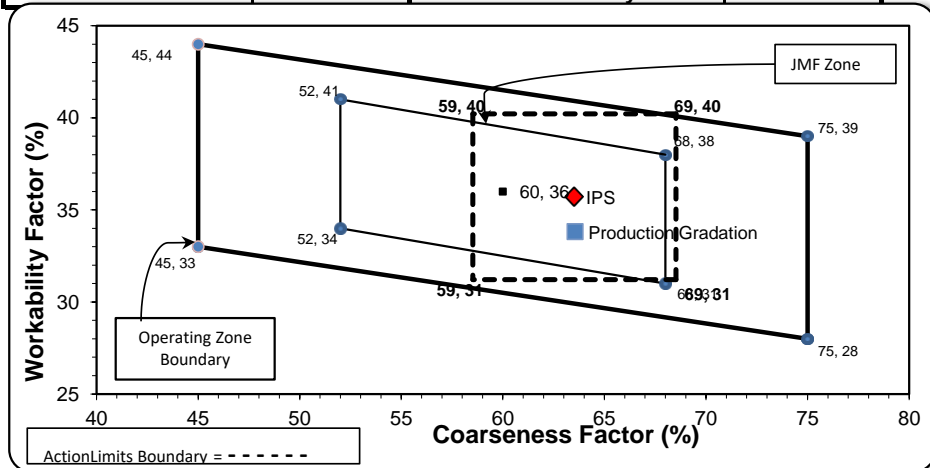

Initial Production Sample (IPS)

Sieve	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	0.0	0.0
1.5"	100.0	0.0	0.0
1"	99.2	0.8	0.8
3/4"	90.9	8.3	9.1
1/2"	71.3	19.6	28.7
3/8"	59.2	12.1	40.8
#4	41.5	17.7	58.5
#8	35.7	5.8	64.3
#16	27.9	7.9	72.1
#30	18.3	9.5	81.7
#50	7.3	11.0	92.7
#100	2.0	5.3	98.0
LBW	0.9	1.1	99.1

PREPARED BY:
 SM, LLC Technical Service

Approved By:

Aggregate Optimization Chart

PLANT #: **P-32**

Sample Date: 10/5/20

Concrete Grade: **S2M**

Contractor: _____

Dates Test Represents: 10/6/2020 through 10/12/2020

MDOT No.: _____

Agg. Class	Pit #	Source	Weight (SSD)	ft ³	Specific Gravity	% Contribution
6AA	71-47	Presque Isle	1520	9.30	2.62	49.8
26A	71-47	Presque Isle	300	1.83	2.62	9.8
2NS	95-013	Smelter Bay	1230	7.44	2.65	40.3
Total Wt			3050	18.57		100.0

<----- Verify this number is 100%




Superior Materials, LLC
 30701 W. 10 Mile Rd.
 Suite 500
 Farmington Hills, MI 48336

Sieve	6AA	26A	2NS	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	100.0	100.0	100.0	0.0	0.0
1.5"	100.0	100.0	100.0	100.0	0.0	0.0
1"	96.7	100.0	100.0	98.4	1.6	1.6
3/4"	77.4	100.0	100.0	88.7	9.6	11.3
1/2"	38.1	96.9	100.0	68.8	19.9	31.2
3/8"	19.4	76.1	100.0	57.5	11.4	42.5
#4	3.3	15.5	96.7	42.2	15.3	57.8
#8	2.5	5.9	83.5	35.5	6.7	64.5
#16	2.2	3.9	67.4	28.7	6.8	71.3
#30	2.1	3.4	47.1	20.4	8.3	79.6
#50	2.0	3.2	22.6	10.4	9.9	89.6
#100	1.9	3.0	6.2	3.7	6.7	96.3
LBW	1.3	2.5	1.0	1.3	2.4	98.7

*Maximum % Retained must be above the 3/8" sieve.
 *Any two adjacent sieves must equal 10% except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 4% for each sieve except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 8% for the 1" sieve when a 2" max. size (nom. Max. 1.5") aggregate is used.

Production Gradation Batch Plant Gradations Aggregate Supplier Gradations

Coarseness Factor:	66	Workability Factor:	36
---------------------------	-----------	----------------------------	-----------

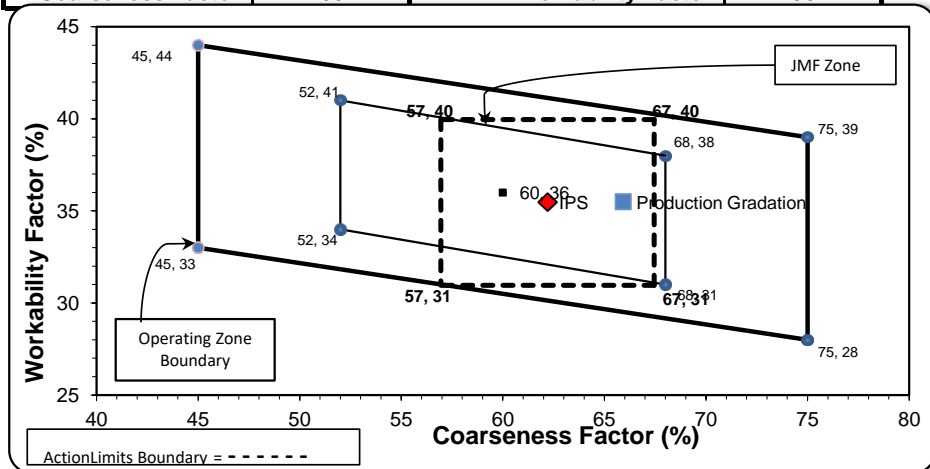

Initial Production Sample (IPS)

Coarseness Factor:	62		
Workability Factor:	35		
Sieve	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	0.0	0.0
1.5"	100.0	0.0	0.0
1"	100.0	0.0	0.0
3/4"	94.0	6.0	6.0
1/2"	70.2	23.7	29.8
3/8"	59.9	10.4	40.1
#4	42.7	17.2	57.3
#8	35.5	7.2	64.5
#16	28.4	7.0	71.6
#30	19.2	9.2	80.8
#50	8.9	10.3	91.1
#100	3.1	5.9	96.9
LBW	1.4	1.7	98.6

PREPARED BY:
 SM, LLC Technical Service

Approved By:

Aggregate Optimization Chart

PLANT #: **P-36**

Sample Date: 10/5/20

Concrete Grade: **S2M**

Contractor: _____

Dates Test Represents: 10/6/2020 through 10/12/2020

MDOT No.: _____

Agg. Class	Pit #	Source	Weight (SSD)	ft ³	Specific Gravity	% Contribution
6AA	71-47	Presque Isle	1500	9.17	2.62	49.2
26A	71-47	Presque Isle	350	2.14	2.62	11.5
2NS	63-92	Grange Hall	1200	7.26	2.65	39.3
Total Wt			3050	18.57		100.0

<----- Verify this number is 100%




Superior Materials, LLC
 30701 W. 10 Mile Rd.
 Suite 500
 Farmington Hills, MI 48336

Sieve	6AA	26A	2NS	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	100.0	100.0	100.0	0.0	0.0
1.5"	100.0	100.0	100.0	100.0	0.0	0.0
1"	97.8	100.0	100.0	98.9	1.1	1.1
3/4"	75.1	100.0	100.0	87.8	11.2	12.2
1/2"	39.8	96.9	100.0	70.0	17.7	30.0
3/8"	23.1	76.1	100.0	59.4	10.6	40.6
#4	5.2	15.5	98.0	42.9	16.5	57.1
#8	3.0	5.9	86.5	36.2	6.7	63.8
#16	2.6	3.9	71.5	29.9	6.3	70.1
#30	2.4	3.4	48.7	20.7	9.1	79.3
#50	2.3	3.2	17.5	8.4	12.3	91.6
#100	2.2	3.0	2.1	2.3	6.1	97.7
LBW	1.6	2.5	0.5	1.3	1.0	98.7

*Maximum % Retained must be above the 3/8" sieve.
 *Any two adjacent sieves must equal 10% except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 4% for each sieve except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 8% for the 1" sieve when a 2" max. size (nom. Max. 1.5") aggregate is used.

Production Gradation Batch Plant Gradations Aggregate Supplier Gradations

Coarseness Factor:	64	Workability Factor:	36
---------------------------	-----------	----------------------------	-----------

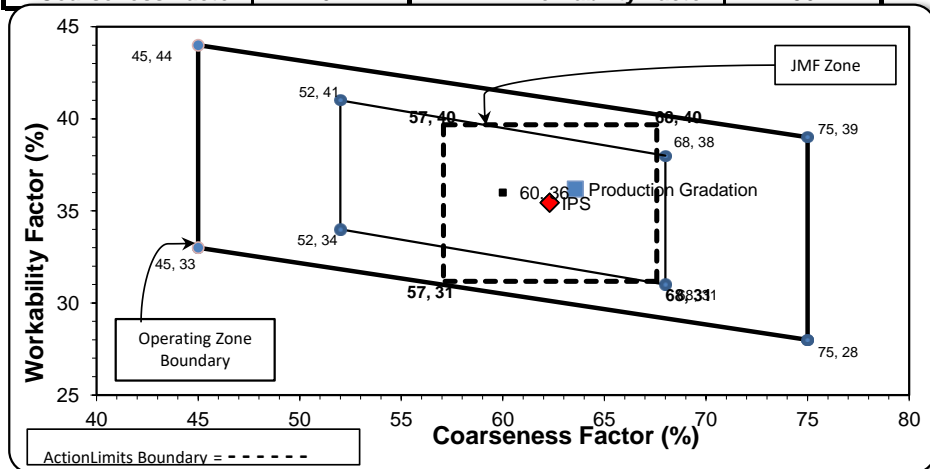

Initial Production Sample (IPS)

Coarseness Factor:	62		
Workability Factor:	35		
Sieve	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	0.0	0.0
1.5"	100.0	0.0	0.0
1"	99.1	0.9	0.9
3/4"	90.5	8.6	9.5
1/2"	69.8	20.7	30.2
3/8"	59.8	10.0	40.2
#4	42.2	17.6	57.8
#8	35.4	6.7	64.6
#16	28.8	6.7	71.2
#30	21.4	7.4	78.6
#50	8.8	12.6	91.2
#100	1.8	7.0	98.2
LBW	0.7	1.0	99.3

PREPARED BY:
 SM, LLC Technical Service

Approved By:

Aggregate Optimization Chart

PLANT #: **P-39**

Sample Date: 10/5/20

Concrete Grade: **S2M**

Contractor: _____

Dates Test Represents: 10/6/2020 through 10/12/2020

MDOT No.: _____

Agg. Class	Pit #	Source	Weight (SSD)	ft ³	Specific Gravity	% Contribution
6AA	71-47	Presque Isle	1650	10.09	2.62	54.1
26A	71-47	Presque Isle	150	0.92	2.62	4.9
2NS	44-051	Krake Willis Rd	1250	7.56	2.65	41.0
Total Wt			3050	18.57		100.0

<----- Verify this number is 100%




Superior Materials, LLC
 30701 W. 10 Mile Rd.
 Suite 500
 Farmington Hills, MI 48336

Sieve	6AA	26A	2NS	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	100.0	100.0	100.0	0.0	0.0
1.5"	100.0	100.0	100.0	100.0	0.0	0.0
1"	97.1	100.0	100.0	98.4	1.6	1.6
3/4"	84.7	100.0	100.0	91.7	6.7	8.3
1/2"	37.6	98.2	100.0	66.2	25.6	33.8
3/8"	19.3	88.6	100.0	55.8	10.4	44.2
#4	2.0	19.3	95.6	41.2	14.6	58.8
#8	1.1	4.9	80.6	33.9	7.3	66.1
#16	1.0	2.4	64.8	27.2	6.7	72.8
#30	0.9	2.0	50.2	21.2	6.1	78.8
#50	0.9	1.9	26.3	11.4	9.8	88.6
#100	0.9	1.8	7.8	3.8	7.6	96.2
LBW	0.8	1.6	0.9	0.9	2.9	99.1

*Maximum % Retained must be above the 3/8" sieve.
 *Any two adjacent sieves must equal 10% except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 4% for each sieve except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 8% for the 1" sieve when a 2" max. size (nom. Max. 1.5") aggregate is used.

Production Gradation Batch Plant Gradations Aggregate Supplier Gradations

Coarseness Factor: **67** **Workability Factor:** **34**

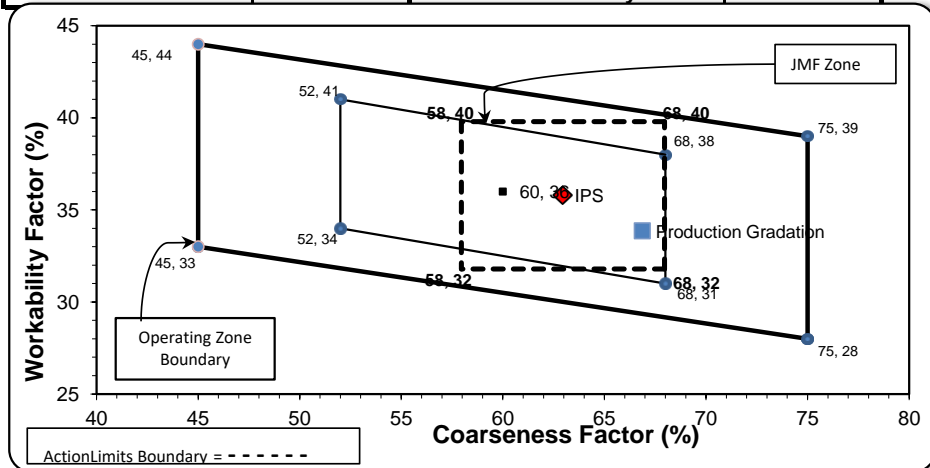

Intial Production Sample (IPS)

Coarseness Factor: **63**
Workability Factor: **36**

Sieve	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	0.0	0.0
1.5"	100.0	0.0	0.0
1"	100.0	0.0	0.0
3/4"	89.8	10.2	10.2
1/2"	70.7	19.1	29.3
3/8"	59.6	11.1	40.4
#4	43.2	16.4	56.8
#8	35.8	7.4	64.2
#16	29.2	6.6	70.8
#30	21.4	7.8	78.6
#50	9.8	11.6	90.2
#100	3.7	6.1	96.3
LBW	1.2	2.5	98.8

PREPARED BY:
 SM, LLC Technical Service

Approved By:

Aggregate Optimization Chart

PLANT #: **P-02**

Sample Date: 10/5/20

Concrete Grade: **S2M**

Contractor: _____

Dates Test Represents: 10/6/2020 through 10/12/2020

MDOT No.: _____

Agg. Class	Pit #	Source	Weight (SSD)	ft ³	Specific Gravity	% Contribution
6AA	71-47	Presque Isle	1550	9.48	2.62	50.8
26A	71-47	Presque Isle	200	1.22	2.62	6.6
2NS	63-115	Ray Rd	1300	7.86	2.65	42.6
Total Wt			3050	18.57		100.0

<----- Verify this number is 100%




Superior Materials, LLC
 30701 W. 10 Mile Rd.
 Suite 500
 Farmington Hills, MI 48336

Sieve	6AA	26A	2NS	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	100.0	100.0	100.0	0.0	0.0
1.5"	100.0	100.0	100.0	100.0	0.0	0.0
1"	97.8	100.0	100.0	98.9	1.1	1.1
3/4"	75.1	100.0	100.0	87.3	11.5	12.7
1/2"	39.8	96.9	100.0	69.2	18.1	30.8
3/8"	23.1	76.1	100.0	59.4	9.9	40.6
#4	5.2	15.5	97.8	45.3	14.0	54.7
#8	3.0	5.9	78.9	35.5	9.8	64.5
#16	2.6	3.9	61.2	27.7	7.9	72.3
#30	2.4	3.4	44.9	20.6	7.1	79.4
#50	2.3	3.2	19.8	9.8	10.8	90.2
#100	2.2	3.0	3.1	2.6	7.2	97.4
LBW	1.6	2.5	0.3	1.1	1.5	98.9

*Maximum % Retained must be above the 3/8" sieve.
 *Any two adjacent sieves must equal 10% except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 4% for each sieve except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 8% for the 1" sieve when a 2" max. size (nom. Max. 1.5") aggregate is used.

Production Gradation Batch Plant Gradations Aggregate Supplier Gradations

Coarseness Factor: **63** **Workability Factor:** **36**

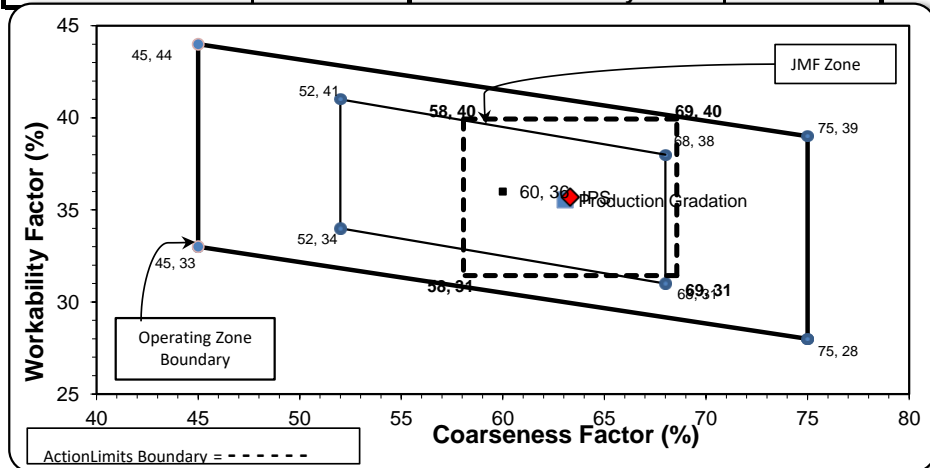

Initial Production Sample (IPS)

Coarseness Factor: **63**
Workability Factor: **36**

Sieve	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	0.0	0.0
1.5"	100.0	0.0	0.0
1"	100.0	0.0	0.0
3/4"	95.6	4.4	4.4
1/2"	73.1	22.6	26.9
3/8"	59.3	13.8	40.7
#4	42.8	16.5	57.2
#8	35.7	7.1	64.3
#16	28.9	6.8	71.1
#30	20.7	8.2	79.3
#50	9.9	10.8	90.1
#100	2.1	7.8	97.9
LBW	0.9	1.2	99.1

PREPARED BY:
 SM, LLC Technical Service

Approved By:
