

Aggregate Optimization Chart

PLANT #: **P-101**

Sample Date: 11/9/20

Concrete Grade: **S2M**

Contractor: _____

Dates Test Represents: 11/10/2020 through 11/16/2020

MDOT No.: _____

Agg. Class	Pit #	Source	Weight (SSD)	ft ³	Specific Gravity	% Contribution
6AA	71-47	Presque Isle	1675	10.25	2.62	54.8
26A	71-47	Presque Isle	150	0.92	2.62	4.9
2NS	75-051	Mid-Michigan	1230	7.41	2.66	40.3
Total Wt			3055	18.57		100.0

<---- Verify this number is 100%



Superior Materials, LLC
 30701 W. 10 Mile Rd.
 Suite 500
 Farmington Hills, MI 48336

Sieve	6AA	26A	2NS	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	100.0	100.0	100.0	0.0	0.0
1.5"	100.0	100.0	100.0	100.0	0.0	0.0
1"	98.0	100.0	100.0	98.9	1.1	1.1
3/4"	82.5	100.0	100.0	90.4	8.5	9.6
1/2"	42.2	98.5	100.0	68.2	22.2	31.8
3/8"	25.6	89.6	100.0	58.7	9.5	41.3
#4	4.6	18.2	98.2	43.0	15.7	57.0
#8	2.4	4.7	81.6	34.4	8.6	65.6
#16	1.8	3.0	65.0	27.3	7.1	72.7
#30	1.7	2.6	48.5	20.6	6.7	79.4
#50	1.6	2.4	23.7	10.5	10.0	89.5
#100	1.6	2.2	4.5	2.8	7.7	97.2
LBW	1.5	1.9	0.5	1.1	1.7	98.9


*Maximum % Retained must be above the 3/8" sieve.
 *Any two adjacent sieves must equal 10% except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 4% for each sieve except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 8% for the 1" sieve when a 2" max. size (nom. Max. 1.5") aggregate is used.

Production Gradation Batch Plant Gradations Aggregate Supplier Gradations

Coarseness Factor:	63	Workability Factor:	34
---------------------------	-----------	----------------------------	-----------

Initial Production Sample (IPS)

Coarseness Factor:	64		
Workability Factor:	35		
Sieve	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	0.0	0.0
1.5"	100.0	0.0	0.0
1"	100.0	0.0	0.0
3/4"	93.9	6.1	6.1
1/2"	71.4	22.5	28.6
3/8"	59.0	12.4	41.0
#4	45.1	13.9	54.9
#8	35.5	9.6	64.5
#16	28.3	7.2	71.7
#30	21.3	6.9	78.7
#50	11.0	10.3	89.0
#100	3.4	7.6	96.6
LBW	1.1	2.3	98.9

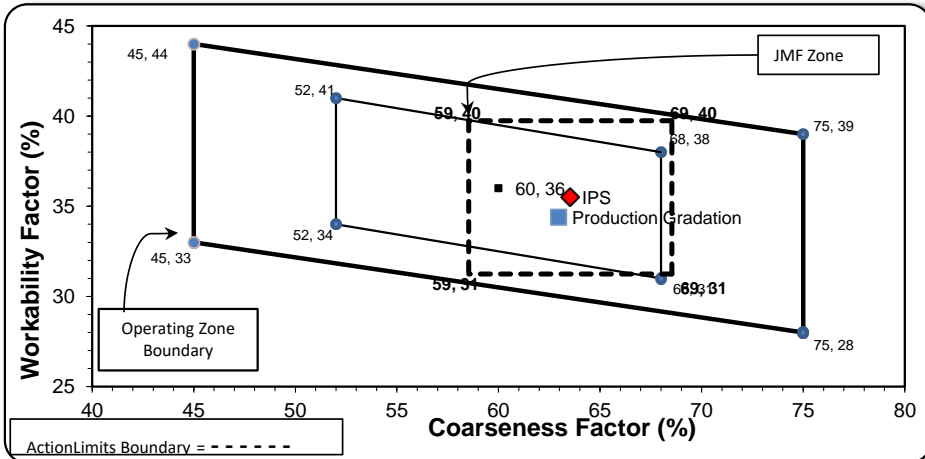

PREPARED BY:
 SM, LLC Technical Service

Approved By:

Aggregate Optimization Chart

PLANT #: **P-32**

Sample Date: 11/9/20

Concrete Grade: **S2M**

Contractor: _____

Dates Test Represents: 11/10/2020 through 11/16/2020

MDOT No.: _____

Agg. Class	Pit #	Source	Weight (SSD)	ft ³	Specific Gravity	% Contribution
6AA	71-47	Presque Isle	1670	10.21	2.62	54.8
26A	71-47	Presque Isle	150	0.92	2.62	4.9
2NS	95-013	Smelter Bay	1230	7.44	2.65	40.3
Total Wt			3050	18.57		100.0

<----- Verify this number is 100%




Superior Materials, LLC
 30701 W. 10 Mile Rd.
 Suite 500
 Farmington Hills, MI 48336

Sieve	6AA	26A	2NS	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	100.0	100.0	100.0	0.0	0.0
1.5"	100.0	100.0	100.0	100.0	0.0	0.0
1"	97.0	100.0	100.0	98.4	1.6	1.6
3/4"	80.3	100.0	100.0	89.2	9.1	10.8
1/2"	42.6	96.5	100.0	68.4	20.8	31.6
3/8"	26.3	84.6	100.0	58.9	9.5	41.1
#4	5.6	14.3	95.1	42.1	16.8	57.9
#8	2.5	4.4	82.8	35.0	7.1	65.0
#16	2.3	2.9	67.3	28.5	6.4	71.5
#30	2.2	2.5	46.5	20.1	8.5	79.9
#50	2.0	2.5	24.4	11.1	9.0	88.9
#100	1.9	2.5	8.6	4.6	6.4	95.4
LBW	1.5	1.7	1.1	1.3	3.3	98.7

*Maximum % Retained must be above the 3/8" sieve.
 *Any two adjacent sieves must equal 10% except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 4% for each sieve except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 8% for the 1" sieve when a 2" max. size (nom. Max. 1.5") aggregate is used.

Production Gradation Batch Plant Gradations Aggregate Supplier Gradations

Coarseness Factor:	63	Workability Factor:	35
---------------------------	-----------	----------------------------	-----------

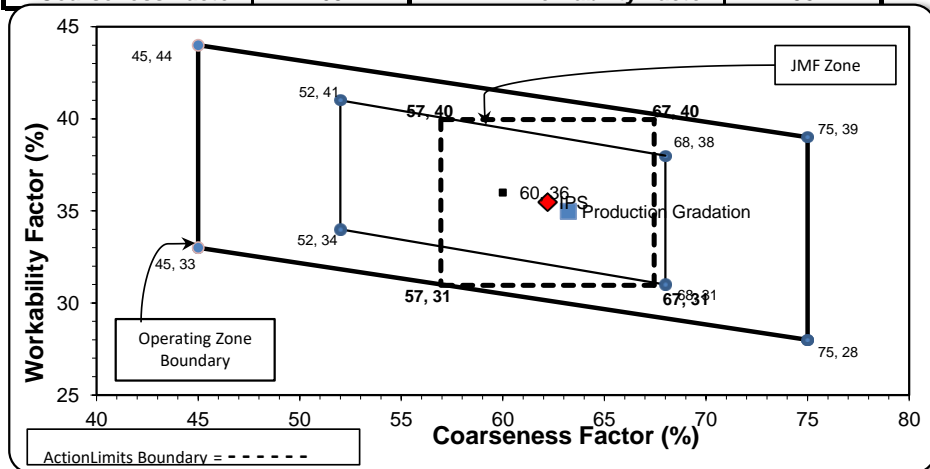

Initial Production Sample (IPS)

Coarseness Factor:	62		
Workability Factor:	35		
Sieve	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	0.0	0.0
1.5"	100.0	0.0	0.0
1"	100.0	0.0	0.0
3/4"	94.0	6.0	6.0
1/2"	70.2	23.7	29.8
3/8"	59.9	10.4	40.1
#4	42.7	17.2	57.3
#8	35.5	7.2	64.5
#16	28.4	7.0	71.6
#30	19.2	9.2	80.8
#50	8.9	10.3	91.1
#100	3.1	5.9	96.9
LBW	1.4	1.7	98.6

PREPARED BY:
 SM, LLC Technical Service

Approved By:

Aggregate Optimization Chart

PLANT #: **P-36**

Sample Date: 11/9/20

Concrete Grade: **S2M**

Contractor: _____

Dates Test Represents: 11/10/2020 through 11/16/2020

MDOT No.: _____

Agg. Class	Pit #	Source	Weight (SSD)	ft ³	Specific Gravity	% Contribution
6AA	71-47	Presque Isle	1650	10.09	2.62	54.1
26A	71-47	Presque Isle	200	1.22	2.62	6.6
2NS	63-92	Grange Hall	1200	7.26	2.65	39.3
Total Wt			3050	18.57		100.0

<----- Verify this number is 100%




Superior Materials, LLC
 30701 W. 10 Mile Rd.
 Suite 500
 Farmington Hills, MI 48336

Sieve	6AA	26A	2NS	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	100.0	100.0	100.0	0.0	0.0
1.5"	100.0	100.0	100.0	100.0	0.0	0.0
1"	96.8	100.0	100.0	98.3	1.7	1.7
3/4"	73.9	100.0	100.0	85.9	12.4	14.1
1/2"	38.9	96.5	100.0	66.7	19.2	33.3
3/8"	23.6	84.6	100.0	57.7	9.1	42.3
#4	5.3	14.3	97.2	42.0	15.6	58.0
#8	2.9	4.4	83.7	34.8	7.3	65.2
#16	2.4	2.9	68.4	28.4	6.4	71.6
#30	2.2	2.5	46.8	19.8	8.6	80.2
#50	2.1	2.5	17.4	8.1	11.6	91.9
#100	1.9	2.5	1.9	1.9	6.2	98.1
LBW	1.3	1.7	0.2	0.9	1.0	99.1

*Maximum % Retained must be above the 3/8" sieve.
 *Any two adjacent sieves must equal 10% except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 4% for each sieve except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 8% for the 1" sieve when a 2" max. size (nom. Max. 1.5") aggregate is used.

Production Gradation Batch Plant Gradations Aggregate Supplier Gradations

Coarseness Factor: **65** **Workability Factor:** **35**

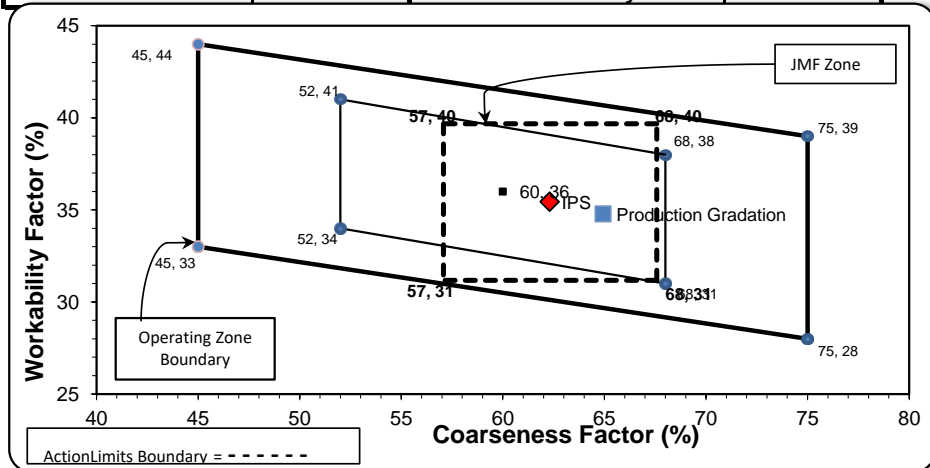

Initial Production Sample (IPS)

Coarseness Factor: **62**
Workability Factor: **35**

Sieve	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	0.0	0.0
1.5"	100.0	0.0	0.0
1"	99.1	0.9	0.9
3/4"	90.5	8.6	9.5
1/2"	69.8	20.7	30.2
3/8"	59.8	10.0	40.2
#4	42.2	17.6	57.8
#8	35.4	6.7	64.6
#16	28.8	6.7	71.2
#30	21.4	7.4	78.6
#50	8.8	12.6	91.2
#100	1.8	7.0	98.2
LBW	0.7	1.0	99.3

PREPARED BY:
 SM, LLC Technical Service

Approved By:

Aggregate Optimization Chart

PLANT #: **P-02**

Sample Date: 11/9/20

Concrete Grade: **S2M**

Contractor: _____

Dates Test Represents: 11/10/2020 through 11/16/2020

MDOT No.: _____

Agg. Class	Pit #	Source	Weight (SSD)	ft ³	Specific Gravity	% Contribution
6AA	71-47	Presque Isle	1650	10.09	2.62	54.1
26A	71-47	Presque Isle	100	0.61	2.62	3.3
2NS	63-115	Ray Rd	1300	7.86	2.65	42.6
Total Wt			3050	18.57		100.0

<----- Verify this number is 100%




Superior Materials, LLC
 30701 W. 10 Mile Rd.
 Suite 500
 Farmington Hills, MI 48336

Sieve	6AA	26A	2NS	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	100.0	100.0	100.0	0.0	0.0
1.5"	100.0	100.0	100.0	100.0	0.0	0.0
1"	96.8	100.0	100.0	98.3	1.7	1.7
3/4"	73.9	100.0	100.0	85.9	12.4	14.1
1/2"	38.9	96.5	100.0	66.8	19.0	33.2
3/8"	23.6	84.6	100.0	58.2	8.7	41.8
#4	5.3	14.3	97.9	45.1	13.1	54.9
#8	2.9	4.4	79.9	35.8	9.3	64.2
#16	2.4	2.9	62.6	28.1	7.7	71.9
#30	2.2	2.5	45.8	20.8	7.3	79.2
#50	2.1	2.5	20.4	9.9	10.9	90.1
#100	1.9	2.5	3.4	2.6	7.4	97.4
LBW	1.3	1.7	0.4	0.9	1.6	99.1

*Maximum % Retained must be above the 3/8" sieve.
 *Any two adjacent sieves must equal 10% except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 4% for each sieve except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 8% for the 1" sieve when a 2" max. size (nom. Max. 1.5") aggregate is used.

Production Gradation Batch Plant Gradations Aggregate Supplier Gradations

Coarseness Factor: **65** **Workability Factor:** **36**

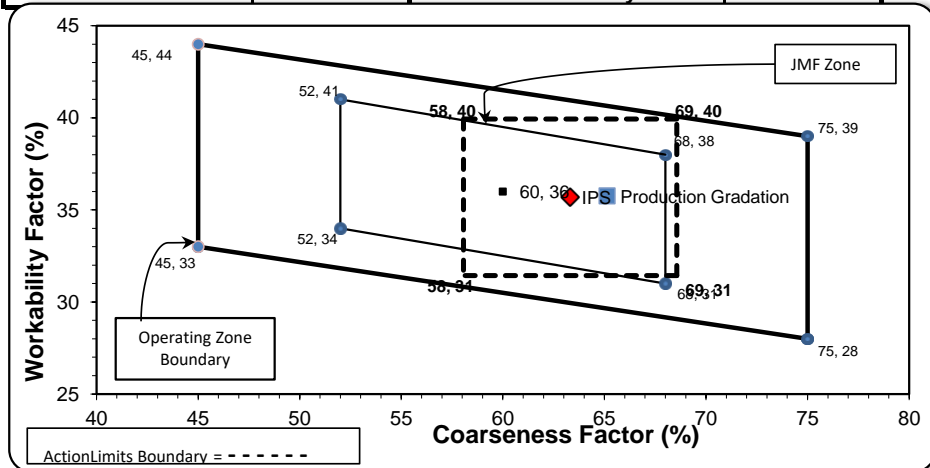

Initial Production Sample (IPS)

Coarseness Factor: 63		Workability Factor: 36	
Sieve	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	0.0	0.0
1.5"	100.0	0.0	0.0
1"	100.0	0.0	0.0
3/4"	95.6	4.4	4.4
1/2"	73.1	22.6	26.9
3/8"	59.3	13.8	40.7
#4	42.8	16.5	57.2
#8	35.7	7.1	64.3
#16	28.9	6.8	71.1
#30	20.7	8.2	79.3
#50	9.9	10.8	90.1
#100	2.1	7.8	97.9
LBW	0.9	1.2	99.1

PREPARED BY:
 SM, LLC Technical Service

Approved By:
