

# Aggregate Optimization Chart

**PLANT #:** **P-32**

Sample Date: 3/23/20 Concrete Grade: **S2M**  
 Dates Test Represents: 3/24/2020 through 3/30/2020

Contractor: \_\_\_\_\_

MDOT No.: \_\_\_\_\_

Agg. Class	Pit #	Source	Weight (SSD)	ft <sup>3</sup>	Specific Gravity	% Contribution
6AA	71-47	Presque Isle	1570	9.60	2.62	51.5
26A	71-47	Presque Isle	200	1.22	2.62	6.6
2NS	63-115	Ray Rd	1280	7.74	2.65	42.0
<b>Total Wt</b>			<b>3050</b>	<b>18.57</b>		<b>100.0</b>

<----- Verify this number is 100%




**Superior Materials, LLC**  
 30701 W. 10 Mile Rd.  
 Suite 500  
 Farmington Hills, MI 48336

Sieve	6AA	26A	2NS	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	100.0	100.0	100.0	0.0	0.0
1.5"	100.0	100.0	100.0	100.0	0.0	0.0
1"	98.8	100.0	100.0	99.4	0.6	0.6
3/4"	82.8	100.0	100.0	91.1	8.2	8.9
1/2"	42.9	99.4	100.0	70.6	20.6	29.4
3/8"	21.3	77.9	100.0	58.0	12.5	42.0
#4	3.9	15.8	96.7	43.6	14.4	56.4
#8	2.4	6.0	79.0	34.8	8.8	65.2
#16	2.1	4.1	62.1	27.4	7.4	72.6
#30	2.0	3.5	46.3	20.7	6.7	79.3
#50	1.8	3.3	23.4	11.0	9.7	89.0
#100	1.6	3.1	4.4	2.9	8.1	97.1
LBW	1.3	2.8	0.9	1.2	1.6	98.8

\*Maximum % Retained must be above the 3/8" sieve.  
 \*Any two adjacent sieves must equal 10% except max., nom. max., #100 and #200 sieves.  
 \*% Retained must be at least 4% for each sieve except max., nom. max., #100 and #200 sieves.  
 \*% Retained must be at least 8% for the 1" sieve when a 2" max. size (nom. Max. 1.5") aggregate is used.

Production Gradation  Batch Plant Gradations  Aggregate Supplier Gradations

**Coarseness Factor:** **64** **Workability Factor:** **35**

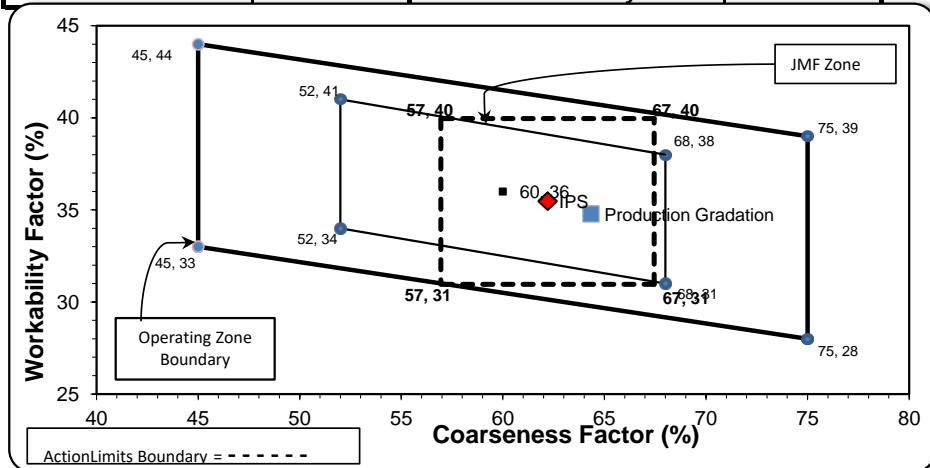

Initial Production Sample (IPS)

**Coarseness Factor:** **62**  
**Workability Factor:** **35**

Sieve	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	0.0	0.0
1.5"	100.0	0.0	0.0
1"	100.0	0.0	0.0
3/4"	94.0	6.0	6.0
1/2"	70.2	23.7	29.8
3/8"	59.9	10.4	40.1
#4	42.7	17.2	57.3
#8	35.5	7.2	64.5
#16	28.4	7.0	71.6
#30	19.2	9.2	80.8
#50	8.9	10.3	91.1
#100	3.1	5.9	96.9
LBW	1.4	1.7	98.6

PREPARED BY:  
 SM, LLC Technical Service

Approved By:

# Aggregate Optimization Chart

**PLANT #:** **P-36**

Sample Date: 3/23/20

Concrete Grade: **S2M**

Contractor: \_\_\_\_\_

Dates Test Represents: 3/24/2020 through 3/30/2020

MDOT No.: \_\_\_\_\_

Agg. Class	Pit #	Source	Weight (SSD)	ft <sup>3</sup>	Specific Gravity	% Contribution
6AA	71-47	Presque Isle	1450	8.87	2.62	47.5
26A	71-47	Presque Isle	400	2.45	2.62	13.1
2NS	63-92	Grange Hall	1200	7.26	2.65	39.3
<b>Total Wt</b>			<b>3050</b>	<b>18.57</b>		<b>100.0</b>

<----- Verify this number is 100%




**Superior Materials, LLC**  
 30701 W. 10 Mile Rd.  
 Suite 500  
 Farmington Hills, MI 48336

Sieve	6AA	26A	2NS	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	100.0	100.0	100.0	0.0	0.0
1.5"	100.0	100.0	100.0	100.0	0.0	0.0
1"	97.1	100.0	100.0	98.6	1.4	1.4
3/4"	72.7	100.0	100.0	87.0	11.6	13.0
1/2"	34.4	99.4	100.0	68.7	18.3	31.3
3/8"	16.9	77.9	100.0	57.6	11.1	42.4
#4	3.3	15.8	97.4	42.0	15.6	58.0
#8	1.6	6.0	84.5	34.8	7.2	65.2
#16	1.2	4.1	69.4	28.4	6.4	71.6
#30	1.0	3.5	50.4	20.8	7.6	79.2
#50	0.9	3.3	21.4	9.3	11.5	90.7
#100	0.8	3.1	3.0	2.0	7.3	98.0
LBW	0.5	2.8	0.6	0.8	1.1	99.2

\*Maximum % Retained must be above the 3/8" sieve.  
 \*Any two adjacent sieves must equal 10% except max., nom. max., #100 and #200 sieves.  
 \*% Retained must be at least 4% for each sieve except max., nom. max., #100 and #200 sieves.  
 \*% Retained must be at least 8% for the 1" sieve when a 2" max. size (nom. Max. 1.5") aggregate is used.

Production Gradation  Batch Plant Gradations  Aggregate Supplier Gradations

<b>Coarseness Factor:</b>	<b>65</b>	<b>Workability Factor:</b>	<b>35</b>
---------------------------	-----------	----------------------------	-----------

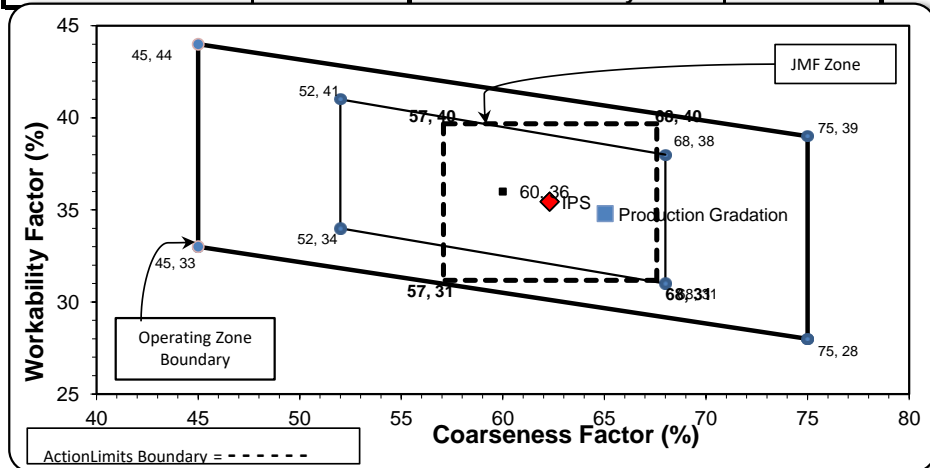

Initial Production Sample (IPS)

<b>Coarseness Factor:</b>	<b>62</b>		
<b>Workability Factor:</b>	<b>35</b>		
Sieve	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	0.0	0.0
1.5"	100.0	0.0	0.0
1"	99.1	0.9	0.9
3/4"	90.5	8.6	9.5
1/2"	69.8	20.7	30.2
3/8"	59.8	10.0	40.2
#4	42.2	17.6	57.8
#8	35.4	6.7	64.6
#16	28.8	6.7	71.2
#30	21.4	7.4	78.6
#50	8.8	12.6	91.2
#100	1.8	7.0	98.2
LBW	0.7	1.0	99.3

PREPARED BY:  
 SM, LLC Technical Service

Approved By:

# Aggregate Optimization Chart

**PLANT #:** **P-39**

Sample Date: 3/23/20

Concrete Grade: **S2M**

Contractor: \_\_\_\_\_

Dates Test Represents: 3/24/2020 through 3/30/2020

MDOT No.: \_\_\_\_\_

Agg. Class	Pit #	Source	Weight (SSD)	ft <sup>3</sup>	Specific Gravity	% Contribution
6AA	71-47	Presque Isle	1600	9.79	2.62	52.5
26A	71-47	Presque Isle	250	1.53	2.62	8.2
2NS	63-92	Grange Hall	1200	7.26	2.65	39.3
<b>Total Wt</b>			<b>3050</b>	<b>18.57</b>		<b>100.0</b>

<----- Verify this number is 100%




**Superior Materials, LLC**  
 30701 W. 10 Mile Rd.  
 Suite 500  
 Farmington Hills, MI 48336

Sieve	6AA	26A	2NS	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	100.0	100.0	100.0	0.0	0.0
1.5"	100.0	100.0	100.0	100.0	0.0	0.0
1"	99.3	100.0	100.0	99.6	0.4	0.4
3/4"	89.3	100.0	100.0	94.4	5.2	5.6
1/2"	49.0	99.4	100.0	73.2	21.2	26.8
3/8"	30.1	77.9	100.0	61.5	11.7	38.5
#4	5.2	15.8	97.4	42.3	19.2	57.7
#8	2.2	6.0	84.5	34.9	7.5	65.1
#16	1.9	4.1	69.4	28.6	6.3	71.4
#30	1.8	3.5	50.4	21.1	7.6	78.9
#50	1.7	3.3	21.4	9.6	11.5	90.4
#100	1.6	3.1	3.0	2.3	7.3	97.7
LBW	1.5	2.8	0.6	1.3	1.0	98.7

\*Maximum % Retained must be above the 3/8" sieve.  
 \*Any two adjacent sieves must equal 10% except max., nom. max., #100 and #200 sieves.  
 \*% Retained must be at least 4% for each sieve except max., nom. max., #100 and #200 sieves.  
 \*% Retained must be at least 8% for the 1" sieve when a 2" max. size (nom. Max. 1.5") aggregate is used.

Production Gradation  Batch Plant Gradations  Aggregate Supplier Gradations

**Coarseness Factor:** **59**      **Workability Factor:** **35**

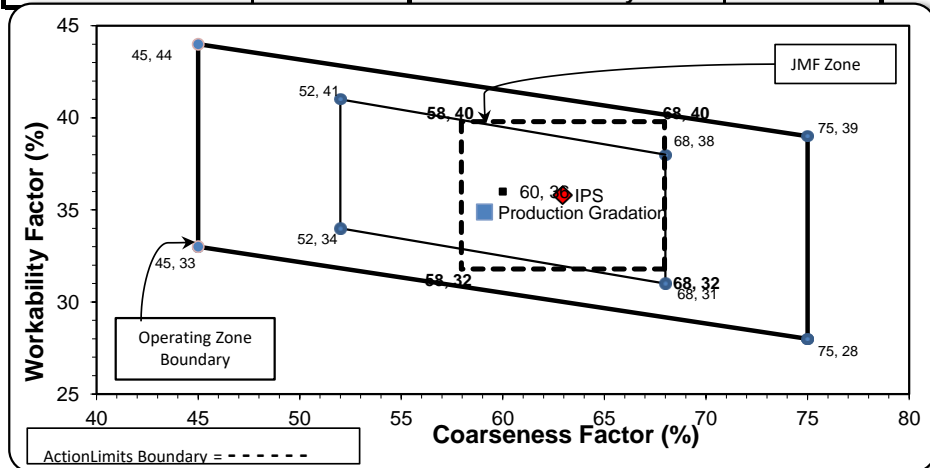

Initial Production Sample (IPS)

**Coarseness Factor:** **63**  
**Workability Factor:** **36**

Sieve	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	0.0	0.0
1.5"	100.0	0.0	0.0
1"	100.0	0.0	0.0
3/4"	89.8	10.2	10.2
1/2"	70.7	19.1	29.3
3/8"	59.6	11.1	40.4
#4	43.2	16.4	56.8
#8	35.8	7.4	64.2
#16	29.2	6.6	70.8
#30	21.4	7.8	78.6
#50	9.8	11.6	90.2
#100	3.7	6.1	96.3
LBW	1.2	2.5	98.8

PREPARED BY:  
 SM, LLC Technical Service

Approved By:

# Aggregate Optimization Chart

**PLANT #:** **P-02**

Sample Date: 3/23/20 Concrete Grade: **S2M**  
 Dates Test Represents: 3/24/2020 through 3/30/2020

Contractor: \_\_\_\_\_

MDOT No.: \_\_\_\_\_

Agg. Class	Pit #	Source	Weight (SSD)	ft <sup>3</sup>	Specific Gravity	% Contribution
6AA	71-47	Presque Isle	1450	8.87	2.62	47.5
26A	71-47	Presque Isle	300	1.83	2.62	9.8
2NS	63-115	Ray Rd	1300	7.86	2.65	42.6
<b>Total Wt</b>			<b>3050</b>	<b>18.57</b>		<b>100.0</b>

<----- Verify this number is 100%




**Superior Materials, LLC**  
 30701 W. 10 Mile Rd.  
 Suite 500  
 Farmington Hills, MI 48336

Sieve	6AA	26A	2NS	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	100.0	100.0	100.0	0.0	0.0
1.5"	100.0	100.0	100.0	100.0	0.0	0.0
1"	97.1	100.0	100.0	98.6	1.4	1.4
3/4"	72.7	100.0	100.0	87.0	11.6	13.0
1/2"	34.4	99.4	100.0	68.8	18.3	31.2
3/8"	16.9	77.9	100.0	58.3	10.4	41.7
#4	3.3	15.8	96.7	44.3	14.0	55.7
#8	1.6	6.0	79.0	35.0	9.3	65.0
#16	1.2	4.1	62.1	27.4	7.6	72.6
#30	1.0	3.5	46.3	20.6	6.9	79.4
#50	0.9	3.3	23.4	10.7	9.8	89.3
#100	0.8	3.1	4.4	2.6	8.2	97.4
LBW	0.5	2.8	0.9	0.9	1.7	99.1

\*Maximum % Retained must be above the 3/8" sieve.  
 \*Any two adjacent sieves must equal 10% except max., nom. max., #100 and #200 sieves.  
 \*% Retained must be at least 4% for each sieve except max., nom. max., #100 and #200 sieves.  
 \*% Retained must be at least 8% for the 1" sieve when a 2" max. size (nom. Max. 1.5") aggregate is used.

Production Gradation  Batch Plant Gradations  Aggregate Supplier Gradations

**Coarseness Factor:** **64** **Workability Factor:** **35**

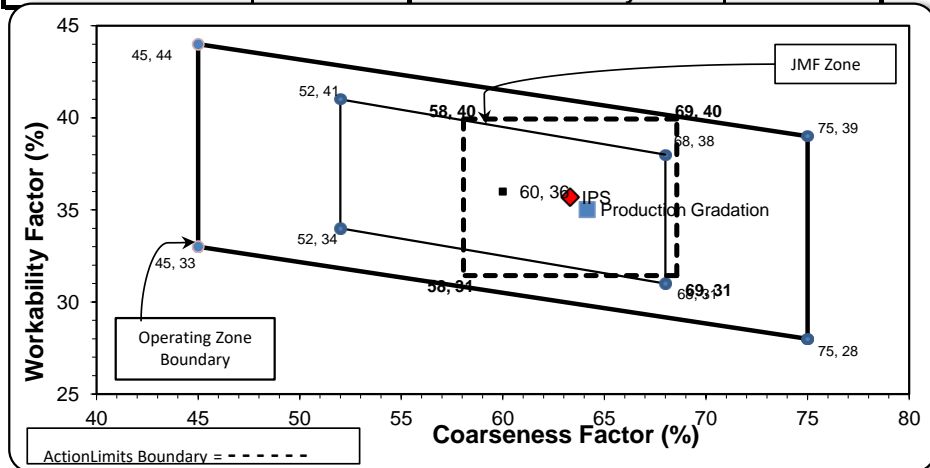

Initial Production Sample (IPS)

**Coarseness Factor:** **63**  
**Workability Factor:** **36**

Sieve	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	0.0	0.0
1.5"	100.0	0.0	0.0
1"	100.0	0.0	0.0
3/4"	95.6	4.4	4.4
1/2"	73.1	22.6	26.9
3/8"	59.3	13.8	40.7
#4	42.8	16.5	57.2
#8	35.7	7.1	64.3
#16	28.9	6.8	71.1
#30	20.7	8.2	79.3
#50	9.9	10.8	90.1
#100	2.1	7.8	97.9
LBW	0.9	1.2	99.1

PREPARED BY:  
 SM, LLC Technical Service

Approved By:
