

Aggregate Optimization Chart

PLANT #: **P-102**

Sample Date: 6/15/20

Concrete Grade: **S2M**

Contractor: _____

Dates Test Represents: 6/16/2020 through 6/22/2020

MDOT No.: _____

Agg. Class	Pit #	Source	Weight (SSD)	ft ³	Specific Gravity	% Contribution
6AA	58-003	Stoneco	1540	9.17	2.69	49.7
26A	58-003	Stoneco	350	2.09	2.69	11.3
2NS	63-114	Highland	1210	7.32	2.65	39.0
Total Wt			3100	18.58		100.0

<----- Verify this number is 100%




Superior Materials, LLC
 30701 W. 10 Mile Rd.
 Suite 500
 Farmington Hills, MI 48336

Sieve	6AA	26A	2NS	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	100.0	100.0	100.0	0.0	0.0
1.5"	100.0	100.0	100.0	100.0	0.0	0.0
1"	100.0	100.0	100.0	100.0	0.0	0.0
3/4"	81.1	100.0	100.0	90.6	9.4	9.4
1/2"	37.7	98.9	100.0	68.9	21.7	31.1
3/8"	15.0	83.5	100.0	55.9	13.0	44.1
#4	2.5	14.1	99.4	41.6	14.3	58.4
#8	1.6	3.3	85.9	34.7	6.9	65.3
#16	1.2	1.9	69.2	27.8	6.9	72.2
#30	0.9	1.5	50.5	20.3	7.5	79.7
#50	0.8	1.3	18.8	7.9	12.4	92.1
#100	0.7	1.3	3.3	1.8	6.1	98.2
LBW	0.7	0.9	0.3	0.6	1.2	99.4

*Maximum % Retained must be above the 3/8" sieve.
 *Any two adjacent sieves must equal 10% except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 4% for each sieve except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 8% for the 1" sieve when a 2" max. size (nom. Max. 1.5") aggregate is used.

Production Gradation Batch Plant Gradations Aggregate Supplier Gradations

Coarseness Factor:	68	Workability Factor:	35
---------------------------	-----------	----------------------------	-----------

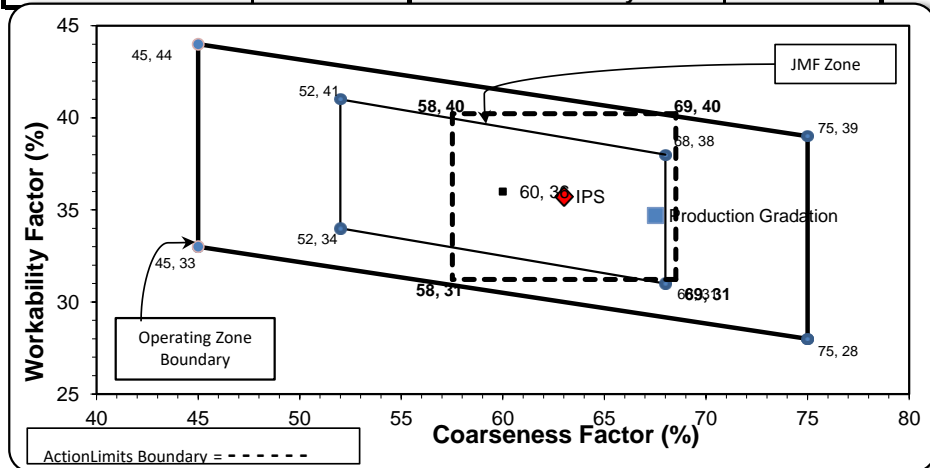

Initial Production Sample (IPS)

Coarseness Factor:	63		
Workability Factor:	36		
Sieve	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	0.0	0.0
1.5"	100.0	0.0	0.0
1"	99.2	0.8	0.8
3/4"	90.9	8.3	9.1
1/2"	71.3	19.6	28.7
3/8"	59.5	11.8	40.5
#4	43.8	15.7	56.2
#8	35.7	8.1	64.3
#16	27.0	8.7	73.0
#30	18.6	8.4	81.4
#50	6.8	11.8	93.2
#100	1.4	5.4	98.6
LBW	0.6	0.8	99.4

PREPARED BY:
 SM, LLC Technical Service

Approved By:

Aggregate Optimization Chart

PLANT #: **P-103**

Sample Date: 6/15/20

Concrete Grade: **S2M**

Contractor: _____

Dates Test Represents: 6/16/2020 through 6/22/2020

MDOT No.: _____

Agg. Class	Pit #	Source	Weight (SSD)	ft ³	Specific Gravity	% Contribution
6AA	58-003	Stoneco	1540	9.17	2.69	49.7
26A	58-003	Stoneco	350	2.09	2.69	11.3
2NS	63-114	Highland	1210	7.32	2.65	39.0
Total Wt			3100	18.58		100.0

<----- Verify this number is 100%




Superior Materials, LLC
 30701 W. 10 Mile Rd.
 Suite 500
 Farmington Hills, MI 48336

Sieve	6AA	26A	2NS	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	100.0	100.0	100.0	0.0	0.0
1.5"	100.0	100.0	100.0	100.0	0.0	0.0
1"	100.0	100.0	100.0	100.0	0.0	0.0
3/4"	81.1	100.0	100.0	90.6	9.4	9.4
1/2"	37.7	98.9	100.0	68.9	21.7	31.1
3/8"	15.0	83.5	100.0	55.9	13.0	44.1
#4	2.5	14.1	99.4	41.6	14.3	58.4
#8	1.6	3.3	85.9	34.7	6.9	65.3
#16	1.2	1.9	69.2	27.8	6.9	72.2
#30	0.9	1.5	50.5	20.3	7.5	79.7
#50	0.8	1.3	18.8	7.9	12.4	92.1
#100	0.7	1.3	3.3	1.8	6.1	98.2
LBW	0.7	0.9	0.3	0.6	1.2	99.4

*Maximum % Retained must be above the 3/8" sieve.
 *Any two adjacent sieves must equal 10% except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 4% for each sieve except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 8% for the 1" sieve when a 2" max. size (nom. Max. 1.5") aggregate is used.

Production Gradation Batch Plant Gradations Aggregate Supplier Gradations

Coarseness Factor:	68	Workability Factor:	35
---------------------------	-----------	----------------------------	-----------

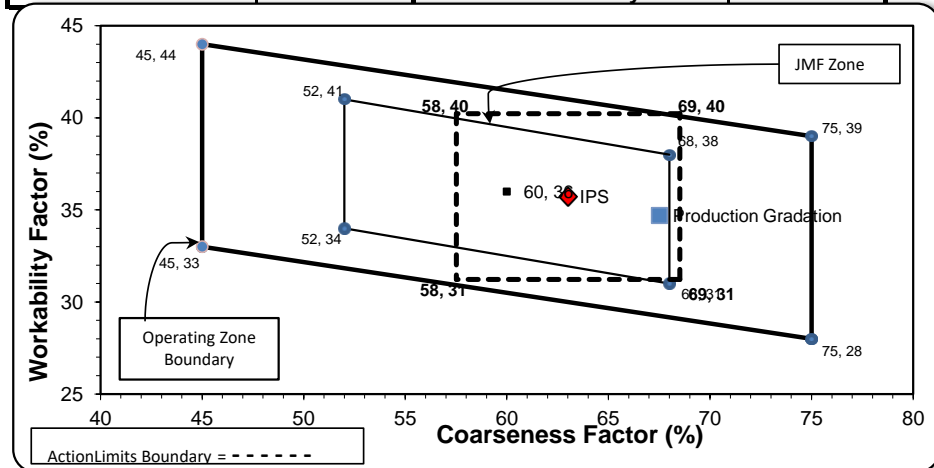

Initial Production Sample (IPS)

Coarseness Factor:	63
Workability Factor:	36

Sieve	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	0.0	0.0
1.5"	100.0	0.0	0.0
1"	99.2	0.8	0.8
3/4"	90.9	8.3	9.1
1/2"	71.3	19.6	28.7
3/8"	59.5	11.8	40.5
#4	43.8	15.7	56.2
#8	35.7	8.1	64.3
#16	27.0	8.7	73.0
#30	18.6	8.4	81.4
#50	6.8	11.8	93.2
#100	1.4	5.4	98.6
LBW	0.6	0.8	99.4

PREPARED BY:
 SM, LLC Technical Service

Approved BY:

Aggregate Optimization Chart

PLANT #: P-12

Sample Date: 6/15/20

Concrete Grade: S2M

Contractor: _____

Dates Test Represents: 6/16/2020 through 6/22/2020

MDOT No.: _____

Agg. Class	Pit #	Source	Weight (SSD)	ft ³	Specific Gravity	% Contribution
6AA	71-47	Presque Isle	1600	9.79	2.62	52.5
26A	71-47	Presque Isle	220	1.35	2.62	7.2
2NS	63-115	Ray Rd	1230	7.44	2.65	40.3
Total Wt			3050	18.57		100.0

<----- Verify this number is 100%




Superior Materials, LLC
 30701 W. 10 Mile Rd.
 Suite 500
 Farmington Hills, MI 48336

Sieve	6AA	26A	2NS	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	100.0	100.0	100.0	0.0	0.0
1.5"	100.0	100.0	100.0	100.0	0.0	0.0
1"	98.6	100.0	100.0	99.3	0.7	0.7
3/4"	76.5	100.0	100.0	87.7	11.6	12.3
1/2"	39.8	99.0	100.0	68.3	19.3	31.7
3/8"	23.4	86.2	100.0	58.8	9.5	41.2
#4	5.8	26.5	98.3	44.6	14.2	55.4
#8	2.9	8.7	80.2	34.5	10.1	65.5
#16	2.4	4.2	62.9	26.9	7.6	73.1
#30	2.2	3.2	47.2	20.4	6.5	79.6
#50	2.1	2.9	24.7	11.3	9.1	88.7
#100	1.9	2.5	5.7	3.5	7.8	96.5
LBW	1.4	2.0	0.6	1.1	2.4	98.9

*Maximum % Retained must be above the 3/8" sieve.
 *Any two adjacent sieves must equal 10% except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 4% for each sieve except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 8% for the 1" sieve when a 2" max. size (nom. Max. 1.5") aggregate is used.

Production Gradation Batch Plant Gradations Aggregate Supplier Gradations

Coarseness Factor:	63	Workability Factor:	34
---------------------------	-----------	----------------------------	-----------

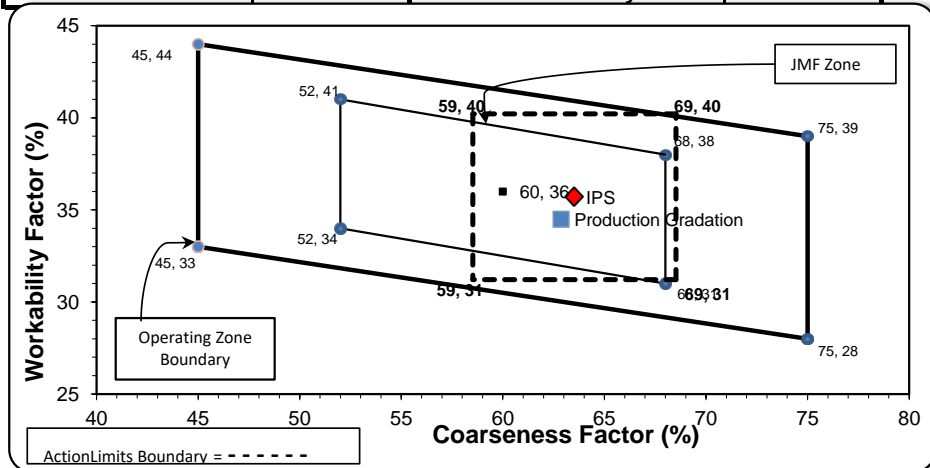

Initial Production Sample (IPS)

Coarseness Factor:	64		
Workability Factor:	36		
Sieve	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	0.0	0.0
1.5"	100.0	0.0	0.0
1"	99.2	0.8	0.8
3/4"	90.9	8.3	9.1
1/2"	71.3	19.6	28.7
3/8"	59.2	12.1	40.8
#4	41.5	17.7	58.5
#8	35.7	5.8	64.3
#16	27.9	7.9	72.1
#30	18.3	9.5	81.7
#50	7.3	11.0	92.7
#100	2.0	5.3	98.0
LBW	0.9	1.1	99.1

PREPARED BY:
 SM, LLC Technical Service

Approved By:

Aggregate Optimization Chart

PLANT #: **P-32**

Sample Date: 6/15/20

Concrete Grade: **S2M**

Contractor: _____

Dates Test Represents: 6/16/2020 through 6/22/2020

MDOT No.: _____

Agg. Class	Pit #	Source	Weight (SSD)	ft ³	Specific Gravity	% Contribution
6AA	71-47	Presque Isle	1520	9.30	2.62	49.8
26A	71-47	Presque Isle	300	1.83	2.62	9.8
2NS	95-013	Smelter Bay	1230	7.44	2.65	40.3
Total Wt			3050	18.57		100.0

<----- Verify this number is 100%




Superior Materials, LLC
 30701 W. 10 Mile Rd.
 Suite 500
 Farmington Hills, MI 48336

Sieve	6AA	26A	2NS	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	100.0	100.0	100.0	0.0	0.0
1.5"	100.0	100.0	100.0	100.0	0.0	0.0
1"	95.8	100.0	100.0	97.9	2.1	2.1
3/4"	78.9	100.0	100.0	89.5	8.4	10.5
1/2"	42.9	99.0	100.0	71.4	18.0	28.6
3/8"	24.9	86.2	100.0	61.2	10.2	38.8
#4	5.2	26.5	97.1	44.4	16.9	55.6
#8	2.6	8.7	85.5	36.6	7.7	63.4
#16	2.2	4.2	70.1	29.8	6.9	70.2
#30	2.0	3.2	49.2	21.2	8.6	78.8
#50	1.9	2.9	21.6	9.9	11.2	90.1
#100	1.8	2.5	6.2	3.6	6.3	96.4
LBW	1.4	2.0	1.4	1.5	2.2	98.5

*Maximum % Retained must be above the 3/8" sieve.
 *Any two adjacent sieves must equal 10% except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 4% for each sieve except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 8% for the 1" sieve when a 2" max. size (nom. Max. 1.5") aggregate is used.

Production Gradation Batch Plant Gradations Aggregate Supplier Gradations

Coarseness Factor: **61** **Workability Factor:** **37**

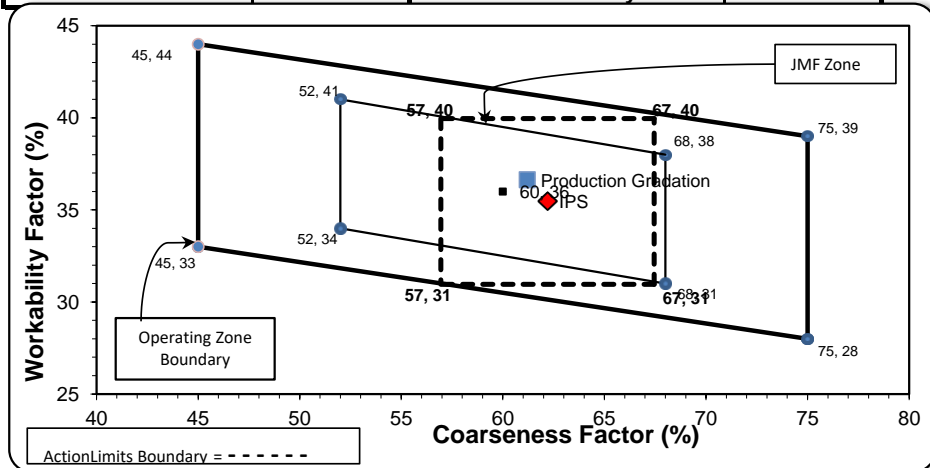

Initial Production Sample (IPS)

Coarseness Factor: **62**
Workability Factor: **35**

Sieve	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	0.0	0.0
1.5"	100.0	0.0	0.0
1"	100.0	0.0	0.0
3/4"	94.0	6.0	6.0
1/2"	70.2	23.7	29.8
3/8"	59.9	10.4	40.1
#4	42.7	17.2	57.3
#8	35.5	7.2	64.5
#16	28.4	7.0	71.6
#30	19.2	9.2	80.8
#50	8.9	10.3	91.1
#100	3.1	5.9	96.9
LBW	1.4	1.7	98.6

PREPARED BY:
 SM, LLC Technical Service

Approved By:

Aggregate Optimization Chart

PLANT #: **P-36**

Sample Date: 6/15/20

Concrete Grade: **S2M**

Contractor: _____

Dates Test Represents: 6/16/2020 through 6/22/2020

MDOT No.: _____

Agg. Class	Pit #	Source	Weight (SSD)	ft ³	Specific Gravity	% Contribution
6AA	71-47	Presque Isle	1500	9.17	2.62	49.2
26A	71-47	Presque Isle	350	2.14	2.62	11.5
2NS	63-92	Grange Hall	1200	7.26	2.65	39.3
Total Wt			3050	18.57		100.0

<----- Verify this number is 100%




Superior Materials, LLC
 30701 W. 10 Mile Rd.
 Suite 500
 Farmington Hills, MI 48336

Sieve	6AA	26A	2NS	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	100.0	100.0	100.0	0.0	0.0
1.5"	100.0	100.0	100.0	100.0	0.0	0.0
1"	98.6	100.0	100.0	99.3	0.7	0.7
3/4"	76.5	100.0	100.0	88.4	10.9	11.6
1/2"	39.8	99.0	100.0	70.3	18.2	29.7
3/8"	23.4	86.2	100.0	60.7	9.5	39.3
#4	5.8	26.5	97.9	44.4	16.3	55.6
#8	2.9	8.7	87.3	36.8	7.6	63.2
#16	2.4	4.2	73.3	30.5	6.3	69.5
#30	2.2	3.2	50.1	21.2	9.3	78.8
#50	2.1	2.9	17.8	8.4	12.8	91.6
#100	1.9	2.5	2.0	2.0	6.4	98.0
LBW	1.4	2.0	0.6	1.2	0.9	98.8

*Maximum % Retained must be above the 3/8" sieve.
 *Any two adjacent sieves must equal 10% except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 4% for each sieve except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 8% for the 1" sieve when a 2" max. size (nom. Max. 1.5") aggregate is used.

Production Gradation Batch Plant Gradations Aggregate Supplier Gradations

Coarseness Factor: **62** **Workability Factor:** **37**

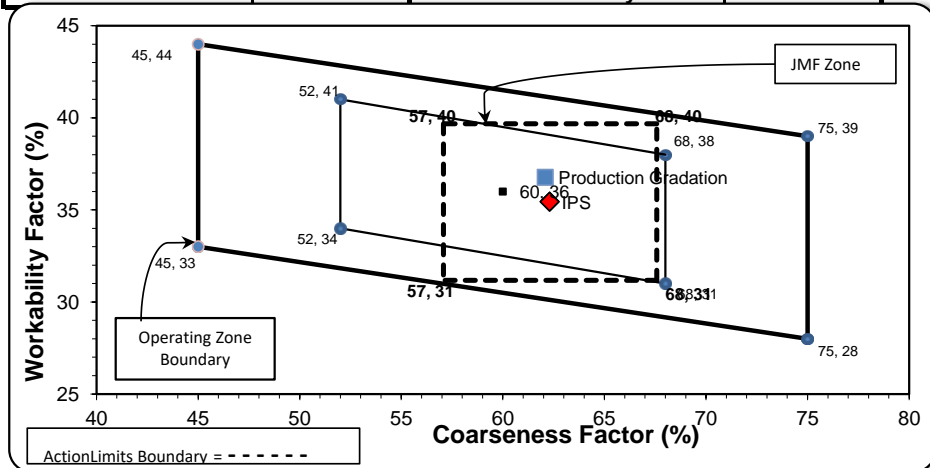

Initial Production Sample (IPS)

Coarseness Factor: **62**
Workability Factor: **35**

Sieve	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	0.0	0.0
1.5"	100.0	0.0	0.0
1"	99.1	0.9	0.9
3/4"	90.5	8.6	9.5
1/2"	69.8	20.7	30.2
3/8"	59.8	10.0	40.2
#4	42.2	17.6	57.8
#8	35.4	6.7	64.6
#16	28.8	6.7	71.2
#30	21.4	7.4	78.6
#50	8.8	12.6	91.2
#100	1.8	7.0	98.2
LBW	0.7	1.0	99.3

PREPARED BY:
 SM, LLC Technical Service

Approved By:

Aggregate Optimization Chart

PLANT #: **P-39**

Sample Date: 6/15/20 Concrete Grade: **S2M**
 Dates Test Represents: 6/16/2020 through 6/22/2020

Contractor: _____

MDOT No.: _____

Agg. Class	Pit #	Source	Weight (SSD)	ft ³	Specific Gravity	% Contribution
6AA	71-47	Presque Isle	1700	10.40	2.62	55.7
26A	71-47	Presque Isle	150	0.92	2.62	4.9
2NS	44-051	Krake Willis Rd	1200	7.26	2.65	39.3
Total Wt			3050	18.57		100.0

<----- Verify this number is 100%




Superior Materials, LLC
 30701 W. 10 Mile Rd.
 Suite 500
 Farmington Hills, MI 48336

Sieve	6AA	26A	2NS	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	100.0	100.0	100.0	0.0	0.0
1.5"	100.0	100.0	100.0	100.0	0.0	0.0
1"	97.5	100.0	100.0	98.6	1.4	1.4
3/4"	82.0	100.0	100.0	90.0	8.6	10.0
1/2"	39.7	98.5	100.0	66.3	23.7	33.7
3/8"	21.8	88.2	100.0	55.8	10.5	44.2
#4	3.7	15.5	95.9	40.6	15.3	59.4
#8	2.0	5.0	78.2	32.1	8.4	67.9
#16	1.7	2.8	64.4	26.4	5.7	73.6
#30	1.5	2.3	48.6	20.1	6.4	79.9
#50	1.5	2.1	23.7	10.3	9.8	89.7
#100	1.4	2.0	7.5	3.8	6.4	96.2
LBW	1.3	1.8	1.7	1.5	2.3	98.5

*Maximum % Retained must be above the 3/8" sieve.
 *Any two adjacent sieves must equal 10% except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 4% for each sieve except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 8% for the 1" sieve when a 2" max. size (nom. Max. 1.5") aggregate is used.

Production Gradation Batch Plant Gradations Aggregate Supplier Gradations

Coarseness Factor:	65	Workability Factor:	32
---------------------------	-----------	----------------------------	-----------

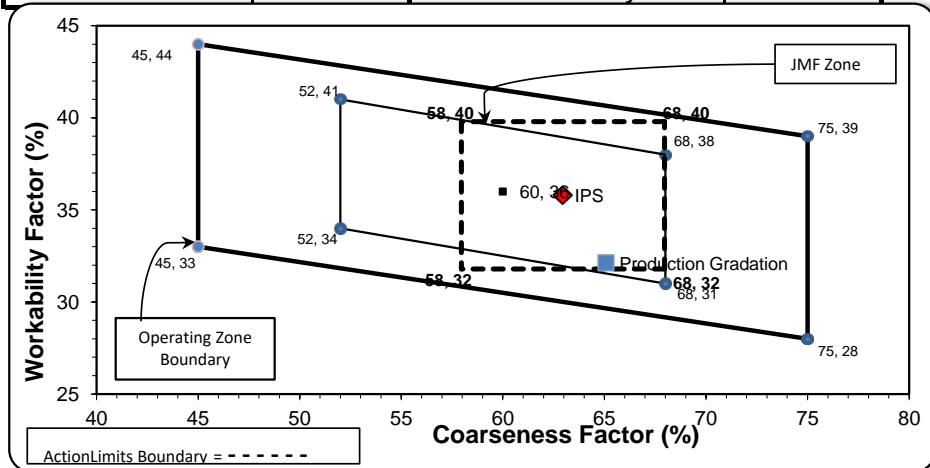

Initial Production Sample (IPS)

Coarseness Factor:	63		
Workability Factor:	36		
Sieve	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	0.0	0.0
1.5"	100.0	0.0	0.0
1"	100.0	0.0	0.0
3/4"	89.8	10.2	10.2
1/2"	70.7	19.1	29.3
3/8"	59.6	11.1	40.4
#4	43.2	16.4	56.8
#8	35.8	7.4	64.2
#16	29.2	6.6	70.8
#30	21.4	7.8	78.6
#50	9.8	11.6	90.2
#100	3.7	6.1	96.3
LBW	1.2	2.5	98.8

PREPARED BY:
 SM, LLC Technical Service

Approved By:

Aggregate Optimization Chart

PLANT #: **P-02**

Sample Date: 6/15/20 Concrete Grade: **S2M**
 Dates Test Represents: 6/16/2020 through 6/22/2020

Contractor: _____

MDOT No.: _____

Agg. Class	Pit #	Source	Weight (SSD)	ft ³	Specific Gravity	% Contribution
6AA	71-47	Presque Isle	1550	9.48	2.62	50.8
26A	71-47	Presque Isle	200	1.22	2.62	6.6
2NS	63-115	Ray Rd	1300	7.86	2.65	42.6
Total Wt			3050	18.57		100.0

<----- Verify this number is 100%




Superior Materials, LLC
 30701 W. 10 Mile Rd.
 Suite 500
 Farmington Hills, MI 48336

Sieve	6AA	26A	2NS	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	100.0	100.0	100.0	0.0	0.0
1.5"	100.0	100.0	100.0	100.0	0.0	0.0
1"	98.6	100.0	100.0	99.3	0.7	0.7
3/4"	76.5	100.0	100.0	88.1	11.2	11.9
1/2"	39.8	99.0	100.0	69.3	18.7	30.7
3/8"	23.4	86.2	100.0	60.2	9.2	39.8
#4	5.8	26.5	98.3	46.6	13.6	53.4
#8	2.9	8.7	80.2	36.2	10.4	63.8
#16	2.4	4.2	62.9	28.3	7.9	71.7
#30	2.2	3.2	47.2	21.4	6.9	78.6
#50	2.1	2.9	24.7	11.8	9.7	88.2
#100	1.9	2.5	5.7	3.6	8.2	96.4
LBW	1.4	2.0	0.6	1.1	2.5	98.9

*Maximum % Retained must be above the 3/8" sieve.
 *Any two adjacent sieves must equal 10% except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 4% for each sieve except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 8% for the 1" sieve when a 2" max. size (nom. Max. 1.5") aggregate is used.

Production Gradation Batch Plant Gradations Aggregate Supplier Gradations

Coarseness Factor: **62** **Workability Factor:** **36**

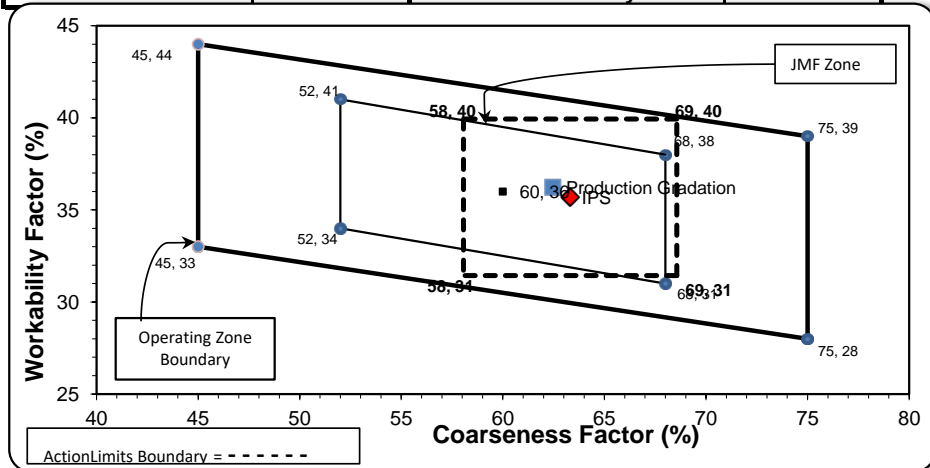

Initial Production Sample (IPS)

Coarseness Factor: **63**
Workability Factor: **36**

Sieve	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	0.0	0.0
1.5"	100.0	0.0	0.0
1"	100.0	0.0	0.0
3/4"	95.6	4.4	4.4
1/2"	73.1	22.6	26.9
3/8"	59.3	13.8	40.7
#4	42.8	16.5	57.2
#8	35.7	7.1	64.3
#16	28.9	6.8	71.1
#30	20.7	8.2	79.3
#50	9.9	10.8	90.1
#100	2.1	7.8	97.9
LBW	0.9	1.2	99.1

PREPARED BY:
 SM, LLC Technical Service

Approved By:
