

# Aggregate Optimization Chart

**PLANT #:** **P-101**

Sample Date: 8/1/22

Concrete Grade: **P1M, 3500HP**

Dates Test Represents: 8/2/2022 through 8/8/2022

Contractor: \_\_\_\_\_

MDOT No.: \_\_\_\_\_

Agg. Class	Pit #	Source	Weight (SSD)	ft <sup>3</sup>	Specific Gravity	% Contribution
CA	71-47	Presque Isle	1070	6.54	2.62	34.9
IA	71-47	Presque Isle	800	4.89	2.62	26.1
2NS	75-051	Mid Michigan	1200	7.23	2.66	39.1
<b>Total Wt</b>			<b>3070</b>	<b>18.67</b>		<b>100.0</b>

<---- Verify this number is 100%



**Superior Materials, LLC**  
 30701 W. 10 Mile Rd.  
 Suite 500  
 Farmington Hills, MI 48336

Sieve	CA	IA	2NS	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	100.0	100.0	100.0	0.0	0.0
1.5"	97.8	100.0	100.0	99.2	0.8	0.8
1"	47.5	100.0	100.0	81.7	17.5	18.3
3/4"	13.7	98.5	100.0	69.5	12.2	30.5
1/2"	3.8	83.2	100.0	62.1	7.4	37.9
3/8"	2.6	63.7	100.0	56.6	5.5	43.4
#4	2.2	17.3	99.0	44.0	12.6	56.0
#8	2.0	4.5	85.3	35.2	8.8	64.8
#16	1.8	2.7	70.1	28.7	6.5	71.3
#30	1.7	2.3	53.2	22.0	6.7	78.0
#50	1.7	2.1	26.3	11.4	10.6	88.6
#100	1.6	1.9	6.8	3.7	7.7	96.3
LBW	1.4	1.7	1.0	1.3	2.4	98.7

\*Maximum % Retained must be above the 3/8" sieve.  
 \*Any two adjacent sieves must equal 10% except max., nom. max., #100 and #200 sieves.  
 \*% Retained must be at least 4% for each sieve except max., nom. max., #100 and #200 sieves.  
 \*% Retained must be at least 8% for the 1" sieve when a 2" max. size (nom. Max. 1.5") aggregate is used.

Production Gradation  Batch Plant Gradations  Aggregate Supplier Gradations


<b>Coarseness Factor:</b>	<b>67</b>	<b>Workability Factor:</b>	<b>35</b>
---------------------------	-----------	----------------------------	-----------

Initial Production Sample (IPS)

<b>Coarseness Factor:</b>	<b>66</b>
---------------------------	-----------

<b>Workability Factor:</b>	<b>35</b>
----------------------------	-----------

Sieve	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	0.0	0.0
1.5"	99.6	0.4	0.4
1"	84.3	15.3	15.7
3/4"	74.8	9.6	25.2
1/2"	64.3	10.4	35.7
3/8"	56.8	7.5	43.2
#4	43.0	13.8	57.0
#8	34.9	8.1	65.1
#16	26.4	8.5	73.6
#30	19.9	6.5	80.1
#50	10.4	9.5	89.6
#100	3.4	7.0	96.6
LBW	1.2	2.2	98.8

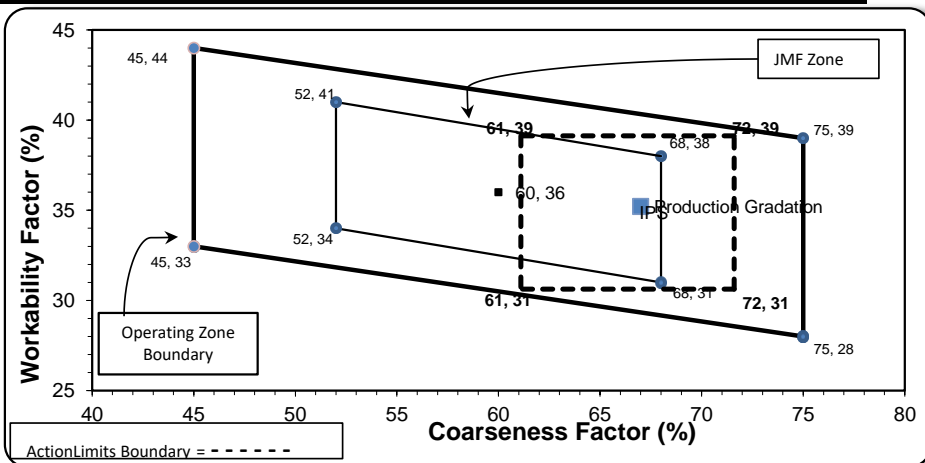

PREPARED BY:  
 SM, LLC Technical Service

Approved By:

# Aggregate Optimization Chart

**PLANT #:** **P-102**

Sample Date: 8/1/22

Concrete Grade: **P1M, 3500HP**

Dates Test Represents: 8/2/2022 through 8/8/2022

Contractor: \_\_\_\_\_

MDOT No.: \_\_\_\_\_

Agg. Class	Pit #	Source	Weight (SSD)	ft <sup>3</sup>	Specific Gravity	% Contribution
CA	58-003	Stoneco	1370	8.16	2.69	43.9
IA	58-003	Stoneco	550	3.28	2.69	17.6
2NS	81-019	Pleasant Lake	1200	7.26	2.65	38.5
<b>Total Wt</b>			<b>3120</b>	<b>18.70</b>		<b>100.0</b>

<----- Verify this number is 100%




**Superior Materials, LLC**  
 30701 W. 10 Mile Rd.  
 Suite 500  
 Farmington Hills, MI 48336

Sieve	CA	IA	2NS	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	100.0	100.0	100.0	0.0	0.0
1.5"	100.0	100.0	100.0	100.0	0.0	0.0
1"	68.5	100.0	100.0	86.2	13.8	13.8
3/4"	38.8	100.0	100.0	73.1	13.0	26.9
1/2"	7.8	92.1	100.0	58.1	15.0	41.9
3/8"	4.5	76.4	100.0	53.9	4.2	46.1
#4	2.4	19.6	99.1	42.6	11.3	57.4
#8	1.8	4.0	85.3	34.3	8.3	65.7
#16	1.5	2.1	68.1	27.2	7.1	72.8
#30	1.4	1.7	51.0	20.5	6.7	79.5
#50	1.2	1.4	27.0	11.2	9.4	88.8
#100	1.2	1.3	8.8	4.1	7.0	95.9
LBW	1.0	1.0	1.6	1.2	2.9	98.8

\*Maximum % Retained must be above the 3/8" sieve.  
 \*Any two adjacent sieves must equal 10% except max., nom. max., #100 and #200 sieves.  
 \*% Retained must be at least 4% for each sieve except max., nom. max., #100 and #200 sieves.  
 \*% Retained must be at least 8% for the 1" sieve when a 2" max. size (nom. Max. 1.5") aggregate is used.

Production Gradation  Batch Plant Gradations  Aggregate Supplier Gradations

**Coarseness Factor:** **70**      **Workability Factor:** **34**

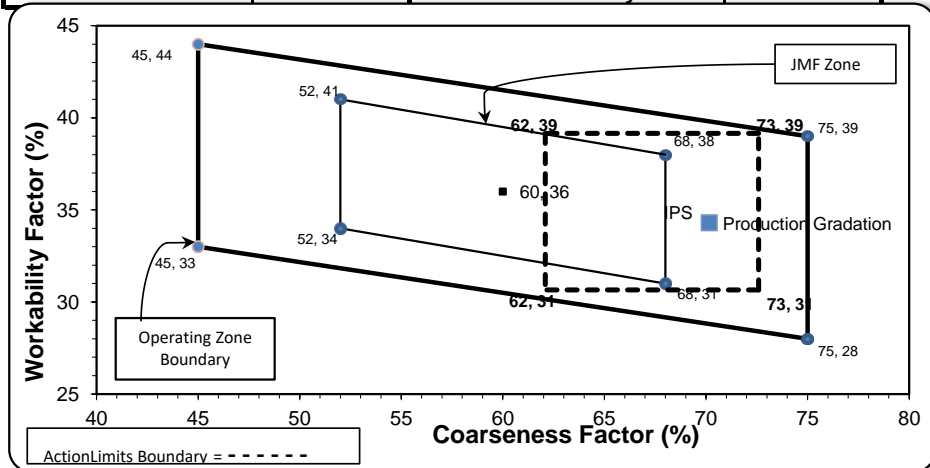

Initial Production Sample (IPS)

**Coarseness Factor:** **67**  
**Workability Factor:** **35**

Sieve	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	0.0	0.0
1.5"	100.0	0.0	0.0
1"	85.5	14.5	14.5
3/4"	73.4	12.1	26.6
1/2"	61.0	12.4	39.0
3/8"	56.2	4.8	43.8
#4	43.1	13.1	56.9
#8	34.9	8.2	65.1
#16	29.4	5.5	70.6
#30	21.6	7.8	78.4
#50	8.1	13.4	91.9
#100	2.2	5.9	97.8
LBW	1.4	0.8	98.6

PREPARED BY:  
 SM, LLC Technical Service

Approved By:

# Aggregate Optimization Chart

**PLANT #:** **P-103**

Sample Date: 8/1/22

Concrete Grade: **P1M, 3500HP**

Dates Test Represents: 8/2/2022 through 8/8/2022

Contractor: \_\_\_\_\_

MDOT No.: \_\_\_\_\_

Agg. Class	Pit #	Source	Weight (SSD)	ft <sup>3</sup>	Specific Gravity	% Contribution
CA	58-003	Stoneco	1370	8.16	2.69	43.9
IA	58-003	Stoneco	550	3.28	2.69	17.6
2NS	81-019	Pleasant Lake	1200	7.26	2.65	38.5
<b>Total Wt</b>			<b>3120</b>	<b>18.70</b>		<b>100.0</b>

<----- Verify this number is 100%




**Superior Materials, LLC**  
 30701 W. 10 Mile Rd.  
 Suite 500  
 Farmington Hills, MI 48336

Sieve	CA	IA	2NS	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	100.0	100.0	100.0	0.0	0.0
1.5"	100.0	100.0	100.0	100.0	0.0	0.0
1"	68.5	100.0	100.0	86.2	13.8	13.8
3/4"	38.8	100.0	100.0	73.1	13.0	26.9
1/2"	7.8	92.1	100.0	58.1	15.0	41.9
3/8"	4.5	76.4	100.0	53.9	4.2	46.1
#4	2.4	19.6	99.1	42.6	11.3	57.4
#8	1.8	4.0	85.3	34.3	8.3	65.7
#16	1.5	2.1	68.1	27.2	7.1	72.8
#30	1.4	1.7	51.0	20.5	6.7	79.5
#50	1.2	1.4	27.0	11.2	9.4	88.8
#100	1.2	1.3	8.8	4.1	7.0	95.9
LBW	1.0	1.0	1.6	1.2	2.9	98.8

\*Maximum % Retained must be above the 3/8" sieve.  
 \*Any two adjacent sieves must equal 10% except max., nom. max., #100 and #200 sieves.  
 \*% Retained must be at least 4% for each sieve except max., nom. max., #100 and #200 sieves.  
 \*% Retained must be at least 8% for the 1" sieve when a 2" max. size (nom. Max. 1.5") aggregate is used.

Production Gradation  Batch Plant Gradations  Aggregate Supplier Gradations

**Coarseness Factor:** **70**      **Workability Factor:** **34**

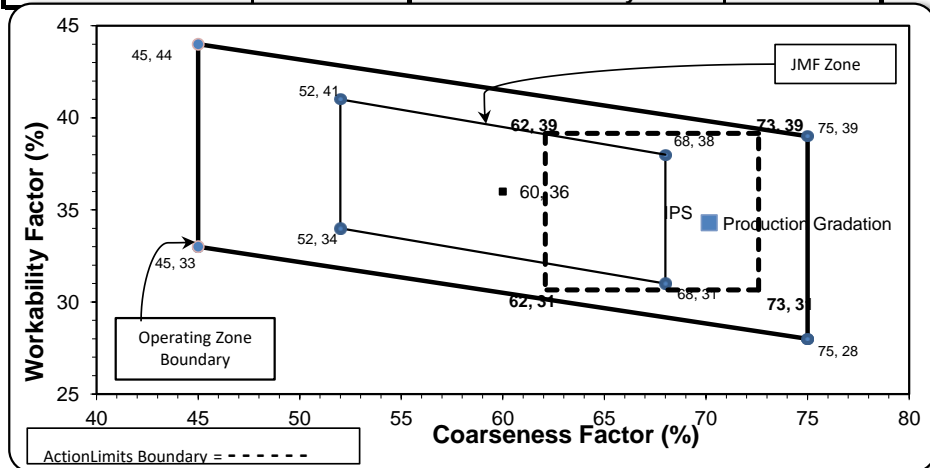

Initial Production Sample (IPS)

**Coarseness Factor:** **67**  
**Workability Factor:** **35**

Sieve	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	0.0	0.0
1.5"	100.0	0.0	0.0
1"	85.5	14.5	14.5
3/4"	73.4	12.1	26.6
1/2"	61.0	12.4	39.0
3/8"	56.2	4.8	43.8
#4	43.1	13.1	56.9
#8	34.9	8.2	65.1
#16	29.4	5.5	70.6
#30	21.6	7.8	78.4
#50	8.1	13.4	91.9
#100	2.2	5.9	97.8
LBW	1.4	0.8	98.6

PREPARED BY:  
 SM, LLC Technical Service

Approved BY:

# Aggregate Optimization Chart

**PLANT #:** **P-12**

Sample Date: 8/1/22

Concrete Grade: **P1M, 3500HP**

Contractor: \_\_\_\_\_

Dates Test Represents: 8/2/2022 through 8/8/2022

MDOT No.: \_\_\_\_\_

Agg. Class	Pit #	Source	Weight (SSD)	ft <sup>3</sup>	Specific Gravity	% Contribution
CA	71-47	Presque Isle	970	5.93	2.62	31.6
IA	71-47	Presque Isle	850	5.20	2.62	27.7
2NS	63-115	Ray Rd	1250	7.56	2.65	40.7
<b>Total Wt</b>			<b>3070</b>	<b>18.69</b>		<b>100.0</b>

<----- Verify this number is 100%




**Superior Materials, LLC**  
 30701 W. 10 Mile Rd.  
 Suite 500  
 Farmington Hills, MI 48336

Sieve	CA	IA	2NS	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	100.0	100.0	100.0	0.0	0.0
1.5"	94.5	100.0	100.0	98.3	1.7	1.7
1"	28.8	100.0	100.0	77.5	20.8	22.5
3/4"	6.0	98.5	100.0	69.9	7.6	30.1
1/2"	2.5	80.0	100.0	63.7	6.2	36.3
3/8"	2.0	57.4	100.0	57.2	6.4	42.8
#4	1.7	11.6	96.2	42.9	14.3	57.1
#8	1.6	3.2	76.6	32.6	10.3	67.4
#16	1.5	2.1	59.7	25.4	7.2	74.6
#30	1.4	1.9	43.9	18.8	6.5	81.2
#50	1.4	1.8	25.4	11.3	7.6	88.7
#100	1.2	1.6	7.6	3.9	7.4	96.1
LBW	0.9	1.4	1.5	1.3	2.6	98.7

\*Maximum % Retained must be above the 3/8" sieve.  
 \*Any two adjacent sieves must equal 10% except max., nom. max., #100 and #200 sieves.  
 \*% Retained must be at least 4% for each sieve except max., nom. max., #100 and #200 sieves.  
 \*% Retained must be at least 8% for the 1" sieve when a 2" max. size (nom. Max. 1.5") aggregate is used.

Production Gradation  Batch Plant Gradations  Aggregate Supplier Gradations

<b>Coarseness Factor:</b>	<b>63</b>	<b>Workability Factor:</b>	<b>33</b>
---------------------------	-----------	----------------------------	-----------

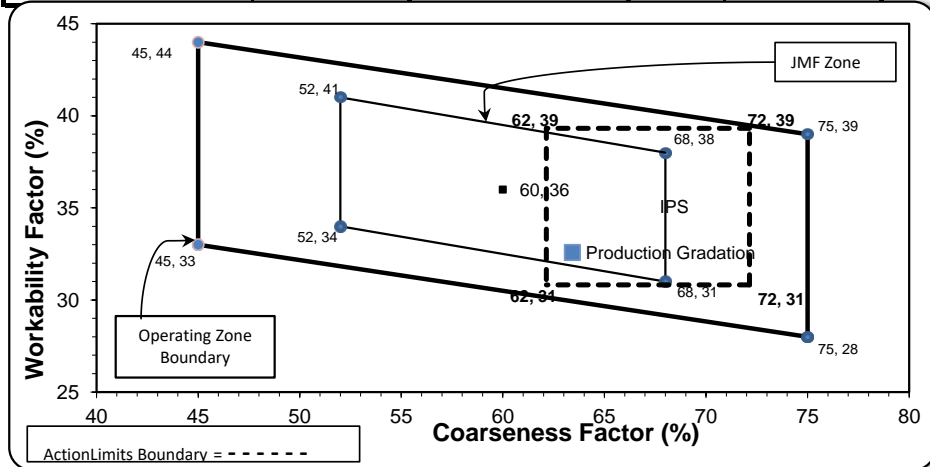

Intial Production Sample (IPS)

<b>Coarseness Factor:</b>	<b>67</b>
<b>Workability Factor:</b>	<b>35</b>

Sieve	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	0.0	0.0
1.5"	99.6	0.4	0.4
1"	83.9	15.7	16.1
3/4"	74.0	9.8	26.0
1/2"	63.7	10.3	36.3
3/8"	56.4	7.3	43.6
#4	43.0	13.4	57.0
#8	35.1	7.9	64.9
#16	29.0	6.1	71.0
#30	20.9	8.0	79.1
#50	8.1	12.8	91.9
#100	1.6	6.5	98.4
LBW	0.9	0.8	99.1

PREPARED BY:  
 SM, LLC Technical Service

Approved By:

# Aggregate Optimization Chart

**PLANT #:** **P-32**

Sample Date: 8/1/22

Concrete Grade: **P1M, 3500HP**

Dates Test Represents: 8/2/2022 through 8/8/2022

Contractor: \_\_\_\_\_

MDOT No.: \_\_\_\_\_

Agg. Class	Pit #	Source	Weight (SSD)	ft <sup>3</sup>	Specific Gravity	% Contribution
CA	71-47	Presque Isle	900	5.50	2.62	29.3
IA	71-47	Presque Isle	920	5.63	2.62	30.0
2NS	95-013	Smelter Bay	1250	7.56	2.65	40.7
<b>Total Wt</b>			<b>3070</b>	<b>18.69</b>		<b>100.0</b>

<----- Verify this number is 100%




**Superior Materials, LLC**  
 30701 W. 10 Mile Rd.  
 Suite 500  
 Farmington Hills, MI 48336

Sieve	CA	IA	2NS	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	100.0	100.0	100.0	0.0	0.0
1.5"	94.5	100.0	100.0	98.4	1.6	1.6
1"	28.8	100.0	100.0	79.1	19.3	20.9
3/4"	6.0	98.5	100.0	72.0	7.1	28.0
1/2"	2.5	80.0	100.0	65.4	6.6	34.6
3/8"	2.0	57.4	100.0	58.5	6.9	41.5
#4	1.7	11.6	96.0	43.1	15.4	56.9
#8	1.6	3.2	82.3	34.9	8.1	65.1
#16	1.5	2.1	66.8	28.3	6.7	71.7
#30	1.4	1.9	47.7	20.4	7.9	79.6
#50	1.4	1.8	23.3	10.4	10.0	89.6
#100	1.2	1.6	7.2	3.8	6.7	96.2
LBW	0.9	1.4	1.3	1.2	2.6	98.8

\*Maximum % Retained must be above the 3/8" sieve.  
 \*Any two adjacent sieves must equal 10% except max., nom. max., #100 and #200 sieves.  
 \*% Retained must be at least 4% for each sieve except max., nom. max., #100 and #200 sieves.  
 \*% Retained must be at least 8% for the 1" sieve when a 2" max. size (nom. Max. 1.5") aggregate is used.

Production Gradation  Batch Plant Gradations  Aggregate Supplier Gradations

**Coarseness Factor:** **64**      **Workability Factor:** **35**

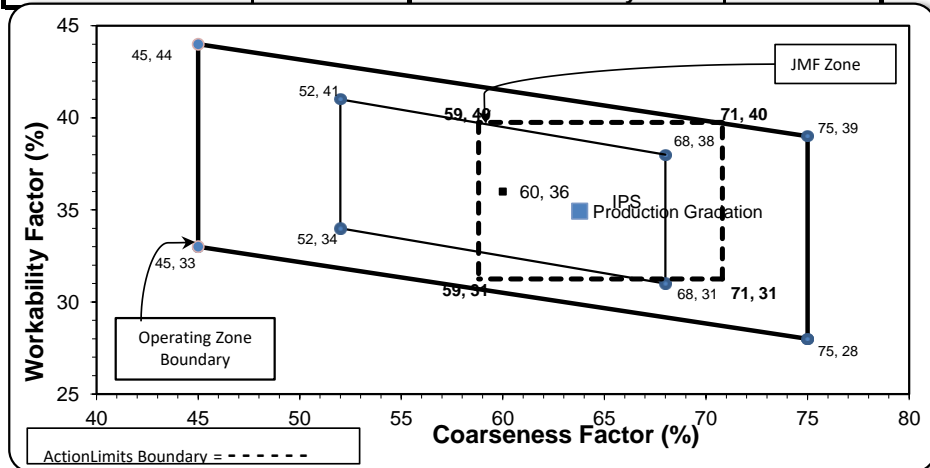

Initial Production Sample (IPS)

**Coarseness Factor:** **65**  
**Workability Factor:** **36**

Sieve	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	0.0	0.0
1.5"	99.0	0.6	0.6
1"	84.0	15.3	16.0
3/4"	73.5	10.5	26.5
1/2"	65.2	8.2	34.8
3/8"	58.2	7.1	41.8
#4	44.1	14.1	55.9
#8	35.5	8.6	64.5
#16	29.1	6.4	70.9
#30	21.9	7.3	78.1
#50	9.6	12.2	90.4
#100	2.6	7.1	97.4
LBW	1.0	1.6	99.0

PREPARED BY:  
 SM, LLC Technical Service

Approved By:

# Aggregate Optimization Chart

**PLANT #:** **P-35**

Sample Date: 8/1/22

Concrete Grade: **P1M, 3500HP**

Dates Test Represents: 8/2/2022 through 8/8/2022

Contractor: \_\_\_\_\_

MDOT No.: \_\_\_\_\_

Agg. Class	Pit #	Source	Weight (SSD)	ft <sup>3</sup>	Specific Gravity	% Contribution
CA	58-003	Stoneco	1370	8.16	2.69	43.9
IA	58-003	Stoneco	550	3.28	2.69	17.6
2NS	81-019	Pleasant Lake	1200	7.26	2.65	38.5
<b>Total Wt</b>			<b>3120</b>	<b>18.70</b>		<b>100.0</b>

<----- Verify this number is 100%




**Superior Materials, LLC**  
 30701 W. 10 Mile Rd.  
 Suite 500  
 Farmington Hills, MI 48336

Sieve	CA	IA	2NS	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	100.0	100.0	100.0	0.0	0.0
1.5"	100.0	100.0	100.0	100.0	0.0	0.0
1"	68.5	100.0	100.0	86.2	13.8	13.8
3/4"	38.8	100.0	100.0	73.1	13.0	26.9
1/2"	7.8	92.1	100.0	58.1	15.0	41.9
3/8"	4.5	76.4	100.0	53.9	4.2	46.1
#4	2.4	19.6	99.1	42.6	11.3	57.4
#8	1.8	4.0	85.3	34.3	8.3	65.7
#16	1.5	2.1	68.1	27.2	7.1	72.8
#30	1.4	1.7	51.0	20.5	6.7	79.5
#50	1.2	1.4	27.0	11.2	9.4	88.8
#100	1.2	1.3	8.8	4.1	7.0	95.9
LBW	1.0	1.0	1.6	1.2	2.9	98.8

\*Maximum % Retained must be above the 3/8" sieve.  
 \*Any two adjacent sieves must equal 10% except max., nom. max., #100 and #200 sieves.  
 \*% Retained must be at least 4% for each sieve except max., nom. max., #100 and #200 sieves.  
 \*% Retained must be at least 8% for the 1" sieve when a 2" max. size (nom. Max. 1.5") aggregate is used.

Production Gradation  Batch Plant Gradations  Aggregate Supplier Gradations

**Coarseness Factor:** **70**      **Workability Factor:** **34**

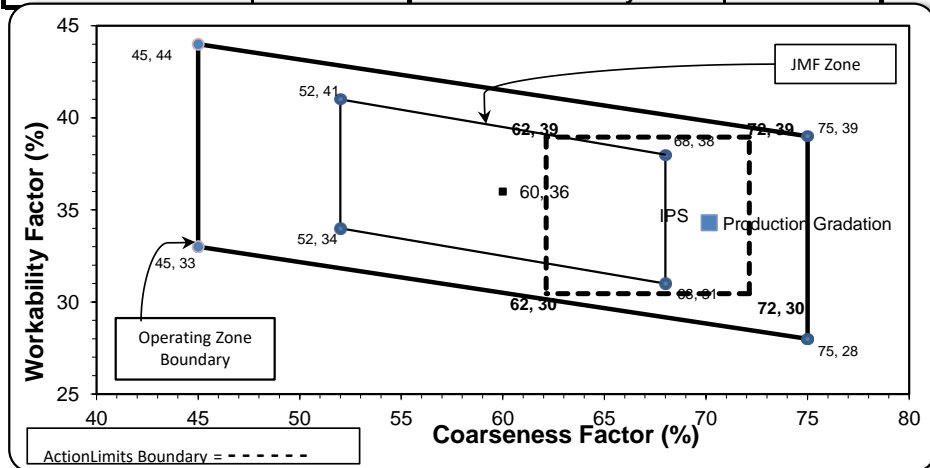

Initial Production Sample (IPS)

**Coarseness Factor:** **67**  
**Workability Factor:** **35**

Sieve	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	0.0	0.0
1.5"	100.0	0.0	0.0
1"	86.9	13.1	13.1
3/4"	76.1	10.8	23.9
1/2"	63.7	12.4	36.3
3/8"	56.2	7.5	43.8
#4	43.2	13.0	56.8
#8	34.7	8.5	65.3
#16	27.5	7.2	72.5
#30	20.6	7.0	79.4
#50	9.0	11.6	91.0
#100	2.1	6.9	97.9
LBW	1.0	1.1	99.0

PREPARED BY:  
 SM, LLC Technical Service

Approved By:

# Aggregate Optimization Chart

**PLANT #:** **P-36**

Sample Date: 8/1/22

Concrete Grade: **P1M, 3500HP**

Dates Test Represents: 8/2/2022 through 8/8/2022

Contractor: \_\_\_\_\_

MDOT No.: \_\_\_\_\_

Agg. Class	Pit #	Source	Weight (SSD)	ft <sup>3</sup>	Specific Gravity	% Contribution
CA	71-47	Presque Isle	900	5.50	2.62	29.3
IA	71-47	Presque Isle	970	5.93	2.62	31.6
2NS	63-92	Grange Hall	1200	7.26	2.65	39.1
<b>Total Wt</b>			<b>3070</b>	<b>18.70</b>		<b>100.0</b>

<----- Verify this number is 100%




**Superior Materials, LLC**  
 30701 W. 10 Mile Rd.  
 Suite 500  
 Farmington Hills, MI 48336

Sieve	CA	IA	2NS	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	100.0	100.0	100.0	0.0	0.0
1.5"	94.5	100.0	100.0	98.4	1.6	1.6
1"	28.8	100.0	100.0	79.1	19.3	20.9
3/4"	6.0	98.5	100.0	72.0	7.2	28.0
1/2"	2.5	80.0	100.0	65.1	6.9	34.9
3/8"	2.0	57.4	100.0	57.8	7.3	42.2
#4	1.7	11.6	94.7	41.2	16.6	58.8
#8	1.6	3.2	83.2	34.0	7.2	66.0
#16	1.5	2.1	68.4	27.8	6.2	72.2
#30	1.4	1.9	49.4	20.3	7.5	79.7
#50	1.4	1.8	19.2	8.5	11.8	91.5
#100	1.2	1.6	3.4	2.2	6.3	97.8
LBW	0.9	1.4	0.4	0.9	1.3	99.1

\*Maximum % Retained must be above the 3/8" sieve.  
 \*Any two adjacent sieves must equal 10% except max., nom. max., #100 and #200 sieves.  
 \*% Retained must be at least 4% for each sieve except max., nom. max., #100 and #200 sieves.  
 \*% Retained must be at least 8% for the 1" sieve when a 2" max. size (nom. Max. 1.5") aggregate is used.

Production Gradation  Batch Plant Gradations  Aggregate Supplier Gradations

<b>Coarseness Factor:</b>	<b>64</b>	<b>Workability Factor:</b>	<b>34</b>
---------------------------	-----------	----------------------------	-----------

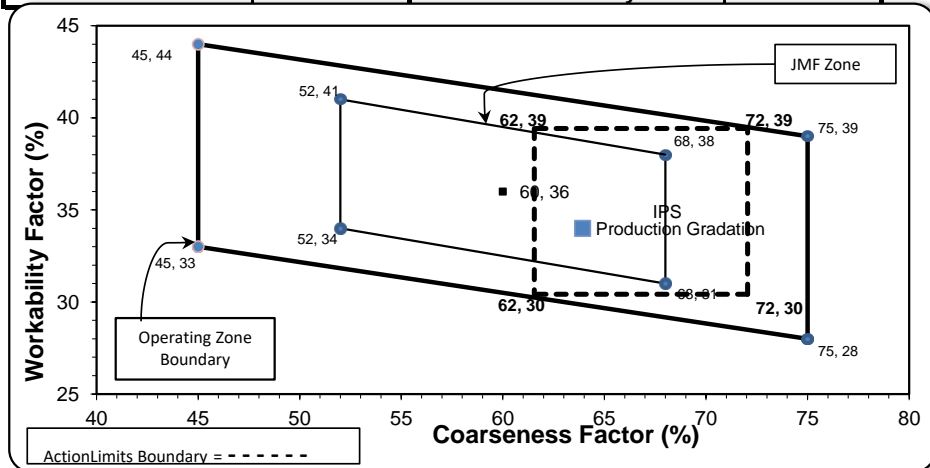

Initial Production Sample (IPS)

<b>Coarseness Factor:</b>	<b>67</b>		
<b>Workability Factor:</b>	<b>35</b>		
Sieve	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	0.0	0.0
1.5"	100.0	0.0	0.0
1"	85.0	15.0	15.0
3/4"	72.1	12.9	27.9
1/2"	64.5	7.6	35.5
3/8"	56.5	8.0	43.5
#4	42.7	13.8	57.3
#8	34.9	7.8	65.1
#16	29.0	5.9	71.0
#30	21.0	8.0	79.0
#50	8.2	12.8	91.8
#100	1.6	6.5	98.4
LBW	0.7	0.9	99.3

PREPARED BY:  
 SM, LLC Technical Service

Approved By:



# Aggregate Optimization Chart

**PLANT #:** **P-39**

Sample Date: 8/1/22

Concrete Grade: **P1M, 3500HP**

Contractor: \_\_\_\_\_

Dates Test Represents: 8/2/2022 through 8/8/2022

MDOT No.: \_\_\_\_\_

Agg. Class	Pit #	Source	Weight (SSD)	ft <sup>3</sup>	Specific Gravity	% Contribution
CA	71-47	Presque Isle	1020	6.24	2.62	33.2
IA	71-47	Presque Isle	800	4.89	2.62	26.1
2NS	44-051	Krake Willis Rd	1250	7.56	2.65	40.7
<b>Total Wt</b>			<b>3070</b>	<b>18.69</b>		<b>100.0</b>

<----- Verify this number is 100%




**Superior Materials, LLC**  
 30701 W. 10 Mile Rd.  
 Suite 500  
 Farmington Hills, MI 48336

Sieve	CA	IA	2NS	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	100.0	100.0	100.0	0.0	0.0
1.5"	97.8	100.0	100.0	99.3	0.7	0.7
1"	47.5	100.0	100.0	82.6	16.7	17.4
3/4"	13.7	98.5	100.0	70.9	11.6	29.1
1/2"	3.8	83.2	100.0	63.7	7.3	36.3
3/8"	2.6	63.7	100.0	58.2	5.5	41.8
#4	2.2	17.3	96.2	44.4	13.8	55.6
#8	2.0	4.5	80.2	34.5	9.9	65.5
#16	1.8	2.7	66.2	28.3	6.2	71.7
#30	1.7	2.3	50.4	21.7	6.6	78.3
#50	1.7	2.1	24.8	11.2	10.5	88.8
#100	1.6	1.9	6.4	3.6	7.6	96.4
LBW	1.4	1.7	0.4	1.1	2.6	98.9

\*Maximum % Retained must be above the 3/8" sieve.  
 \*Any two adjacent sieves must equal 10% except max., nom. max., #100 and #200 sieves.  
 \*% Retained must be at least 4% for each sieve except max., nom. max., #100 and #200 sieves.  
 \*% Retained must be at least 8% for the 1" sieve when a 2" max. size (nom. Max. 1.5") aggregate is used.

Production Gradation  Batch Plant Gradations  Aggregate Supplier Gradations

<b>Coarseness Factor:</b>	<b>64</b>	<b>Workability Factor:</b>	<b>34</b>
---------------------------	-----------	----------------------------	-----------

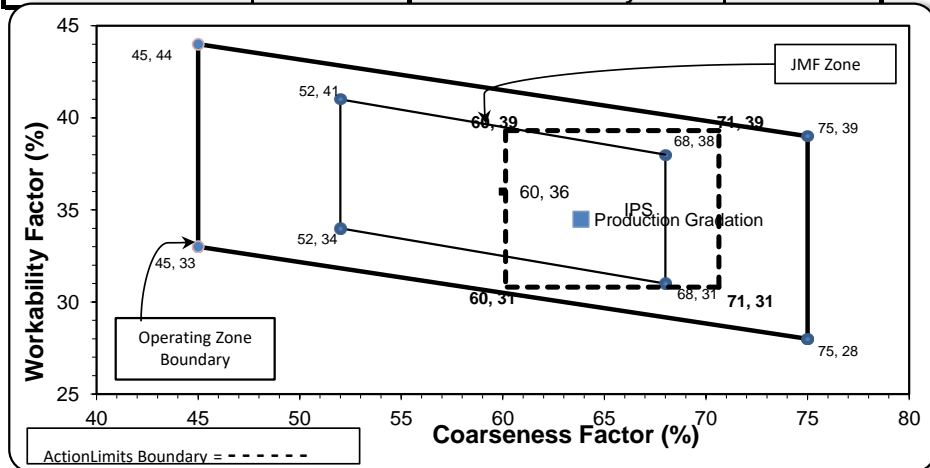

Initial Production Sample (IPS)

<b>Coarseness Factor:</b>	<b>65</b>
<b>Workability Factor:</b>	<b>35</b>

Sieve	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	0.0	0.0
1.5"	99.6	0.4	0.4
1"	83.9	15.7	16.1
3/4"	74.1	9.8	25.9
1/2"	64.3	9.7	35.7
3/8"	57.5	6.8	42.5
#4	44.5	13.1	55.5
#8	35.1	9.4	64.9
#16	27.9	7.2	72.1
#30	21.7	6.2	78.3
#50	12.6	9.1	87.4
#100	3.5	9.1	96.5
LBW	1.2	2.4	98.8

PREPARED BY:  
 SM, LLC Technical Service

Approved By:



# Aggregate Optimization Chart

**PLANT #:** **P-O2**

Sample Date: 8/1/22

Concrete Grade: **P1M, 3500HP**

Contractor: \_\_\_\_\_

Dates Test Represents: 8/2/2022 through 8/8/2022

MDOT No.: \_\_\_\_\_

Agg. Class	Pit #	Source	Weight (SSD)	ft <sup>3</sup>	Specific Gravity	% Contribution
CA	71-47	Presque Isle	950	5.81	2.62	30.9
IA	71-47	Presque Isle	870	5.32	2.62	28.3
2NS	63-115	Ray Rd	1250	7.56	2.65	40.7
<b>Total Wt</b>			<b>3070</b>	<b>18.69</b>		<b>100.0</b>

<----- Verify this number is 100%




**Superior Materials, LLC**  
 30701 W. 10 Mile Rd.  
 Suite 500  
 Farmington Hills, MI 48336

Sieve	CA	IA	2NS	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	100.0	100.0	100.0	0.0	0.0
1.5"	94.5	100.0	100.0	98.3	1.7	1.7
1"	28.8	100.0	100.0	78.0	20.3	22.0
3/4"	6.0	98.5	100.0	70.5	7.5	29.5
1/2"	2.5	80.0	100.0	64.2	6.3	35.8
3/8"	2.0	57.4	100.0	57.6	6.6	42.4
#4	1.7	11.6	96.2	43.0	14.6	57.0
#8	1.6	3.2	76.6	32.6	10.4	67.4
#16	1.5	2.1	59.7	25.4	7.2	74.6
#30	1.4	1.9	43.9	18.8	6.5	81.2
#50	1.4	1.8	25.4	11.3	7.6	88.7
#100	1.2	1.6	7.6	3.9	7.4	96.1
LBW	0.9	1.4	1.5	1.3	2.6	98.7

\*Maximum % Retained must be above the 3/8" sieve.  
 \*Any two adjacent sieves must equal 10% except max., nom. max., #100 and #200 sieves.  
 \*% Retained must be at least 4% for each sieve except max., nom. max., #100 and #200 sieves.  
 \*% Retained must be at least 8% for the 1" sieve when a 2" max. size (nom. Max. 1.5") aggregate is used.

Production Gradation  Batch Plant Gradations  Aggregate Supplier Gradations

**Coarseness Factor:** **63**      **Workability Factor:** **33**

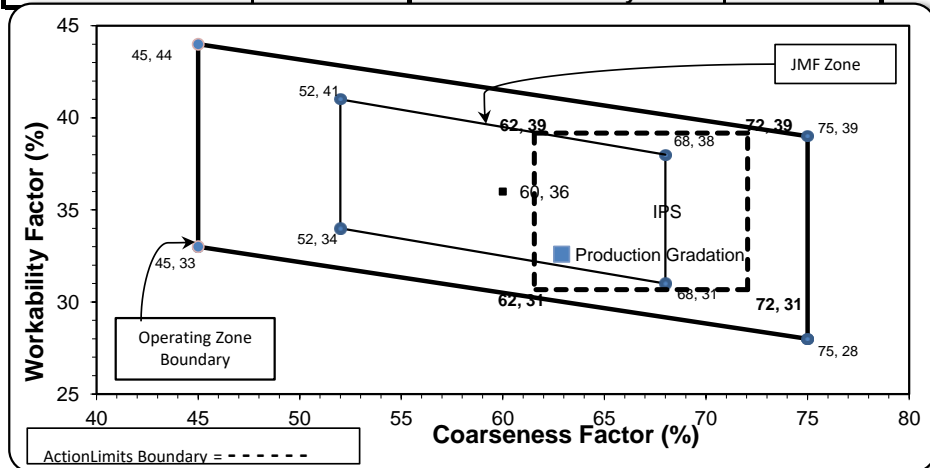

Initial Production Sample (IPS)

**Coarseness Factor:** **67**  
**Workability Factor:** **35**

Sieve	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	0.0	0.0
1.5"	100.0	0.0	0.0
1"	85.0	15.0	15.0
3/4"	72.3	12.7	27.7
1/2"	64.5	7.8	35.5
3/8"	56.5	8.0	43.5
#4	42.7	13.8	57.3
#8	34.9	7.8	65.1
#16	29.0	5.9	71.0
#30	21.0	8.0	79.0
#50	8.2	12.8	91.8
#100	1.6	6.5	98.4
LBW	0.7	0.9	99.3

PREPARED BY:  
 SM, LLC Technical Service

Approved By:
