

Aggregate Optimization Chart

PLANT #: **P-101**

Sample Date: 8/8/22

Concrete Grade: **S2M, 3500HP**

Dates Test Represents: 8/9/2022 through 8/15/2022

Contractor: _____

MDOT No.: _____

Agg. Class	Pit #	Source	Weight (SSD)	ft ³	Specific Gravity	% Contribution
6AA	71-47	Presque Isle	1625	9.94	2.62	53.2
26A	71-47	Presque Isle	200	1.22	2.62	6.5
2NS	75-051	Mid Michigan	1230	7.41	2.66	40.3
Total Wt			3055	18.57		100.0

<---- Verify this number is 100%



Superior Materials, LLC
 30701 W. 10 Mile Rd.
 Suite 500
 Farmington Hills, MI 48336

Sieve	6AA	26A	2NS	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	100.0	100.0	100.0	0.0	0.0
1.5"	100.0	100.0	100.0	100.0	0.0	0.0
1"	98.0	100.0	100.0	98.9	1.1	1.1
3/4"	87.4	100.0	100.0	93.3	5.6	6.7
1/2"	41.8	98.7	100.0	69.0	24.3	31.0
3/8"	21.0	87.9	100.0	57.2	11.8	42.8
#4	2.9	22.1	99.0	42.8	14.3	57.2
#8	1.9	5.2	85.3	35.7	7.2	64.3
#16	1.6	2.9	70.1	29.3	6.4	70.7
#30	1.5	2.4	53.2	22.4	6.9	77.6
#50	1.4	2.1	26.3	11.5	10.9	88.5
#100	1.3	1.9	6.8	3.6	7.9	96.4
LBW	1.2	1.7	1.0	1.2	2.4	98.8

*Maximum % Retained must be above the 3/8" sieve.
 *Any two adjacent sieves must equal 10% except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 4% for each sieve except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 8% for the 1" sieve when a 2" max. size (nom. Max. 1.5") aggregate is used.


Production Gradation Batch Plant Gradations Aggregate Supplier Gradations

Coarseness Factor: **67** **Workability Factor:** **36**

Initial Production Sample (IPS)

Coarseness Factor: **64**

Workability Factor: **35**

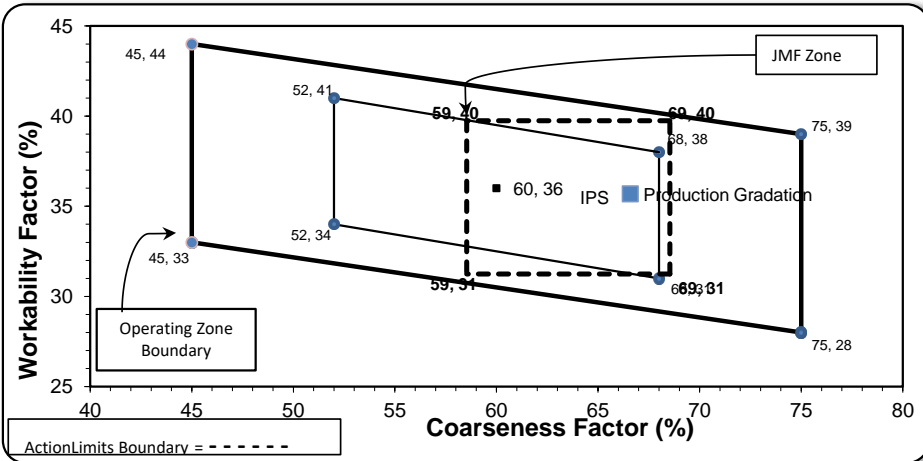

Sieve	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	0.0	0.0
1.5"	100.0	0.0	0.0
1"	100.0	0.0	0.0
3/4"	93.9	6.1	6.1
1/2"	71.4	22.5	28.6
3/8"	59.0	12.4	41.0
#4	45.1	13.9	54.9
#8	35.5	9.6	64.5
#16	28.3	7.2	71.7
#30	21.3	6.9	78.7
#50	11.0	10.3	89.0
#100	3.4	7.6	96.6
LBW	1.1	2.3	98.9

PREPARED BY:
 SM, LLC Technical Service

Approved By:

Aggregate Optimization Chart

PLANT #: **P-102**

Sample Date: 8/8/22

Concrete Grade: **S2M, 3500HP**

Dates Test Represents: 8/9/2022 through 8/15/2022

Contractor: _____

MDOT No.: _____

Agg. Class	Pit #	Source	Weight (SSD)	ft ³	Specific Gravity	% Contribution
6AA	58-003	Stoneco	1600	9.53	2.69	51.6
26A	58-003	Stoneco	300	1.79	2.69	9.7
2NS	81-019	Pleasant Lake	1200	7.26	2.65	38.7
Total Wt			3100	18.58		100.0

<----- Verify this number is 100%




Superior Materials, LLC
 30701 W. 10 Mile Rd.
 Suite 500
 Farmington Hills, MI 48336

Sieve	6AA	26A	2NS	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	100.0	100.0	100.0	0.0	0.0
1.5"	100.0	100.0	100.0	100.0	0.0	0.0
1"	99.8	100.0	100.0	99.9	0.1	0.1
3/4"	80.8	100.0	100.0	90.1	9.8	9.9
1/2"	36.8	99.5	100.0	67.3	22.8	32.7
3/8"	16.1	82.5	100.0	55.0	12.3	45.0
#4	2.9	12.7	99.3	41.2	13.8	58.8
#8	1.4	4.3	84.2	33.7	7.4	66.3
#16	1.2	2.9	66.5	26.6	7.1	73.4
#30	1.0	2.4	48.3	19.4	7.2	80.6
#50	0.9	2.2	25.1	10.4	9.1	89.6
#100	0.9	2.1	7.8	3.7	6.7	96.3
LBW	0.7	1.9	1.4	1.1	2.6	98.9

*Maximum % Retained must be above the 3/8" sieve.
 *Any two adjacent sieves must equal 10% except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 4% for each sieve except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 8% for the 1" sieve when a 2" max. size (nom. Max. 1.5") aggregate is used.

Production Gradation Batch Plant Gradations Aggregate Supplier Gradations

Coarseness Factor:	68	Workability Factor:	34
---------------------------	-----------	----------------------------	-----------

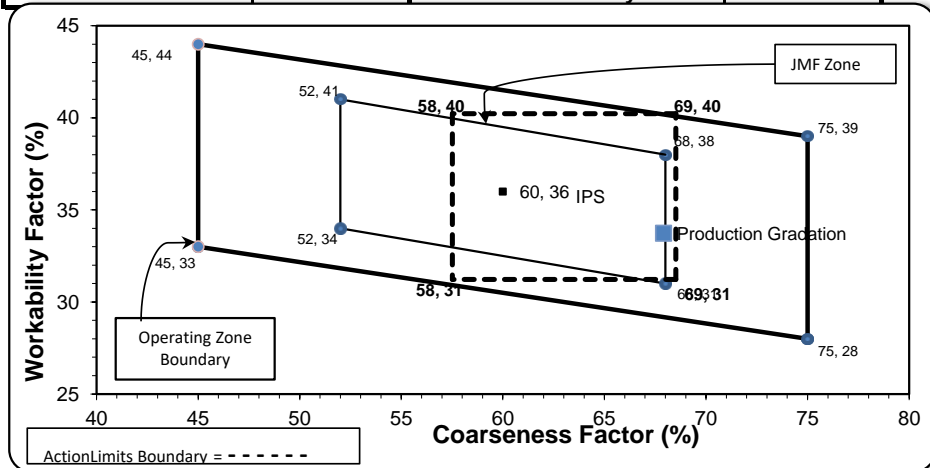

Initial Production Sample (IPS)

Coarseness Factor:	63
Workability Factor:	36

Sieve	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	0.0	0.0
1.5"	100.0	0.0	0.0
1"	99.2	0.8	0.8
3/4"	90.9	8.3	9.1
1/2"	71.3	19.6	28.7
3/8"	59.5	11.8	40.5
#4	43.8	15.7	56.2
#8	35.7	8.1	64.3
#16	27.0	8.7	73.0
#30	18.6	8.4	81.4
#50	6.8	11.8	93.2
#100	1.4	5.4	98.6
LBW	0.6	0.8	99.4

PREPARED BY:
 SM, LLC Technical Service

Approved By:

Aggregate Optimization Chart

PLANT #: **P-103**

Sample Date: 8/8/22

Concrete Grade: **S2M, 3500HP**

Dates Test Represents: 8/9/2022 through 8/15/2022

Contractor: _____

MDOT No.: _____

Agg. Class	Pit #	Source	Weight (SSD)	ft ³	Specific Gravity	% Contribution
6AA	58-003	Stoneco	1600	9.53	2.69	51.6
26A	58-003	Stoneco	300	1.79	2.69	9.7
2NS	81-019	Pleasant Lake	1200	7.26	2.65	38.7
Total Wt			3100	18.58		100.0

<----- Verify this number is 100%




Superior Materials, LLC
 30701 W. 10 Mile Rd.
 Suite 500
 Farmington Hills, MI 48336

Sieve	6AA	26A	2NS	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	100.0	100.0	100.0	0.0	0.0
1.5"	100.0	100.0	100.0	100.0	0.0	0.0
1"	99.8	100.0	100.0	99.9	0.1	0.1
3/4"	80.8	100.0	100.0	90.1	9.8	9.9
1/2"	36.8	99.5	100.0	67.3	22.8	32.7
3/8"	16.1	82.5	100.0	55.0	12.3	45.0
#4	2.9	12.7	99.3	41.2	13.8	58.8
#8	1.4	4.3	84.2	33.7	7.4	66.3
#16	1.2	2.9	66.5	26.6	7.1	73.4
#30	1.0	2.4	48.3	19.4	7.2	80.6
#50	0.9	2.2	25.1	10.4	9.1	89.6
#100	0.9	2.1	7.8	3.7	6.7	96.3
LBW	0.7	1.9	1.4	1.1	2.6	98.9

*Maximum % Retained must be above the 3/8" sieve.
 *Any two adjacent sieves must equal 10% except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 4% for each sieve except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 8% for the 1" sieve when a 2" max. size (nom. Max. 1.5") aggregate is used.

Production Gradation Batch Plant Gradations Aggregate Supplier Gradations

Coarseness Factor:	68	Workability Factor:	34
---------------------------	-----------	----------------------------	-----------

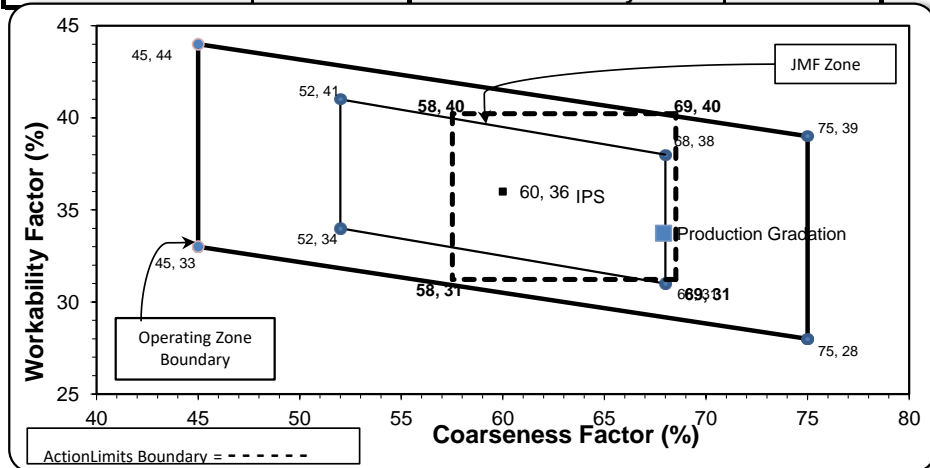

Initial Production Sample (IPS)

Coarseness Factor:	63		
Workability Factor:	36		
Sieve	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	0.0	0.0
1.5"	100.0	0.0	0.0
1"	99.2	0.8	0.8
3/4"	90.9	8.3	9.1
1/2"	71.3	19.6	28.7
3/8"	59.5	11.8	40.5
#4	43.8	15.7	56.2
#8	35.7	8.1	64.3
#16	27.0	8.7	73.0
#30	18.6	8.4	81.4
#50	6.8	11.8	93.2
#100	1.4	5.4	98.6
LBW	0.6	0.8	99.4

PREPARED BY:
 SM, LLC Technical Service

Approved BY:

Aggregate Optimization Chart

PLANT #: **P-32**

Sample Date: 8/8/22

Concrete Grade: **S2M, 3500HP**

Dates Test Represents: 8/9/2022 through 8/15/2022

Contractor: _____

MDOT No.: _____

Agg. Class	Pit #	Source	Weight (SSD)	ft ³	Specific Gravity	% Contribution
6AA	71-47	Presque Isle	1620	9.91	2.62	53.1
26A	71-47	Presque Isle	200	1.22	2.62	6.6
2NS	95-013	Smelter Bay	1230	7.44	2.65	40.3
Total Wt			3050	18.57		100.0

<----- Verify this number is 100%




Superior Materials, LLC
 30701 W. 10 Mile Rd.
 Suite 500
 Farmington Hills, MI 48336

Sieve	6AA	26A	2NS	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	100.0	100.0	100.0	0.0	0.0
1.5"	100.0	100.0	100.0	100.0	0.0	0.0
1"	100.0	100.0	100.0	100.0	0.0	0.0
3/4"	80.2	100.0	100.0	89.5	10.5	10.5
1/2"	43.6	96.8	100.0	69.8	19.6	30.2
3/8"	24.9	86.1	100.0	59.2	10.6	40.8
#4	4.4	27.7	96.8	43.2	16.0	56.8
#8	2.0	8.2	84.7	35.8	7.4	64.2
#16	1.8	3.8	69.2	29.1	6.6	70.9
#30	1.7	2.8	49.9	21.2	7.9	78.8
#50	1.6	2.5	24.5	10.9	10.3	89.1
#100	1.6	2.3	7.4	4.0	6.9	96.0
LBW	1.3	1.9	1.6	1.5	2.5	98.5

*Maximum % Retained must be above the 3/8" sieve.
 *Any two adjacent sieves must equal 10% except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 4% for each sieve except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 8% for the 1" sieve when a 2" max. size (nom. Max. 1.5") aggregate is used.

Production Gradation Batch Plant Gradations Aggregate Supplier Gradations

Coarseness Factor: **64** **Workability Factor:** **36**

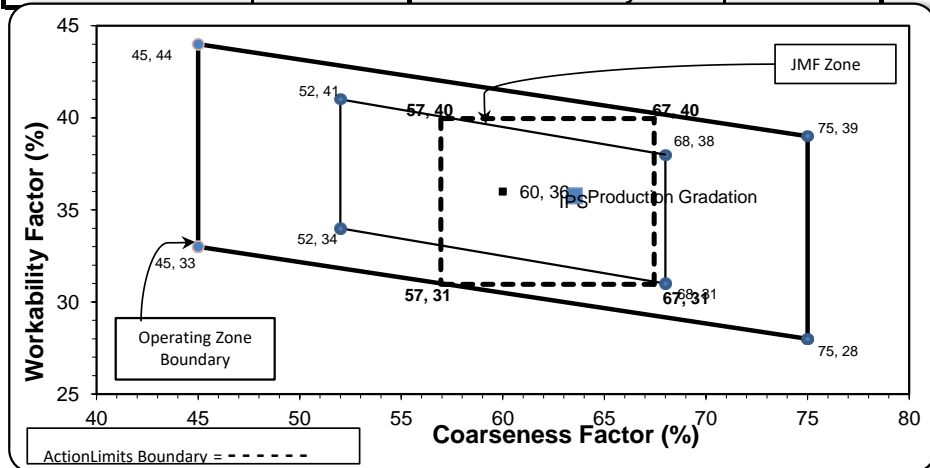

Initial Production Sample (IPS)

Coarseness Factor: **62**
Workability Factor: **35**

Sieve	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	0.0	0.0
1.5"	100.0	0.0	0.0
1"	100.0	0.0	0.0
3/4"	94.0	6.0	6.0
1/2"	70.2	23.7	29.8
3/8"	59.9	10.4	40.1
#4	42.7	17.2	57.3
#8	35.5	7.2	64.5
#16	28.4	7.0	71.6
#30	19.2	9.2	80.8
#50	8.9	10.3	91.1
#100	3.1	5.9	96.9
LBW	1.4	1.7	98.6

PREPARED BY:
 SM, LLC Technical Service

Approved By:

Aggregate Optimization Chart

PLANT #: **P-35**

Sample Date: 8/8/22

Concrete Grade: **S2M, 3500HP**

Dates Test Represents: 8/9/2022 through 8/15/2022

Contractor: _____

MDOT No.: _____

Agg. Class	Pit #	Source	Weight (SSD)	ft ³	Specific Gravity	% Contribution
6AA	58-003	Stoneco	1600	9.53	2.69	51.6
26A	58-003	Stoneco	300	1.79	2.69	9.7
2NS	81-019	Pleasant Lake	1200	7.26	2.65	38.7
Total Wt			3100	18.58		100.0

<----- Verify this number is 100%




Superior Materials, LLC
 30701 W. 10 Mile Rd.
 Suite 500
 Farmington Hills, MI 48336

Sieve	6AA	26A	2NS	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	100.0	100.0	100.0	0.0	0.0
1.5"	100.0	100.0	100.0	100.0	0.0	0.0
1"	99.8	100.0	100.0	99.9	0.1	0.1
3/4"	80.8	100.0	100.0	90.1	9.8	9.9
1/2"	36.8	99.5	100.0	67.3	22.8	32.7
3/8"	16.1	82.5	100.0	55.0	12.3	45.0
#4	2.9	12.7	99.3	41.2	13.8	58.8
#8	1.4	4.3	84.2	33.7	7.4	66.3
#16	1.2	2.9	66.5	26.6	7.1	73.4
#30	1.0	2.4	48.3	19.4	7.2	80.6
#50	0.9	2.2	25.1	10.4	9.1	89.6
#100	0.9	2.1	7.8	3.7	6.7	96.3
LBW	0.7	1.9	1.4	1.1	2.6	98.9

*Maximum % Retained must be above the 3/8" sieve.
 *Any two adjacent sieves must equal 10% except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 4% for each sieve except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 8% for the 1" sieve when a 2" max. size (nom. Max. 1.5") aggregate is used.

Production Gradation Batch Plant Gradations Aggregate Supplier Gradations

Coarseness Factor:	68	Workability Factor:	34
---------------------------	-----------	----------------------------	-----------

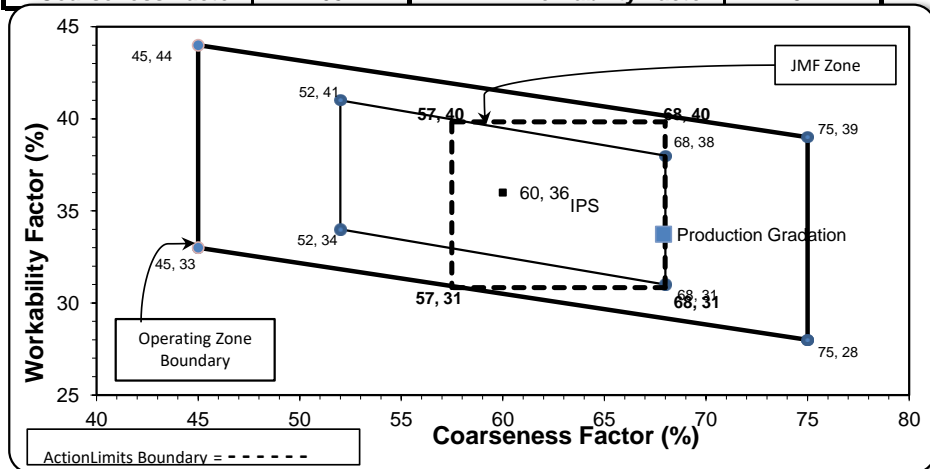

Intial Production Sample (IPS)

Coarseness Factor:	63		
Workability Factor:	35		
Sieve	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	0.0	0.0
1.5"	100.0	0.0	0.0
1"	99.2	0.8	0.8
3/4"	90.9	8.3	9.1
1/2"	71.3	19.6	28.7
3/8"	59.4	11.9	40.6
#4	43.0	16.5	57.0
#8	35.3	7.6	64.7
#16	28.2	7.1	71.8
#30	21.6	6.6	78.4
#50	9.1	12.5	90.9
#100	1.7	7.4	98.3
LBW	1.1	0.6	98.9

PREPARED BY:
 SM, LLC Technical Service

Approved By:

Aggregate Optimization Chart

PLANT #: **P-36**

Sample Date: 8/8/22

Concrete Grade: **S2M, 3500HP**

Contractor: _____

Dates Test Represents: 8/9/2022 through 8/15/2022

MDOT No.: _____

Agg. Class	Pit #	Source	Weight (SSD)	ft ³	Specific Gravity	% Contribution
6AA	71-47	Presque Isle	1550	9.48	2.62	50.8
26A	71-47	Presque Isle	300	1.83	2.62	9.8
2NS	63-92	Grange Hall	1200	7.26	2.65	39.3
Total Wt			3050	18.57		100.0

<----- Verify this number is 100%




Superior Materials, LLC
 30701 W. 10 Mile Rd.
 Suite 500
 Farmington Hills, MI 48336

Sieve	6AA	26A	2NS	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	100.0	100.0	100.0	0.0	0.0
1.5"	100.0	100.0	100.0	100.0	0.0	0.0
1"	94.8	100.0	100.0	97.4	2.6	2.6
3/4"	71.3	100.0	100.0	85.4	11.9	14.6
1/2"	33.8	96.8	100.0	66.0	19.4	34.0
3/8"	16.5	86.1	100.0	56.2	9.8	43.8
#4	3.9	27.7	97.5	43.1	13.1	56.9
#8	2.6	8.2	82.1	34.4	8.6	65.6
#16	2.1	3.8	67.4	28.0	6.5	72.0
#30	1.8	2.8	49.3	20.6	7.4	79.4
#50	1.7	2.5	21.5	9.6	11.0	90.4
#100	1.5	2.3	3.8	2.5	7.1	97.5
LBW	1.2	1.9	0.8	1.1	1.4	98.9

*Maximum % Retained must be above the 3/8" sieve.
 *Any two adjacent sieves must equal 10% except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 4% for each sieve except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 8% for the 1" sieve when a 2" max. size (nom. Max. 1.5") aggregate is used.

Production Gradation Batch Plant Gradations Aggregate Supplier Gradations

Coarseness Factor: **67** **Workability Factor:** **34**

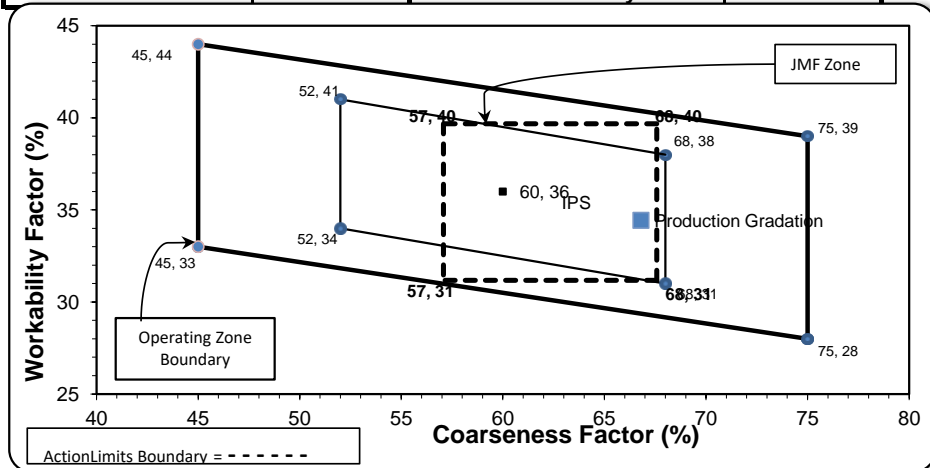

Initial Production Sample (IPS)

Coarseness Factor: **62**
Workability Factor: **35**

Sieve	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	0.0	0.0
1.5"	100.0	0.0	0.0
1"	99.1	0.9	0.9
3/4"	90.5	8.6	9.5
1/2"	69.8	20.7	30.2
3/8"	59.8	10.0	40.2
#4	42.2	17.6	57.8
#8	35.4	6.7	64.6
#16	28.8	6.7	71.2
#30	21.4	7.4	78.6
#50	8.8	12.6	91.2
#100	1.8	7.0	98.2
LBW	0.7	1.0	99.3

PREPARED BY:
 SM, LLC Technical Service

Approved By:

Aggregate Optimization Chart

PLANT #: **P-39**

Sample Date: 8/8/22

Concrete Grade: **S2M, 3500HP**

Contractor: _____

Dates Test Represents: 8/9/2022 through 8/15/2022

MDOT No.: _____

Agg. Class	Pit #	Source	Weight (SSD)	ft ³	Specific Gravity	% Contribution
6AA	71-47	Presque Isle	1600	9.79	2.62	52.5
26A	71-47	Presque Isle	200	1.22	2.62	6.6
2NS	44-051	Krake Willis Rd	1250	7.56	2.65	41.0
Total Wt			3050	18.57		100.0

<----- Verify this number is 100%




Superior Materials, LLC
 30701 W. 10 Mile Rd.
 Suite 500
 Farmington Hills, MI 48336

Sieve	6AA	26A	2NS	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	100.0	100.0	100.0	0.0	0.0
1.5"	100.0	100.0	100.0	100.0	0.0	0.0
1"	98.0	100.0	100.0	99.0	1.0	1.0
3/4"	87.4	100.0	100.0	93.4	5.6	6.6
1/2"	41.8	98.7	100.0	69.4	24.0	30.6
3/8"	21.0	87.9	100.0	57.8	11.6	42.2
#4	2.9	22.1	96.2	42.4	15.4	57.6
#8	1.9	5.2	80.2	34.2	8.2	65.8
#16	1.6	2.9	66.2	28.2	6.0	71.8
#30	1.5	2.4	50.4	21.6	6.6	78.4
#50	1.4	2.1	24.8	11.0	10.6	89.0
#100	1.3	1.9	6.4	3.4	7.6	96.6
LBW	1.2	1.7	0.4	0.9	2.5	99.1

*Maximum % Retained must be above the 3/8" sieve.
 *Any two adjacent sieves must equal 10% except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 4% for each sieve except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 8% for the 1" sieve when a 2" max. size (nom. Max. 1.5") aggregate is used.

Production Gradation Batch Plant Gradations Aggregate Supplier Gradations

Coarseness Factor:	64	Workability Factor:	34
---------------------------	-----------	----------------------------	-----------

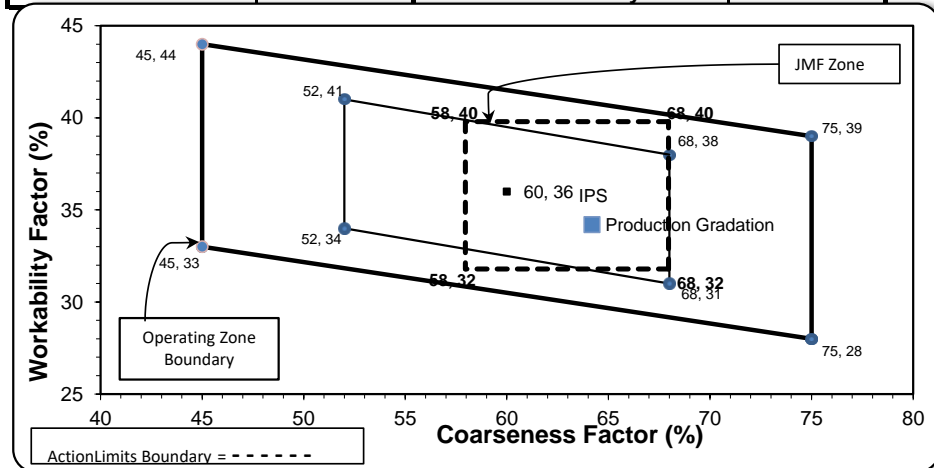

Initial Production Sample (IPS)

Coarseness Factor:	63		
Workability Factor:	36		
Sieve	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	0.0	0.0
1.5"	100.0	0.0	0.0
1"	100.0	0.0	0.0
3/4"	89.8	10.2	10.2
1/2"	70.7	19.1	29.3
3/8"	59.6	11.1	40.4
#4	43.2	16.4	56.8
#8	35.8	7.4	64.2
#16	29.2	6.6	70.8
#30	21.4	7.8	78.6
#50	9.8	11.6	90.2
#100	3.7	6.1	96.3
LBW	1.2	2.5	98.8

PREPARED BY:
 SM, LLC Technical Service

Approved By:

Aggregate Optimization Chart

PLANT #: **P-O2**

Sample Date: 8/8/22

Concrete Grade: **S2M, 3500HP**

Dates Test Represents: 8/9/2022 through 8/15/2022

Contractor: _____

MDOT No.: _____

Agg. Class	Pit #	Source	Weight (SSD)	ft ³	Specific Gravity	% Contribution
6AA	71-47	Presque Isle	1600	9.79	2.62	52.5
26A	71-47	Presque Isle	220	1.35	2.62	7.2
2NS	63-115	Ray Rd	1230	7.44	2.65	40.3
Total Wt			3050	18.57		100.0

<----- Verify this number is 100%




Superior Materials, LLC
 30701 W. 10 Mile Rd.
 Suite 500
 Farmington Hills, MI 48336

Sieve	6AA	26A	2NS	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	100.0	100.0	100.0	0.0	0.0
1.5"	100.0	100.0	100.0	100.0	0.0	0.0
1"	94.8	100.0	100.0	97.3	2.7	2.7
3/4"	71.3	100.0	100.0	84.9	12.3	15.1
1/2"	33.8	96.8	100.0	65.0	19.9	35.0
3/8"	16.5	86.1	100.0	55.2	9.8	44.8
#4	3.9	27.7	96.0	42.8	12.4	57.2
#8	2.6	8.2	77.5	33.2	9.5	66.8
#16	2.1	3.8	61.4	26.1	7.1	73.9
#30	1.8	2.8	46.2	19.8	6.4	80.2
#50	1.7	2.5	27.0	12.0	7.8	88.0
#100	1.5	2.3	7.2	3.9	8.1	96.1
LBW	1.2	1.9	1.0	1.2	2.7	98.8

*Maximum % Retained must be above the 3/8" sieve.
 *Any two adjacent sieves must equal 10% except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 4% for each sieve except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 8% for the 1" sieve when a 2" max. size (nom. Max. 1.5") aggregate is used.

Production Gradation Batch Plant Gradations Aggregate Supplier Gradations

Coarseness Factor: **67** Workability Factor: **33**

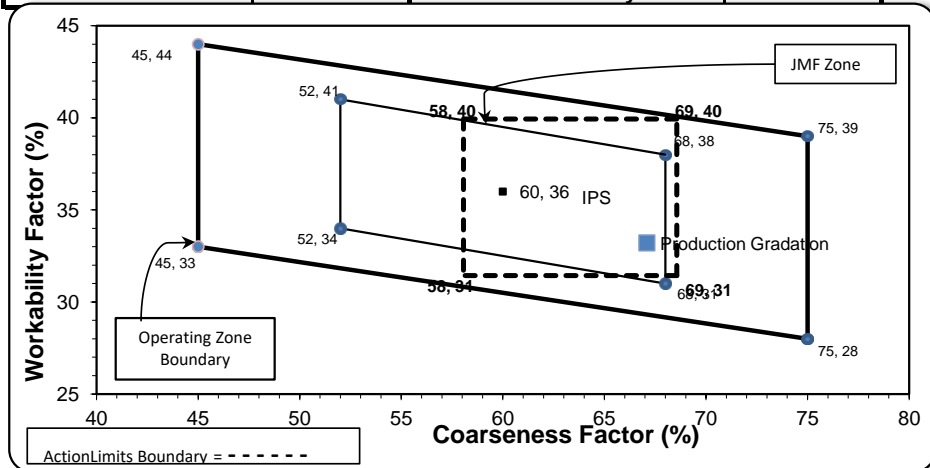

Initial Production Sample (IPS)

Coarseness Factor: 63		Workability Factor: 36	
Sieve	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	0.0	0.0
1.5"	100.0	0.0	0.0
1"	100.0	0.0	0.0
3/4"	95.6	4.4	4.4
1/2"	73.1	22.6	26.9
3/8"	59.3	13.8	40.7
#4	42.8	16.5	57.2
#8	35.7	7.1	64.3
#16	28.9	6.8	71.1
#30	20.7	8.2	79.3
#50	9.9	10.8	90.1
#100	2.1	7.8	97.9
LBW	0.9	1.2	99.1

PREPARED BY:
 SM, LLC Technical Service

Approved By:
