

Aggregate Optimization Chart

PLANT #: **P-102**

Sample Date: 12/11/23

Concrete Grade: **S2M, 3500HP**

Dates Test Represents: 12/12/2023 through 12/18/2023

Contractor: _____

MDOT No.: _____

Agg. Class	Pit #	Source	Weight (SSD)	ft ³	Specific Gravity	% Contribution
6AA	58-003	Stoneco	1550	9.23	2.69	50.0
26A	58-003	Stoneco	350	2.09	2.69	11.3
2NS	81-019	Pleasant Lake	1200	7.26	2.65	38.7
Total Wt			3100	18.58		100.0

<----- Verify this number is 100%




Superior Materials, LLC
 30701 W. 10 Mile Rd.
 Suite 500
 Farmington Hills, MI 48336

Sieve	6AA	26A	2NS	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	100.0	100.0	100.0	0.0	0.0
1.5"	100.0	100.0	100.0	100.0	0.0	0.0
1"	100.0	100.0	100.0	100.0	0.0	0.0
3/4"	82.6	100.0	100.0	91.3	8.7	8.7
1/2"	39.9	98.5	100.0	69.8	21.5	30.2
3/8"	14.9	86.7	100.0	55.9	13.8	44.1
#4	2.7	13.3	98.8	41.1	14.9	58.9
#8	1.6	4.2	86.6	34.8	6.3	65.2
#16	1.5	2.7	67.7	27.3	7.5	72.7
#30	1.4	2.2	44.0	18.0	9.3	82.0
#50	1.3	2.0	14.6	6.5	11.5	93.5
#100	1.2	1.8	1.8	1.5	5.0	98.5
LBW	0.9	1.7	0.4	0.8	0.7	99.2

*Maximum % Retained must be above the 3/8" sieve.
 *Any two adjacent sieves must equal 10% except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 4% for each sieve except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 4% for the 3/4" sieve when a 1.5" max. size (nom. Max. 1.0") aggregate is used.

Production Gradation Batch Plant Gradations Aggregate Supplier Gradations

Coarseness Factor: **68** **Workability Factor:** **35**

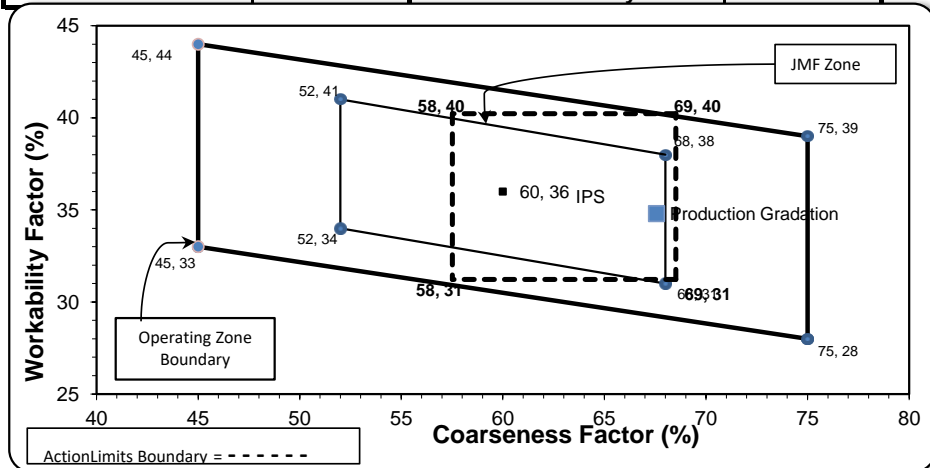

Initial Production Sample (IPS)

Coarseness Factor: **63**
Workability Factor: **36**

Sieve	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	0.0	0.0
1.5"	100.0	0.0	0.0
1"	99.2	0.8	0.8
3/4"	90.9	8.3	9.1
1/2"	71.3	19.6	28.7
3/8"	59.5	11.8	40.5
#4	43.8	15.7	56.2
#8	35.7	8.1	64.3
#16	27.0	8.7	73.0
#30	18.6	8.4	81.4
#50	6.8	11.8	93.2
#100	1.4	5.4	98.6
LBW	0.6	0.8	99.4

PREPARED BY:
 SM, LLC Technical Service

Approved By:

Aggregate Optimization Chart

PLANT #: 12

Sample Date: 12/11/23

Concrete Grade: **S2M, 3500HP**

Dates Test Represents: 12/12/2023 through 12/18/2023

Contractor: _____

MDOT No.: _____

Agg. Class	Pit #	Source	Weight (SSD)	ft ³	Specific Gravity	% Contribution
6AA	71-47	Presque Isle	1550	9.48	2.62	50.8
26A	71-47	Presque Isle	270	1.65	2.62	8.9
2NS	63-115	Ray Rd	1230	7.44	2.65	40.3
Total Wt			3050	18.57		100.0

<----- Verify this number is 100%




Superior Materials, LLC
 30701 W. 10 Mile Rd.
 Suite 500
 Farmington Hills, MI 48336

Sieve	6AA	26A	2NS	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	100.0	100.0	100.0	0.0	0.0
1.5"	100.0	100.0	100.0	100.0	0.0	0.0
1"	98.9	100.0	100.0	99.4	0.6	0.6
3/4"	72.8	100.0	100.0	86.2	13.3	13.8
1/2"	29.1	96.3	100.0	63.6	22.5	36.4
3/8"	15.8	85.4	100.0	55.9	7.7	44.1
#4	2.6	20.6	96.7	42.1	13.8	57.9
#8	1.4	4.0	81.2	33.8	8.3	66.2
#16	1.2	1.8	64.8	26.9	6.9	73.1
#30	1.1	1.5	48.8	20.4	6.5	79.6
#50	1.1	1.4	26.2	11.2	9.1	88.8
#100	1.0	1.3	5.6	2.9	8.4	97.1
LBW	0.9	1.2	1.1	1.0	1.9	99.0

*Maximum % Retained must be above the 3/8" sieve.
 *Any two adjacent sieves must equal 10% except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 4% for each sieve except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 4% for the 3/4" sieve when a 1.5" max. size (nom. Max. 1.0") aggregate is used.

Production Gradation Batch Plant Gradations Aggregate Supplier Gradations

Coarseness Factor: 67 **Workability Factor:** 34

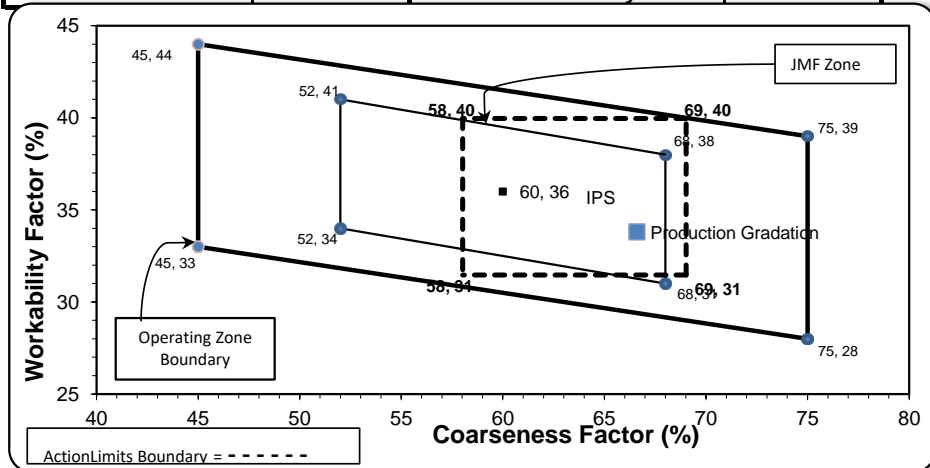

Intial Production Sample (IPS)

Coarseness Factor: 64
Workability Factor: 36

Sieve	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	0.0	0.0
1.5"	100.0	0.0	0.0
1"	99.2	0.8	0.8
3/4"	90.9	8.3	9.1
1/2"	71.3	19.6	28.7
3/8"	59.2	12.1	40.8
#4	41.5	17.7	58.5
#8	35.7	5.8	64.3
#16	27.9	7.9	72.1
#30	18.3	9.5	81.7
#50	7.3	11.0	92.7
#100	2.0	5.3	98.0
LBW	0.9	1.1	99.1

PREPARED BY:
 SM, LLC Technical Service

Approved By:

Aggregate Optimization Chart

PLANT #: p11

Sample Date: 12/11/23

Concrete Grade: **S2M, 3500HP**

Dates Test Represents: 12/12/2023 through 12/18/2023

Contractor: _____

MDOT No.: _____

Agg. Class	Pit #	Source	Weight (SSD)	ft ³	Specific Gravity	% Contribution
6AA	71-47	Presque Isle	1670	10.21	2.62	54.8
26A	71-47	Presque Isle	150	0.92	2.62	4.9
2NS	95-013	Smelter Bay	1230	7.44	2.65	40.3
Total Wt			3050	18.57		100.0

<----- Verify this number is 100%




Superior Materials, LLC
 30701 W. 10 Mile Rd.
 Suite 500
 Farmington Hills, MI 48336

Sieve	6AA	26A	2NS	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	100.0	100.0	100.0	0.0	0.0
1.5"	100.0	100.0	100.0	100.0	0.0	0.0
1"	100.0	100.0	100.0	100.0	0.0	0.0
3/4"	80.7	100.0	100.0	89.4	10.6	10.6
1/2"	44.9	96.3	100.0	69.6	19.8	30.4
3/8"	25.5	85.4	100.0	58.5	11.2	41.5
#4	4.3	20.6	96.3	42.2	16.3	57.8
#8	2.6	4.0	85.5	36.1	6.1	63.9
#16	2.3	1.8	70.7	29.9	6.2	70.1
#30	2.2	1.5	50.6	21.7	8.2	78.3
#50	2.1	1.4	23.7	10.8	10.9	89.2
#100	2.0	1.3	7.2	4.1	6.7	95.9
LBW	1.7	1.2	1.5	1.6	2.5	98.4

*Maximum % Retained must be above the 3/8" sieve.
 *Any two adjacent sieves must equal 10% except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 4% for each sieve except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 4% for the 3/4" sieve when a 1.5" max. size (nom. Max. 1.0") aggregate is used.

Production Gradation Batch Plant Gradations Aggregate Supplier Gradations

Coarseness Factor: 65 **Workability Factor:** 36

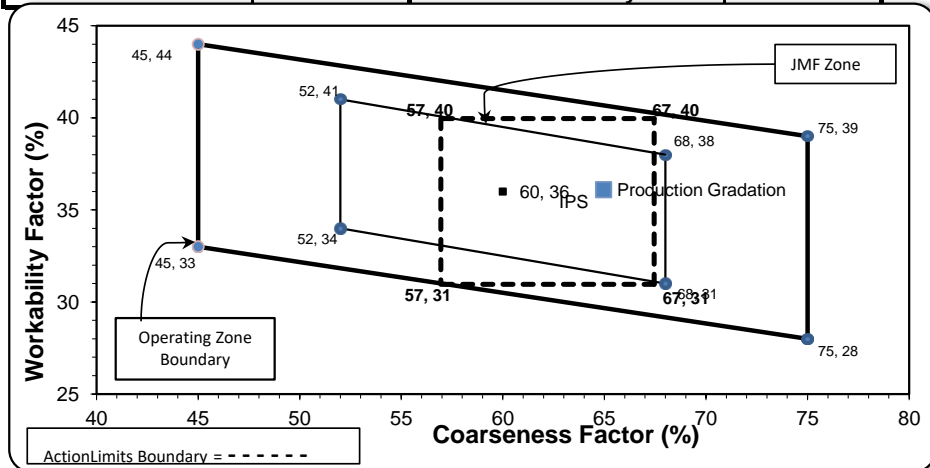

Initial Production Sample (IPS)

Coarseness Factor: 62
Workability Factor: 35

Sieve	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	0.0	0.0
1.5"	100.0	0.0	0.0
1"	100.0	0.0	0.0
3/4"	94.0	6.0	6.0
1/2"	70.2	23.7	29.8
3/8"	59.9	10.4	40.1
#4	42.7	17.2	57.3
#8	35.5	7.2	64.5
#16	28.4	7.0	71.6
#30	19.2	9.2	80.8
#50	8.9	10.3	91.1
#100	3.1	5.9	96.9
LBW	1.4	1.7	98.6

PREPARED BY:
 SM, LLC Technical Service

Approved By:

Aggregate Optimization Chart

PLANT #: **P-35**

Sample Date: 12/11/23

Concrete Grade: **S2M, 3500HP**

Dates Test Represents: 12/12/2023 through 12/18/2023

Contractor: _____

MDOT No.: _____

Agg. Class	Pit #	Source	Weight (SSD)	ft ³	Specific Gravity	% Contribution
6AA	58-003	Stoneco	1550	9.23	2.69	50.0
26A	58-003	Stoneco	350	2.09	2.69	11.3
2NS	81-019	Pleasant Lake	1200	7.26	2.65	38.7
Total Wt			3100	18.58		100.0

<----- Verify this number is 100%




Superior Materials, LLC
 30701 W. 10 Mile Rd.
 Suite 500
 Farmington Hills, MI 48336

Sieve	6AA	26A	2NS	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	100.0	100.0	100.0	0.0	0.0
1.5"	100.0	100.0	100.0	100.0	0.0	0.0
1"	100.0	100.0	100.0	100.0	0.0	0.0
3/4"	82.6	100.0	100.0	91.3	8.7	8.7
1/2"	39.9	98.5	100.0	69.8	21.5	30.2
3/8"	14.9	86.7	100.0	55.9	13.8	44.1
#4	2.7	13.3	98.8	41.1	14.9	58.9
#8	1.6	4.2	86.6	34.8	6.3	65.2
#16	1.5	2.7	67.7	27.3	7.5	72.7
#30	1.4	2.2	44.0	18.0	9.3	82.0
#50	1.3	2.0	14.6	6.5	11.5	93.5
#100	1.2	1.8	1.8	1.5	5.0	98.5
LBW	0.9	1.7	0.4	0.8	0.7	99.2

*Maximum % Retained must be above the 3/8" sieve.
 *Any two adjacent sieves must equal 10% except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 4% for each sieve except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 4% for the 3/4" sieve when a 1.5" max. size (nom. Max. 1.0") aggregate is used.

Production Gradation Batch Plant Gradations Aggregate Supplier Gradations

Coarseness Factor:	68	Workability Factor:	35
---------------------------	-----------	----------------------------	-----------

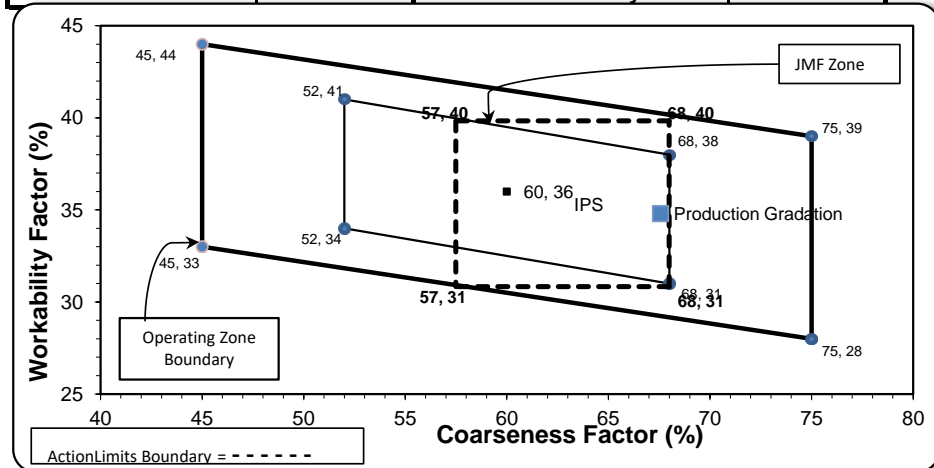

Intial Production Sample (IPS)

Coarseness Factor:	63		
Workability Factor:	35		
Sieve	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	0.0	0.0
1.5"	100.0	0.0	0.0
1"	99.2	0.8	0.8
3/4"	90.9	8.3	9.1
1/2"	71.3	19.6	28.7
3/8"	59.4	11.9	40.6
#4	43.0	16.5	57.0
#8	35.3	7.6	64.7
#16	28.2	7.1	71.8
#30	21.6	6.6	78.4
#50	9.1	12.5	90.9
#100	1.7	7.4	98.3
LBW	1.1	0.6	98.9

PREPARED BY:
 SM, LLC Technical Service

Approved By:

Aggregate Optimization Chart

PLANT #: **P-36**

Sample Date: 12/11/23

Concrete Grade: **S2M, 3500HP**

Dates Test Represents: 12/12/2023 through 12/18/2023

Contractor: _____

MDOT No.: _____

Agg. Class	Pit #	Source	Weight (SSD)	ft ³	Specific Gravity	% Contribution
6AA	71-47	Presque Isle	1500	9.17	2.62	49.2
26A	71-47	Presque Isle	350	2.14	2.62	11.5
2NS	63-92	Grange Hall	1200	7.26	2.65	39.3
Total Wt			3050	18.57		100.0

<----- Verify this number is 100%




Superior Materials, LLC
 30701 W. 10 Mile Rd.
 Suite 500
 Farmington Hills, MI 48336

Sieve	6AA	26A	2NS	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	100.0	100.0	100.0	0.0	0.0
1.5"	100.0	100.0	100.0	100.0	0.0	0.0
1"	98.9	100.0	100.0	99.5	0.5	0.5
3/4"	72.8	100.0	100.0	86.6	12.8	13.4
1/2"	29.1	96.3	100.0	64.7	21.9	35.3
3/8"	15.8	85.4	100.0	56.9	7.8	43.1
#4	2.6	20.6	97.2	41.9	15.0	58.1
#8	1.4	4.0	83.8	34.1	7.8	65.9
#16	1.2	1.8	69.2	28.0	6.1	72.0
#30	1.1	1.5	50.8	20.7	7.3	79.3
#50	1.1	1.4	20.2	8.6	12.1	91.4
#100	1.0	1.3	2.6	1.7	7.0	98.3
LBW	0.9	1.2	0.5	0.8	0.9	99.2

*Maximum % Retained must be above the 3/8" sieve.
 *Any two adjacent sieves must equal 10% except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 4% for each sieve except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 4% for the 3/4" sieve when a 1.5" max. size (nom. Max. 1.0") aggregate is used.

Production Gradation Batch Plant Gradations Aggregate Supplier Gradations

Coarseness Factor: 65 **Workability Factor:** 34

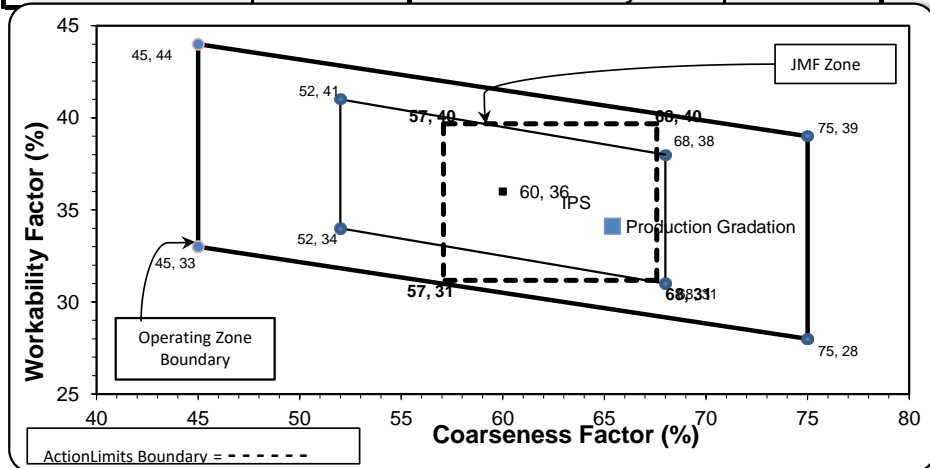

Initial Production Sample (IPS)

Coarseness Factor: 62
Workability Factor: 35

Sieve	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	0.0	0.0
1.5"	100.0	0.0	0.0
1"	99.1	0.9	0.9
3/4"	90.5	8.6	9.5
1/2"	69.8	20.7	30.2
3/8"	59.8	10.0	40.2
#4	42.2	17.6	57.8
#8	35.4	6.7	64.6
#16	28.8	6.7	71.2
#30	21.4	7.4	78.6
#50	8.8	12.6	91.2
#100	1.8	7.0	98.2
LBW	0.7	1.0	99.3

PREPARED BY:
 SM, LLC Technical Service

Approved By:

Aggregate Optimization Chart

PLANT #: P-02

Sample Date: 12/11/23

Concrete Grade: S2M, 3500HP

Dates Test Represents: 12/12/2023 through 12/18/2023

Contractor: _____

MDOT No.: _____

Agg. Class	Pit #	Source	Weight (SSD)	ft ³	Specific Gravity	% Contribution
6AA	71-47	Presque Isle	1550	9.48	2.62	50.8
26A	71-47	Presque Isle	270	1.65	2.62	8.9
2NS	63-115	Ray Rd	1230	7.44	2.65	40.3
Total Wt			3050	18.57		100.0

<----- Verify this number is 100%




Superior Materials, LLC
 30701 W. 10 Mile Rd.
 Suite 500
 Farmington Hills, MI 48336

Sieve	6AA	26A	2NS	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	100.0	100.0	100.0	0.0	0.0
1.5"	100.0	100.0	100.0	100.0	0.0	0.0
1"	98.9	100.0	100.0	99.4	0.6	0.6
3/4"	72.8	100.0	100.0	86.2	13.3	13.8
1/2"	29.1	96.3	100.0	63.6	22.5	36.4
3/8"	15.8	85.4	100.0	55.9	7.7	44.1
#4	2.6	20.6	96.7	42.1	13.8	57.9
#8	1.4	4.0	81.2	33.8	8.3	66.2
#16	1.2	1.8	64.8	26.9	6.9	73.1
#30	1.1	1.5	48.8	20.4	6.5	79.6
#50	1.1	1.4	26.2	11.2	9.1	88.8
#100	1.0	1.3	5.6	2.9	8.4	97.1
LBW	0.9	1.2	1.1	1.0	1.9	99.0

*Maximum % Retained must be above the 3/8" sieve.
 *Any two adjacent sieves must equal 10% except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 4% for each sieve except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 4% for the 3/4" sieve when a 1.5" max. size (nom. Max. 1.0") aggregate is used.

Production Gradation Batch Plant Gradations Aggregate Supplier Gradations

Coarseness Factor: 67 **Workability Factor:** 34

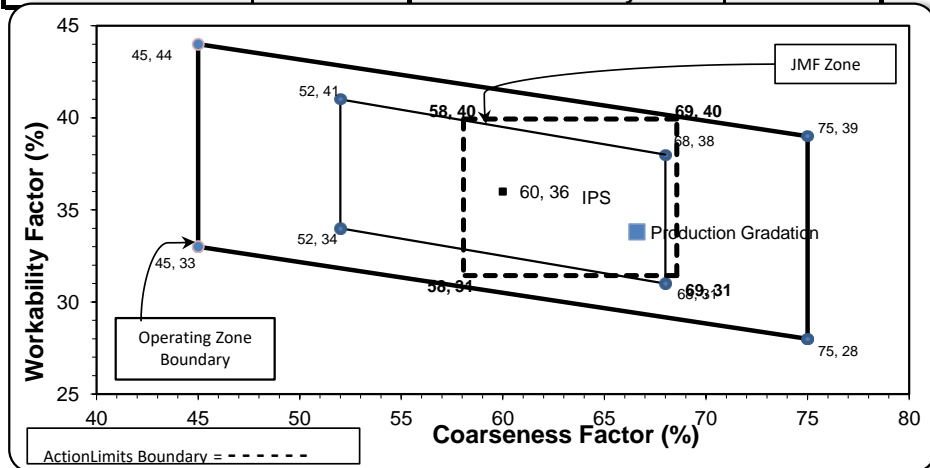

Initial Production Sample (IPS)

Coarseness Factor: 63
Workability Factor: 36

Sieve	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	0.0	0.0
1.5"	100.0	0.0	0.0
1"	100.0	0.0	0.0
3/4"	95.6	4.4	4.4
1/2"	73.1	22.6	26.9
3/8"	59.3	13.8	40.7
#4	42.8	16.5	57.2
#8	35.7	7.1	64.3
#16	28.9	6.8	71.1
#30	20.7	8.2	79.3
#50	9.9	10.8	90.1
#100	2.1	7.8	97.9
LBW	0.9	1.2	99.1

PREPARED BY:
 SM, LLC Technical Service

Approved By:
