

# Aggregate Optimization Chart

**PLANT #:** **P-102**

Sample Date: 4/15/24

Concrete Grade: **S2M, 3500HP**

Contractor: \_\_\_\_\_

Dates Test Represents: 4/16/2024 through 4/22/2024

MDOT No.: \_\_\_\_\_

Agg. Class	Pit #	Source	Weight (SSD)	ft <sup>3</sup>	Specific Gravity	% Contribution
6AA	58-003	Stoneco	1500	8.94	2.69	48.4
26A	58-003	Stoneco	400	2.38	2.69	12.9
2NS	63-114	Highland	1200	7.26	2.65	38.7
<b>Total Wt</b>			<b>3100</b>	<b>18.58</b>		<b>100.0</b>

<----- Verify this number is 100%




**Superior Materials, LLC**  
 30701 W. 10 Mile Rd.  
 Suite 500  
 Farmington Hills, MI 48336

Sieve	6AA	26A	2NS	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	100.0	100.0	100.0	0.0	0.0
1.5"	100.0	100.0	100.0	100.0	0.0	0.0
1"	100.0	100.0	100.0	100.0	0.0	0.0
3/4"	88.7	100.0	100.0	94.5	5.5	5.5
1/2"	45.3	95.2	100.0	72.9	21.6	27.1
3/8"	23.2	64.1	100.0	58.2	14.7	41.8
#4	3.3	9.4	99.2	41.2	17.0	58.8
#8	2.0	4.0	85.4	34.5	6.7	65.5
#16	1.7	2.7	66.3	26.8	7.7	73.2
#30	1.5	2.2	46.8	19.1	7.7	80.9
#50	1.3	2.0	19.3	8.4	10.8	91.6
#100	1.2	1.9	3.6	2.2	6.1	97.8
LBW	0.9	1.8	0.9	1.0	1.2	99.0

\*Maximum % Retained must be above the 3/8" sieve.  
 \*Any two adjacent sieves must equal 10% except max., nom. max., #100 and #200 sieves.  
 \*% Retained must be at least 4% for each sieve except max., nom. max., #100 and #200 sieves.  
 \*% Retained must be at least 4% for the 3/4" sieve when a 1.5" max. size (nom. Max. 1.0") aggregate is used.

Production Gradation  Batch Plant Gradations  Aggregate Supplier Gradations

**Coarseness Factor:** **64**      **Workability Factor:** **35**

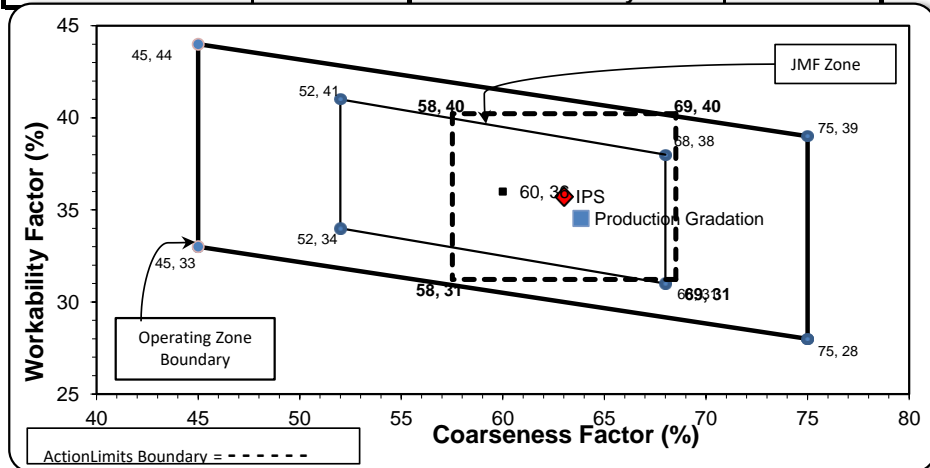

Initial Production Sample (IPS)

**Coarseness Factor:** **63**  
**Workability Factor:** **36**

Sieve	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	0.0	0.0
1.5"	100.0	0.0	0.0
1"	99.2	0.8	0.8
3/4"	90.9	8.3	9.1
1/2"	71.3	19.6	28.7
3/8"	59.5	11.8	40.5
#4	43.8	15.7	56.2
#8	35.7	8.1	64.3
#16	27.0	8.7	73.0
#30	18.6	8.4	81.4
#50	6.8	11.8	93.2
#100	1.4	5.4	98.6
LBW	0.6	0.8	99.4

PREPARED BY:  
 SM, LLC Technical Service

Approved By:

# Aggregate Optimization Chart

**PLANT #:** **P-103**

Sample Date: 4/15/24

Concrete Grade: **S2M, 3500HP**

Dates Test Represents: 4/16/2024 through 4/22/2024

Contractor: \_\_\_\_\_

MDOT No.: \_\_\_\_\_

Agg. Class	Pit #	Source	Weight (SSD)	ft <sup>3</sup>	Specific Gravity	% Contribution
6AA	58-003	Stoneco	1500	8.94	2.69	48.4
26A	58-003	Stoneco	400	2.38	2.69	12.9
2NS	63-114	Highland	1200	7.26	2.65	38.7
<b>Total Wt</b>			<b>3100</b>	<b>18.58</b>		<b>100.0</b>

<----- Verify this number is 100%




**Superior Materials, LLC**  
 30701 W. 10 Mile Rd.  
 Suite 500  
 Farmington Hills, MI 48336

Sieve	6AA	26A	2NS	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	100.0	100.0	100.0	0.0	0.0
1.5"	100.0	100.0	100.0	100.0	0.0	0.0
1"	100.0	100.0	100.0	100.0	0.0	0.0
3/4"	88.7	100.0	100.0	94.5	5.5	5.5
1/2"	45.3	95.2	100.0	72.9	21.6	27.1
3/8"	23.2	64.1	100.0	58.2	14.7	41.8
#4	3.3	9.4	99.2	41.2	17.0	58.8
#8	2.0	4.0	85.4	34.5	6.7	65.5
#16	1.7	2.7	66.3	26.8	7.7	73.2
#30	1.5	2.2	46.8	19.1	7.7	80.9
#50	1.3	2.0	19.3	8.4	10.8	91.6
#100	1.2	1.9	3.6	2.2	6.1	97.8
LBW	0.9	1.8	0.9	1.0	1.2	99.0

\*Maximum % Retained must be above the 3/8" sieve.  
 \*Any two adjacent sieves must equal 10% except max., nom. max., #100 and #200 sieves.  
 \*% Retained must be at least 4% for each sieve except max., nom. max., #100 and #200 sieves.  
 \*% Retained must be at least 4% for the 3/4" sieve when a 1.5" max. size (nom. Max. 1.0") aggregate is used.

Production Gradation  Batch Plant Gradations  Aggregate Supplier Gradations

**Coarseness Factor:** **64**      **Workability Factor:** **35**

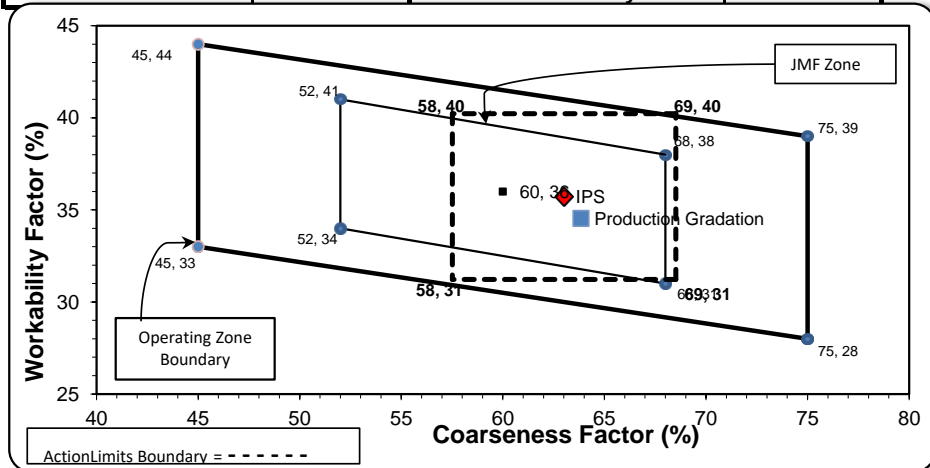

Initial Production Sample (IPS)

**Coarseness Factor:** **63**  
**Workability Factor:** **36**

Sieve	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	0.0	0.0
1.5"	100.0	0.0	0.0
1"	99.2	0.8	0.8
3/4"	90.9	8.3	9.1
1/2"	71.3	19.6	28.7
3/8"	59.5	11.8	40.5
#4	43.8	15.7	56.2
#8	35.7	8.1	64.3
#16	27.0	8.7	73.0
#30	18.6	8.4	81.4
#50	6.8	11.8	93.2
#100	1.4	5.4	98.6
LBW	0.6	0.8	99.4

PREPARED BY:  
 SM, LLC Technical Service

Approved BY:

# Aggregate Optimization Chart

**PLANT #:** 12

Sample Date: 4/15/24

Concrete Grade: **S2M, 3500HP**

Dates Test Represents: 4/16/2024 through 4/22/2024

Contractor: \_\_\_\_\_

MDOT No.: \_\_\_\_\_

Agg. Class	Pit #	Source	Weight (SSD)	ft <sup>3</sup>	Specific Gravity	% Contribution
6AA	71-47	Presque Isle	1550	9.48	2.62	50.8
26A	71-47	Presque Isle	270	1.65	2.62	8.9
2NS	63-115	Ray Rd	1230	7.44	2.65	40.3
<b>Total Wt</b>			<b>3050</b>	<b>18.57</b>		<b>100.0</b>

<---- Verify this number is 100%




**Superior Materials, LLC**  
 30701 W. 10 Mile Rd.  
 Suite 500  
 Farmington Hills, MI 48336

Sieve	6AA	26A	2NS	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	100.0	100.0	100.0	0.0	0.0
1.5"	100.0	100.0	100.0	100.0	0.0	0.0
1"	98.8	100.0	100.0	99.4	0.6	0.6
3/4"	76.7	100.0	100.0	88.2	11.2	11.8
1/2"	28.4	93.1	100.0	63.0	25.2	37.0
3/8"	15.5	79.6	100.0	55.3	7.8	44.7
#4	2.9	13.0	96.7	41.6	13.6	58.4
#8	1.6	2.8	81.8	34.0	7.6	66.0
#16	1.5	1.7	65.2	27.2	6.8	72.8
#30	1.4	1.5	49.0	20.6	6.6	79.4
#50	1.4	1.5	24.8	10.8	9.8	89.2
#100	1.3	1.4	4.3	2.5	8.3	97.5
LBW	1.0	1.2	0.6	0.9	1.7	99.1

\*Maximum % Retained must be above the 3/8" sieve.  
 \*Any two adjacent sieves must equal 10% except max., nom. max., #100 and #200 sieves.  
 \*% Retained must be at least 4% for each sieve except max., nom. max., #100 and #200 sieves.  
 \*% Retained must be at least 4% for the 3/4" sieve when a 1.5" max. size (nom. Max. 1.0") aggregate is used.

Production Gradation  Batch Plant Gradations  Aggregate Supplier Gradations

**Coarseness Factor:** 68      **Workability Factor:** 34

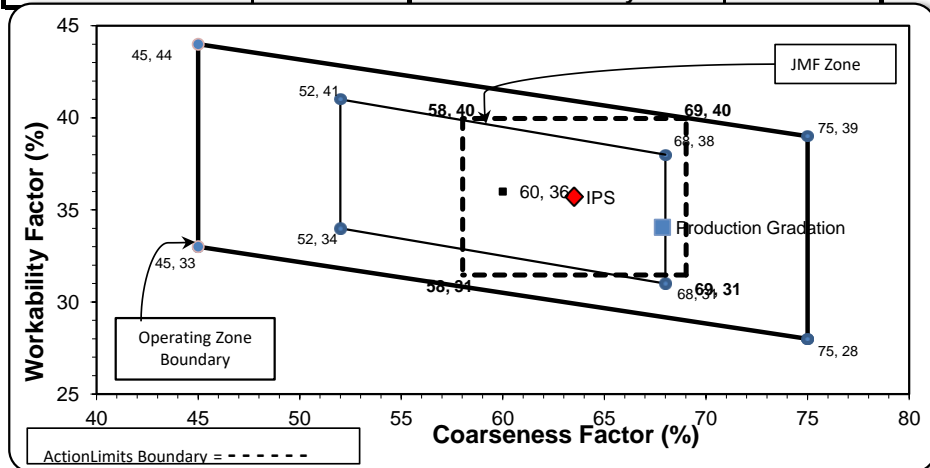

Initial Production Sample (IPS)

**Coarseness Factor:** 64  
**Workability Factor:** 36

Sieve	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	0.0	0.0
1.5"	100.0	0.0	0.0
1"	99.2	0.8	0.8
3/4"	90.9	8.3	9.1
1/2"	71.3	19.6	28.7
3/8"	59.2	12.1	40.8
#4	41.5	17.7	58.5
#8	35.7	5.8	64.3
#16	27.9	7.9	72.1
#30	18.3	9.5	81.7
#50	7.3	11.0	92.7
#100	2.0	5.3	98.0
LBW	0.9	1.1	99.1

PREPARED BY:  
 SM, LLC Technical Service

Approved By:

# Aggregate Optimization Chart

**PLANT #:** p11

Sample Date: 4/15/24

Concrete Grade: **S2M, 3500HP**

Dates Test Represents: 4/16/2024 through 4/22/2024

Contractor: \_\_\_\_\_

MDOT No.: \_\_\_\_\_

Agg. Class	Pit #	Source	Weight (SSD)	ft <sup>3</sup>	Specific Gravity	% Contribution
6AA	71-47	Presque Isle	1600	9.79	2.62	52.5
26A	71-47	Presque Isle	220	1.35	2.62	7.2
2NS	95-013	Smelter Bay	1230	7.44	2.65	40.3
<b>Total Wt</b>			<b>3050</b>	<b>18.57</b>		<b>100.0</b>

<----- Verify this number is 100%




**Superior Materials, LLC**  
 30701 W. 10 Mile Rd.  
 Suite 500  
 Farmington Hills, MI 48336

Sieve	6AA	26A	2NS	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	100.0	100.0	100.0	0.0	0.0
1.5"	100.0	100.0	100.0	100.0	0.0	0.0
1"	98.3	100.0	100.0	99.1	0.9	0.9
3/4"	79.8	100.0	100.0	89.4	9.7	10.6
1/2"	35.8	93.1	100.0	65.8	23.6	34.2
3/8"	20.5	79.6	100.0	56.8	9.0	43.2
#4	3.0	13.0	96.5	41.4	15.4	58.6
#8	2.1	2.8	85.2	35.7	5.8	64.3
#16	1.7	1.7	70.3	29.4	6.3	70.6
#30	1.6	1.5	50.2	21.2	8.2	78.8
#50	1.5	1.5	24.0	10.6	10.6	89.4
#100	1.5	1.4	7.3	3.8	6.7	96.2
LBW	1.2	1.2	1.3	1.2	2.6	98.8

\*Maximum % Retained must be above the 3/8" sieve.  
 \*Any two adjacent sieves must equal 10% except max., nom. max., #100 and #200 sieves.  
 \*% Retained must be at least 4% for each sieve except max., nom. max., #100 and #200 sieves.  
 \*% Retained must be at least 4% for the 3/4" sieve when a 1.5" max. size (nom. Max. 1.0") aggregate is used.

Production Gradation  Batch Plant Gradations  Aggregate Supplier Gradations

**Coarseness Factor:** 67      **Workability Factor:** 36

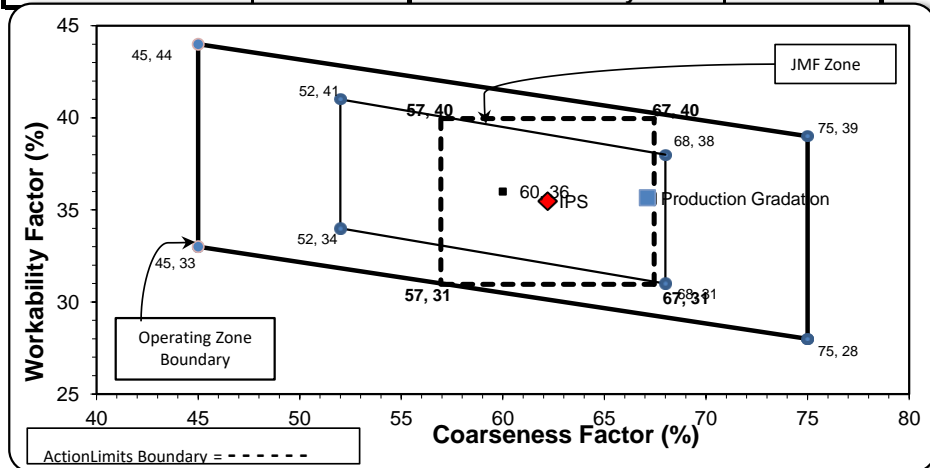

Initial Production Sample (IPS)

**Coarseness Factor:** 62  
**Workability Factor:** 35

Sieve	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	0.0	0.0
1.5"	100.0	0.0	0.0
1"	100.0	0.0	0.0
3/4"	94.0	6.0	6.0
1/2"	70.2	23.7	29.8
3/8"	59.9	10.4	40.1
#4	42.7	17.2	57.3
#8	35.5	7.2	64.5
#16	28.4	7.0	71.6
#30	19.2	9.2	80.8
#50	8.9	10.3	91.1
#100	3.1	5.9	96.9
LBW	1.4	1.7	98.6

PREPARED BY:  
 SM, LLC Technical Service

Approved By:

# Aggregate Optimization Chart

**PLANT #:** **P-35**

Sample Date: 4/15/24

Concrete Grade: **S2M, 3500HP**

Dates Test Represents: 4/16/2024 through 4/22/2024

Contractor: \_\_\_\_\_

MDOT No.: \_\_\_\_\_

Agg. Class	Pit #	Source	Weight (SSD)	ft <sup>3</sup>	Specific Gravity	% Contribution
6AA	58-003	Stoneco	1500	8.94	2.69	48.4
26A	58-003	Stoneco	400	2.38	2.69	12.9
2NS	81-019	Pleasant Lake	1200	7.26	2.65	38.7
<b>Total Wt</b>			<b>3100</b>	<b>18.58</b>		<b>100.0</b>

<----- Verify this number is 100%




**Superior Materials, LLC**  
 30701 W. 10 Mile Rd.  
 Suite 500  
 Farmington Hills, MI 48336

Sieve	6AA	26A	2NS	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	100.0	100.0	100.0	0.0	0.0
1.5"	100.0	100.0	100.0	100.0	0.0	0.0
1"	100.0	100.0	100.0	100.0	0.0	0.0
3/4"	88.7	100.0	100.0	94.5	5.5	5.5
1/2"	45.3	95.2	100.0	72.9	21.6	27.1
3/8"	23.2	64.1	100.0	58.2	14.7	41.8
#4	3.3	9.4	98.7	41.0	17.2	59.0
#8	2.0	4.0	86.0	34.8	6.2	65.2
#16	1.7	2.7	65.8	26.6	8.1	73.4
#30	1.5	2.2	44.0	18.0	8.6	82.0
#50	1.3	2.0	17.3	7.6	10.5	92.4
#100	1.2	1.9	2.7	1.9	5.7	98.1
LBW	0.9	1.8	1.0	1.1	0.8	98.9

\*Maximum % Retained must be above the 3/8" sieve.  
 \*Any two adjacent sieves must equal 10% except max., nom. max., #100 and #200 sieves.  
 \*% Retained must be at least 4% for each sieve except max., nom. max., #100 and #200 sieves.  
 \*% Retained must be at least 4% for the 3/4" sieve when a 1.5" max. size (nom. Max. 1.0") aggregate is used.

Production Gradation  Batch Plant Gradations  Aggregate Supplier Gradations

**Coarseness Factor:** **64**      **Workability Factor:** **35**

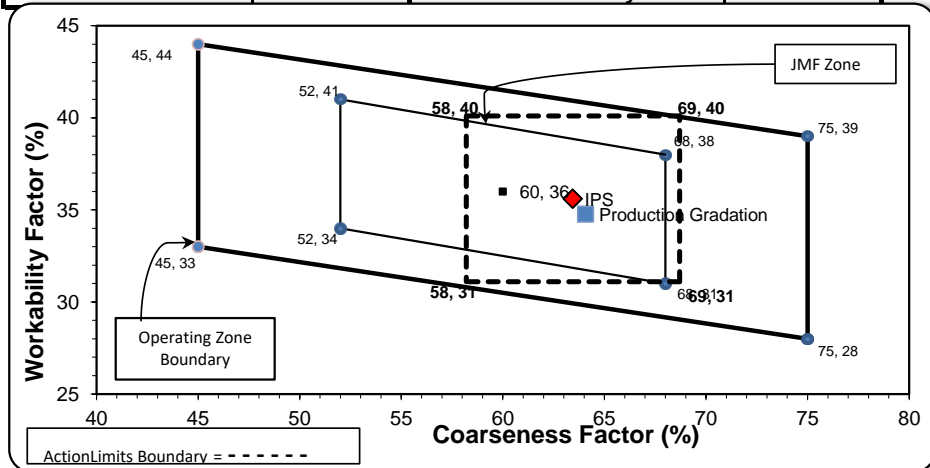

Initial Production Sample (IPS)

**Coarseness Factor:** **63**  
**Workability Factor:** **36**

Sieve	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	0.0	0.0
1.5"	100.0	0.0	0.0
1"	100.0	0.0	0.0
3/4"	93.1	6.9	6.9
1/2"	70.0	23.1	30.0
3/8"	59.1	10.9	40.9
#4	46.0	13.1	54.0
#8	35.6	10.4	64.4
#16	27.2	8.4	72.8
#30	19.8	7.4	80.2
#50	10.1	9.7	89.9
#100	2.5	7.6	97.5
LBW	0.9	1.6	99.1

PREPARED BY:  
 SM, LLC Technical Service

Approved By:

# Aggregate Optimization Chart

**PLANT #:** **P-38**

Sample Date: 4/15/24

Concrete Grade: **S2M, 3500HP**

Contractor: \_\_\_\_\_

Dates Test Represents: 4/16/2024 through 4/22/2024

MDOT No.: \_\_\_\_\_

Agg. Class	Pit #	Source	Weight (SSD)	ft <sup>3</sup>	Specific Gravity	% Contribution
6AA	58-003	Stoneco	1500	8.94	2.69	48.4
26A	58-003	Stoneco	400	2.38	2.69	12.9
2NS	81-019	Pleasant Lake	1200	7.26	2.65	38.7
<b>Total Wt</b>			<b>3100</b>	<b>18.58</b>		<b>100.0</b>

<----- Verify this number is 100%




**Superior Materials, LLC**  
 30701 W. 10 Mile Rd.  
 Suite 500  
 Farmington Hills, MI 48336

Sieve	6AA	26A	2NS	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	100.0	100.0	100.0	0.0	0.0
1.5"	100.0	100.0	100.0	100.0	0.0	0.0
1"	100.0	100.0	100.0	100.0	0.0	0.0
3/4"	88.7	100.0	100.0	94.5	5.5	5.5
1/2"	45.3	95.2	100.0	72.9	21.6	27.1
3/8"	23.2	64.1	100.0	58.2	14.7	41.8
#4	3.3	9.4	98.7	41.0	17.2	59.0
#8	2.0	4.0	86.0	34.8	6.2	65.2
#16	1.7	2.7	65.8	26.6	8.1	73.4
#30	1.5	2.2	44.0	18.0	8.6	82.0
#50	1.3	2.0	17.3	7.6	10.5	92.4
#100	1.2	1.9	2.7	1.9	5.7	98.1
LBW	0.9	1.8	1.0	1.1	0.8	98.9

\*Maximum % Retained must be above the 3/8" sieve.  
 \*Any two adjacent sieves must equal 10% except max., nom. max., #100 and #200 sieves.  
 \*% Retained must be at least 4% for each sieve except max., nom. max., #100 and #200 sieves.  
 \*% Retained must be at least 4% for the 3/4" sieve when a 1.5" max. size (nom. Max. 1.0") aggregate is used.

Production Gradation  Batch Plant Gradations  Aggregate Supplier Gradations

**Coarseness Factor:** **64**      **Workability Factor:** **35**

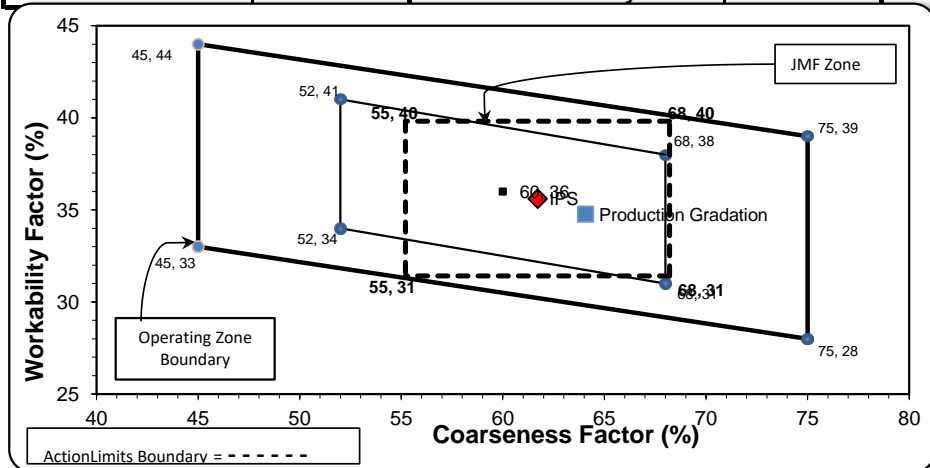

Initial Production Sample (IPS)

**Coarseness Factor:** **62**  
**Workability Factor:** **36**

Sieve	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	0.0	0.0
1.5"	100.0	0.0	0.0
1"	99.2	0.8	0.8
3/4"	91.1	8.1	8.9
1/2"	72.0	19.1	28.0
3/8"	60.3	11.7	39.7
#4	43.4	16.9	56.6
#8	35.6	7.8	64.4
#16	28.4	7.2	71.6
#30	21.8	6.7	78.2
#50	9.1	12.6	90.9
#100	1.7	7.4	98.3
LBW	1.1	0.6	98.9

PREPARED BY:  
 SM, LLC Technical Service

Approved By:

# Aggregate Optimization Chart

**PLANT #:** **P-O2**

Sample Date: 4/15/24

Concrete Grade: **S2M, 3500HP**

Dates Test Represents: 4/16/2024 through 4/22/2024

Contractor: \_\_\_\_\_

MDOT No.: \_\_\_\_\_

Agg. Class	Pit #	Source	Weight (SSD)	ft <sup>3</sup>	Specific Gravity	% Contribution
6AA	71-47	Presque Isle	1500	9.17	2.62	49.2
26A	71-47	Presque Isle	320	1.96	2.62	10.5
2NS	63-115	Ray Rd	1230	7.44	2.65	40.3
<b>Total Wt</b>			<b>3050</b>	<b>18.57</b>		<b>100.0</b>

<---- Verify this number is 100%




**Superior Materials, LLC**  
 30701 W. 10 Mile Rd.  
 Suite 500  
 Farmington Hills, MI 48336

Sieve	6AA	26A	2NS	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	100.0	100.0	100.0	0.0	0.0
1.5"	100.0	100.0	100.0	100.0	0.0	0.0
1"	98.8	100.0	100.0	99.4	0.6	0.6
3/4"	76.7	100.0	100.0	88.5	10.9	11.5
1/2"	28.4	93.1	100.0	64.1	24.5	35.9
3/8"	15.5	79.6	100.0	56.3	7.8	43.7
#4	2.9	13.0	96.7	41.8	14.5	58.2
#8	1.6	2.8	81.8	34.1	7.7	65.9
#16	1.5	1.7	65.2	27.2	6.9	72.8
#30	1.4	1.5	49.0	20.6	6.6	79.4
#50	1.4	1.5	24.8	10.8	9.8	89.2
#100	1.3	1.4	4.3	2.5	8.3	97.5
LBW	1.0	1.2	0.6	0.9	1.7	99.1

\*Maximum % Retained must be above the 3/8" sieve.  
 \*Any two adjacent sieves must equal 10% except max., nom. max., #100 and #200 sieves.  
 \*% Retained must be at least 4% for each sieve except max., nom. max., #100 and #200 sieves.  
 \*% Retained must be at least 4% for the 3/4" sieve when a 1.5" max. size (nom. Max. 1.0") aggregate is used.

Production Gradation  Batch Plant Gradations  Aggregate Supplier Gradations

**Coarseness Factor:** **66**      **Workability Factor:** **34**

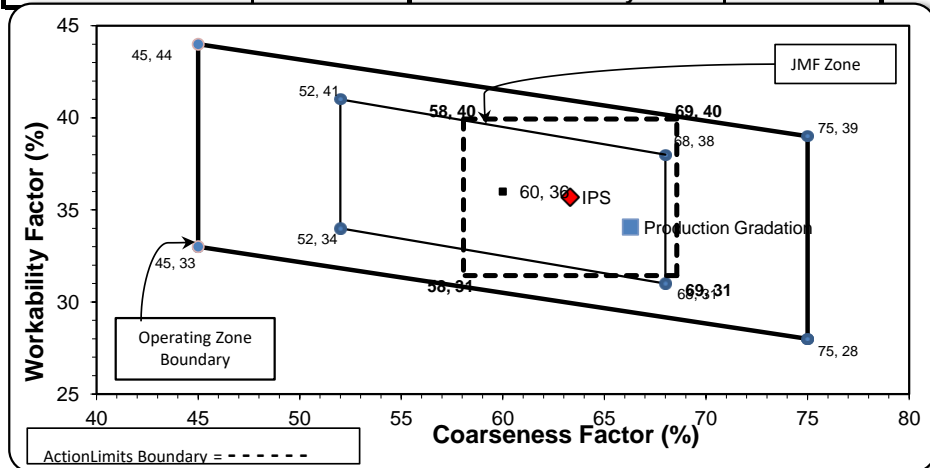

Intial Production Sample (IPS)

**Coarseness Factor:** **63**  
**Workability Factor:** **36**

Sieve	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	0.0	0.0
1.5"	100.0	0.0	0.0
1"	100.0	0.0	0.0
3/4"	95.6	4.4	4.4
1/2"	73.1	22.6	26.9
3/8"	59.3	13.8	40.7
#4	42.8	16.5	57.2
#8	35.7	7.1	64.3
#16	28.9	6.8	71.1
#30	20.7	8.2	79.3
#50	9.9	10.8	90.1
#100	2.1	7.8	97.9
LBW	0.9	1.2	99.1

PREPARED BY:  
 SM, LLC Technical Service

Approved By:
