

# Aggregate Optimization Chart

# Production Gradation Report

**PLANT #:** **P-102**

Sample Date: 9/2/24

Concrete Grade: DM, 4500HP

Contractor: \_\_\_\_\_

Dates Test Represents: 9/3/2024 through 9/9/2024

MDOT No.: \_\_\_\_\_

Agg. Class	Pit #	Source	Weight (SSD)	ft <sup>3</sup>	Specific Gravity	% Contribution
6AA	58-003	Stoneco	1475	8.79	2.69	50.0
26A	58-003	Stoneco	325	1.94	2.69	11.0
2NS	63-114	Highland	1150	6.95	2.65	39.0
<b>Total Wt</b>			<b>2950</b>	<b>17.68</b>		<b>100.0</b>

<----- Verify this number is 100%



**Superior Materials, LLC**  
 30701 W. 10 Mile Rd.  
 Suite 500  
 Farmington Hills, MI 48336


Sieve	6AA	26A	2NS	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	100.0	100.0	100.0	0.0	0.0
1.5"	100.0	100.0	100.0	100.0	0.0	0.0
1"	100.0	100.0	100.0	100.0	0.0	0.0
3/4"	82.8	100.0	100.0	91.4	8.6	8.6
1/2"	41.4	98.6	100.0	70.5	20.9	29.5
3/8"	19.9	87.6	100.0	58.6	12.0	41.4
#4	2.8	14.6	99.0	41.6	17.0	58.4
#8	1.4	4.8	85.9	34.7	6.9	65.3
#16	1.0	3.0	69.7	28.0	6.7	72.0
#30	1.0	2.3	51.8	20.9	7.1	79.1
#50	0.9	2.1	23.7	9.9	11.0	90.1
#100	0.9	2.0	4.7	2.5	7.4	97.5
LBW	0.7	1.8	1.1	1.0	1.5	99.0

\*Maximum % Retained must be above the 3/8" sieve.  
 \*Any two adjacent sieves must equal 10% except max., nom. max., #100 and #200 sieves.  
 \*% Retained must be at least 4% for each sieve except max., nom. max., #100 and #200 sieves.  
 \*% Retained must be at least 4% for the 3/4" sieve when a 1.5" max. size (nom. Max. 1.0") aggregate is used.

Production Gradation  Batch Plant Gradations  Aggregate Supplier Gradations  Adjusted WF Initial Production Sample (IPS)

<b>Coarseness Factor:</b>	<b>63</b>	<b>Workability Factor:</b>	<b>35</b>	<b>37.2</b>
---------------------------	-----------	----------------------------	-----------	-------------

<b>Coarseness Factor:</b>	<b>61</b>
<b>Workability Factor:</b>	<b>36</b>

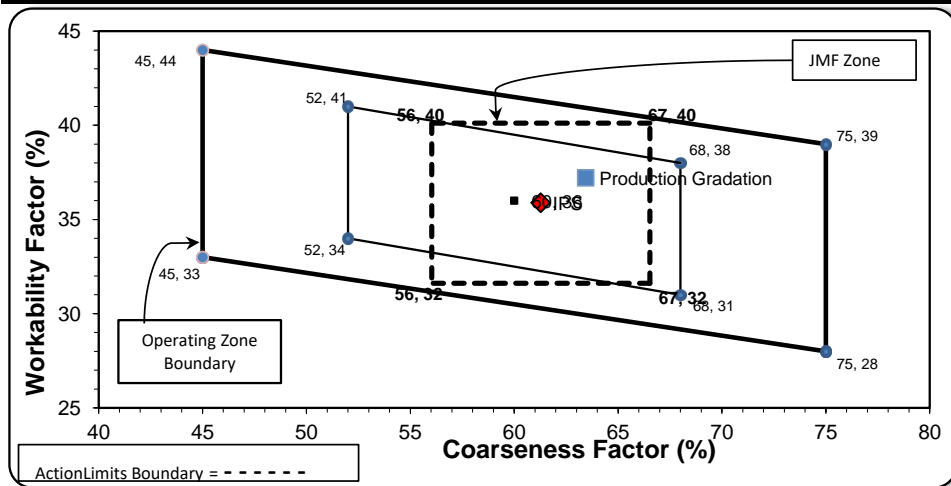

Sieve	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	0.0	0.0
1.5"	100.0	0.0	0.0
1"	99.3	0.7	0.7
3/4"	89.2	10.1	10.8
1/2"	70.7	18.5	29.3
3/8"	60.7	10.0	39.3
#4	44.4	16.3	55.6
#8	35.9	8.5	64.1
#16	27.3	8.6	72.7
#30	19.1	8.2	80.9
#50	7.4	11.7	92.6
#100	1.9	5.6	98.1
LBW	0.7	1.2	99.3

PREPARED BY:  
 SM, LLC Technical Service

Approved By:

# Aggregate Optimization Chart

# Production Gradation Report

**PLANT #:** P-103

Sample Date: 9/2/24

Concrete Grade: DM, 4500HP

Contractor: \_\_\_\_\_

Dates Test Represents: 9/3/2024 through 9/9/2024

MDOT No.: \_\_\_\_\_

Agg. Class	Pit #	Source	Weight (SSD)	ft <sup>3</sup>	Specific Gravity	% Contribution
6AA	58-003	Stoneco	1475	8.79	2.69	50.0
26A	58-003	Stoneco	325	1.94	2.69	11.0
2NS	63-114	Highland	1150	6.95	2.65	39.0
<b>Total Wt</b>			<b>2950</b>	<b>17.68</b>		<b>100.0</b>

<----- Verify this number is 100%



**Superior Materials, LLC**  
 30701 W. 10 Mile Rd.  
 Suite 500  
 Farmington Hills, MI 48336

Sieve	6AA	26A	2NS	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	100.0	100.0	100.0	0.0	0.0
1.5"	100.0	100.0	100.0	100.0	0.0	0.0
1"	100.0	100.0	100.0	100.0	0.0	0.0
3/4"	82.8	100.0	100.0	91.4	8.6	8.6
1/2"	41.4	98.6	100.0	70.5	20.9	29.5
3/8"	19.9	87.6	100.0	58.6	12.0	41.4
#4	2.8	14.6	99.0	41.6	17.0	58.4
#8	1.4	4.8	85.9	34.7	6.9	65.3
#16	1.0	3.0	69.7	28.0	6.7	72.0
#30	1.0	2.3	51.8	20.9	7.1	79.1
#50	0.9	2.1	23.7	9.9	11.0	90.1
#100	0.9	2.0	4.7	2.5	7.4	97.5
LBW	0.7	1.8	1.1	1.0	1.5	99.0

\*Maximum % Retained must be above the 3/8" sieve.  
 \*Any two adjacent sieves must equal 10% except max., nom. max., #100 and #200 sieves.  
 \*% Retained must be at least 4% for each sieve except max., nom. max., #100 and #200 sieves.  
 \*% Retained must be at least 4% for the 3/4" sieve when a 1.5" max. size (nom. Max. 1.0") aggregate is used.

Production Gradation  Batch Plant Gradations  Aggregate Supplier Gradations


Adjusted WF Initial Production Sample (IPS)

<b>Coarseness Factor:</b>	<b>63</b>	<b>Workability Factor:</b>	<b>35</b>	<b>37.2</b>
---------------------------	-----------	----------------------------	-----------	-------------

<b>Coarseness Factor:</b>	<b>61</b>
---------------------------	-----------

<b>Workability Factor:</b>	<b>36</b>
----------------------------	-----------

Sieve	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	0.0	0.0
1.5"	100.0	0.0	0.0
1"	99.3	0.7	0.7
3/4"	89.2	10.1	10.8
1/2"	70.7	18.5	29.3
3/8"	60.7	10.0	39.3
#4	44.4	16.3	55.6
#8	35.9	8.5	64.1
#16	27.3	8.6	72.7
#30	19.1	8.2	80.9
#50	7.4	11.7	92.6
#100	1.9	5.6	98.1
LBW	0.7	1.2	99.3

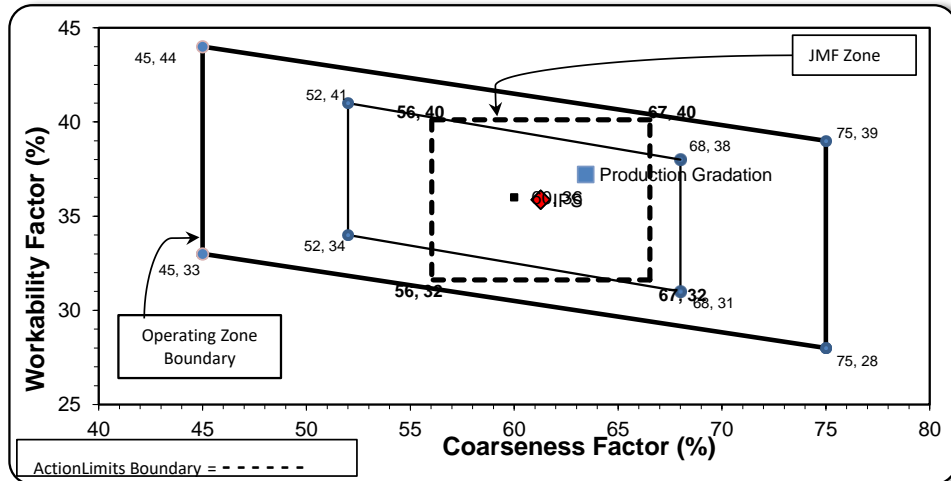

PREPARED BY:  
 SM, LLC Technical Service

Approved BY:

# Aggregate Optimization Chart

**PLANT #:** 12

Sample Date: 9/2/24

Dates Test Represents: 9/3/2024 through 9/9/2024

Concrete Grade: DM, 4500HP

Contractor: \_\_\_\_\_

MDOT No.: \_\_\_\_\_

Agg. Class	Pit #	Source	Weight (SSD)	ft <sup>3</sup>	Specific Gravity	% Contribution
6AA	71-47	Presque Isle	1450	8.87	2.62	49.9
26A	71-47	Presque Isle	305	1.87	2.62	10.5
2NS	63-115	Ray Rd	1150	6.95	2.65	39.6
<b>Total Wt</b>			<b>2905</b>	<b>17.69</b>		<b>100.0</b>

<----- Verify this number is 100%



**Superior Materials, LLC**  
 30701 W. 10 Mile Rd.  
 Suite 500  
 Farmington Hills, MI 48336

Sieve	6AA	26A	2NS	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	100.0	100.0	100.0	0.0	0.0
1.5"	100.0	100.0	100.0	100.0	0.0	0.0
1"	94.8	100.0	100.0	97.4	2.6	2.6
3/4"	71.9	100.0	100.0	86.0	11.4	14.0
1/2"	28.0	94.6	100.0	63.5	22.5	36.5
3/8"	14.2	81.1	100.0	55.2	8.3	44.8
#4	3.0	14.1	96.9	41.3	13.9	58.7
#8	1.8	3.2	79.3	32.6	8.7	67.4
#16	1.7	1.9	62.9	25.9	6.7	74.1
#30	1.6	1.7	47.5	19.8	6.2	80.2
#50	1.6	1.6	26.3	11.4	8.4	88.6
#100	1.5	1.6	6.9	3.6	7.7	96.4
LBW	1.3	1.4	0.8	1.1	2.5	98.9


\*Maximum % Retained must be above the 3/8" sieve.  
 \*Any two adjacent sieves must equal 10% except max., nom. max., #100 and #200 sieves.  
 \*% Retained must be at least 4% for each sieve except max., nom. max., #100 and #200 sieves.  
 \*% Retained must be at least 4% for the 3/4" sieve when a 1.5" max. size (nom. Max. 1.0") aggregate is used.

Production Gradation  Batch Plant Gradations  Aggregate Supplier Gradations

Adjusted WF Initial Production Sample (IPS)

<b>Coarseness Factor:</b>	<b>67</b>	<b>Workability Factor:</b>	<b>33</b>	<b>Adjusted WF</b>	<b>35.1</b>	<b>Coarseness Factor:</b>	<b>63</b>
---------------------------	-----------	----------------------------	-----------	--------------------	-------------	---------------------------	-----------

**Workability Factor:** 36

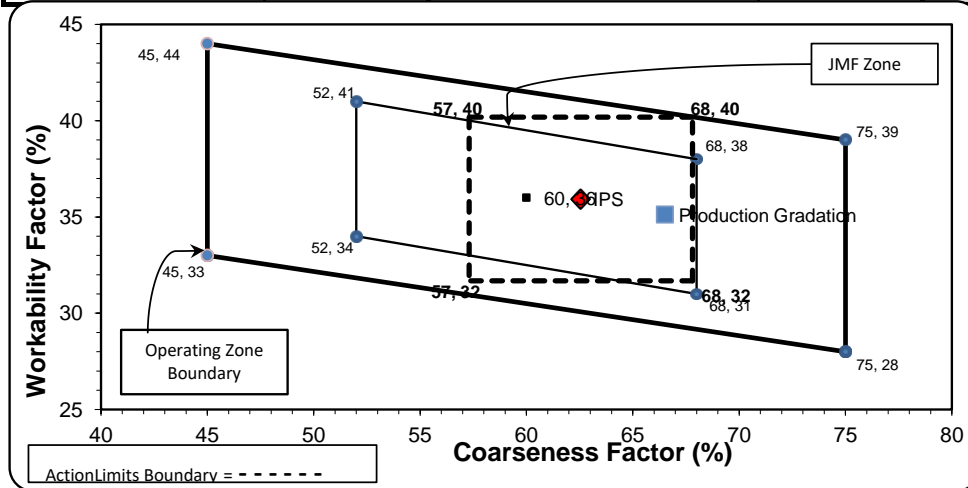

Sieve	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	0.0	0.0
1.5"	100.0	0.0	0.0
1"	99.3	0.7	0.7
3/4"	89.0	10.3	11.0
1/2"	70.3	18.7	29.7
3/8"	59.9	10.4	40.1
#4	41.9	18.0	58.1
#8	35.9	6.0	64.1
#16	27.8	8.2	72.2
#30	18.9	8.8	81.1
#50	6.3	12.6	93.7
#100	1.7	4.6	98.3
LBW	1.0	0.7	99.0

PREPARED BY:  
 SM, LLC Technical Service

Approved By:

# Aggregate Optimization Chart

**PLANT #:** p11

Contractor: \_\_\_\_\_

Sample Date: 9/2/24

Concrete Grade: DM, 4500HP

Dates Test Represents: 9/3/2024 through 9/9/2024

MDOT No.: \_\_\_\_\_

Agg. Class	Pit #	Source	Weight (SSD)	ft <sup>3</sup>	Specific Gravity	% Contribution
6AA	71-47	Presque Isle	1455	8.90	2.62	50.1
26A	71-47	Presque Isle	300	1.83	2.62	10.3
2NS	63-115	Ray Rd	1150	6.95	2.65	39.6
<b>Total Wt</b>			<b>2905</b>	<b>17.69</b>		<b>100.0</b>

<----- Verify this number is 100%



**Superior Materials, LLC**  
 30701 W. 10 Mile Rd.  
 Suite 500  
 Farmington Hills, MI 48336


Sieve	6AA	26A	2NS	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	100.0	100.0	100.0	0.0	0.0
1.5"	100.0	100.0	100.0	100.0	0.0	0.0
1"	94.8	100.0	100.0	97.4	2.6	2.6
3/4"	71.9	100.0	100.0	85.9	11.5	14.1
1/2"	28.0	94.6	100.0	63.4	22.5	36.6
3/8"	14.2	81.1	100.0	55.1	8.3	44.9
#4	3.0	14.1	96.9	41.3	13.8	58.7
#8	1.8	3.2	79.3	32.6	8.7	67.4
#16	1.7	1.9	62.9	25.9	6.7	74.1
#30	1.6	1.7	47.5	19.8	6.2	80.2
#50	1.6	1.6	26.3	11.4	8.4	88.6
#100	1.5	1.6	6.9	3.6	7.7	96.4
LBW	1.3	1.4	0.8	1.1	2.5	98.9

\*Maximum % Retained must be above the 3/8" sieve.  
 \*Any two adjacent sieves must equal 10% except max., nom. max., #100 and #200 sieves.  
 \*% Retained must be at least 4% for each sieve except max., nom. max., #100 and #200 sieves.  
 \*% Retained must be at least 4% for the 3/4" sieve when a 1.5" max. size (nom. Max. 1.0") aggregate is used.

Production Gradation  Batch Plant Gradations  Aggregate Supplier Gradations

Adjusted WF Initial Production Sample (IPS)

<b>Coarseness Factor:</b> 67	<b>Workability Factor:</b> 33	<b>Adjusted WF</b> 35.1	<b>Coarseness Factor:</b> 62
------------------------------	-------------------------------	-------------------------	------------------------------

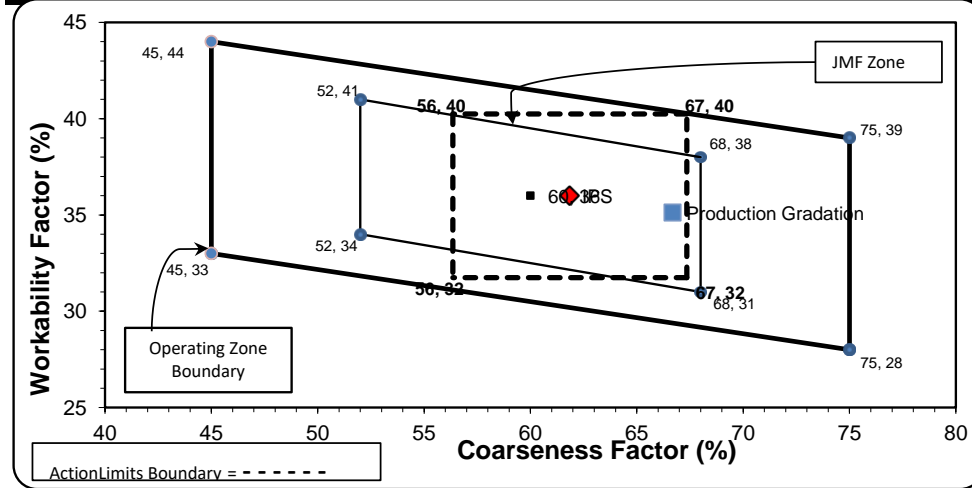

<b>Workability Factor:</b> 36		<b>Coarseness Factor:</b> 62	
Sieve	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	0.0	0.0
1.5"	100.0	0.0	0.0
1"	100.0	0.0	0.0
3/4"	95.0	5.0	5.0
1/2"	72.3	22.8	27.7
3/8"	60.4	11.8	39.6
#4	42.6	17.8	57.4
#8	36.0	6.6	64.0
#16	29.5	6.5	70.5
#30	20.3	9.2	79.7
#50	9.5	10.8	90.5
#100	3.4	6.1	96.6
LBW	1.3	2.1	98.7

PREPARED BY:  
 SM, LLC Technical Service

Approved By:

# Aggregate Optimization Chart

# Production Gradation Report

**PLANT #:** **P-35**

Sample Date: 9/2/24

Concrete Grade: DM, 4500HP

Contractor: \_\_\_\_\_

Dates Test Represents: 9/3/2024 through 9/9/2024

MDOT No.: \_\_\_\_\_

Agg. Class	Pit #	Source	Weight (SSD)	ft <sup>3</sup>	Specific Gravity	% Contribution
6AA	58-003	Stoneco	1475	8.79	2.69	50.0
26A	58-003	Stoneco	325	1.94	2.69	11.0
2NS	81-019	Pleasant Lake	1150	6.95	2.65	39.0
<b>Total Wt</b>			<b>2950</b>	<b>17.68</b>		<b>100.0</b>

<----- Verify this number is 100%



**Superior Materials, LLC**  
 30701 W. 10 Mile Rd.  
 Suite 500  
 Farmington Hills, MI 48336


Sieve	6AA	26A	2NS	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	100.0	100.0	100.0	0.0	0.0
1.5"	100.0	100.0	100.0	100.0	0.0	0.0
1"	100.0	100.0	100.0	100.0	0.0	0.0
3/4"	82.8	100.0	100.0	91.4	8.6	8.6
1/2"	41.4	98.6	100.0	70.5	20.9	29.5
3/8"	19.9	87.6	100.0	58.6	12.0	41.4
#4	2.8	14.6	97.3	40.9	17.6	59.1
#8	1.4	4.8	83.4	33.7	7.2	66.3
#16	1.0	3.0	63.7	25.7	8.1	74.3
#30	1.0	2.3	42.9	17.5	8.2	82.5
#50	0.9	2.1	21.7	9.1	8.3	90.9
#100	0.9	2.0	4.8	2.5	6.6	97.5
LBW	0.7	1.8	0.6	0.8	1.8	99.2

\*Maximum % Retained must be above the 3/8" sieve.  
 \*Any two adjacent sieves must equal 10% except max., nom. max., #100 and #200 sieves.  
 \*% Retained must be at least 4% for each sieve except max., nom. max., #100 and #200 sieves.  
 \*% Retained must be at least 4% for the 3/4" sieve when a 1.5" max. size (nom. Max. 1.0") aggregate is used.

Production Gradation  Batch Plant Gradations  Aggregate Supplier Gradations  Adjusted WF Initial Production Sample (IPS)

<b>Coarseness Factor:</b>	<b>63</b>	<b>Workability Factor:</b>	<b>34</b>	<b>36.2</b>
---------------------------	-----------	----------------------------	-----------	-------------

<b>Coarseness Factor:</b>	<b>61</b>
<b>Workability Factor:</b>	<b>36</b>

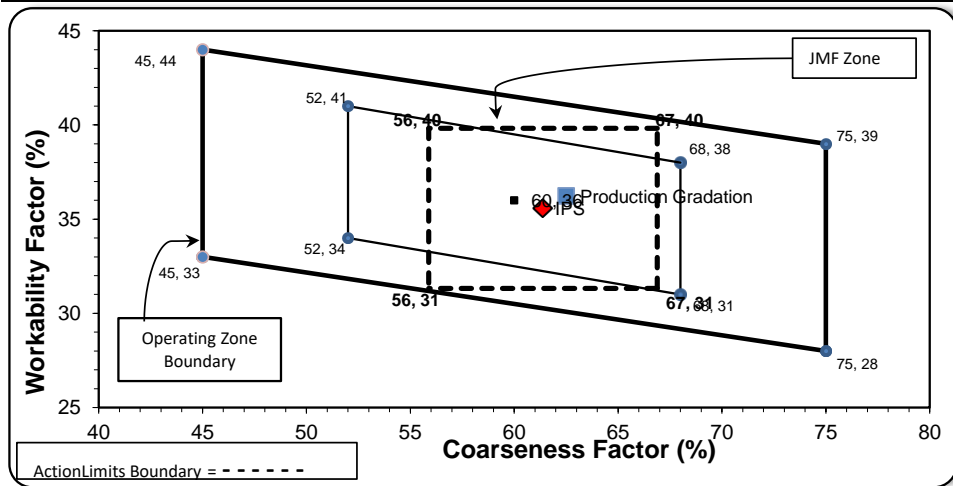

Sieve	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	0.0	0.0
1.5"	100.0	0.0	0.0
1"	99.3	0.7	0.7
3/4"	89.1	10.2	10.9
1/2"	70.5	18.6	29.5
3/8"	60.5	10.0	39.5
#4	44.1	16.4	55.9
#8	35.6	8.5	64.4
#16	27.7	7.9	72.3
#30	20.6	7.1	79.4
#50	8.7	11.8	91.3
#100	1.6	7.1	98.4
LBW	1.1	0.6	98.9

PREPARED BY:  
 SM, LLC Technical Service

Approved By:

# Aggregate Optimization Chart

# Production Gradation Report

**PLANT #:** **P-38**

Sample Date: 9/2/24

Concrete Grade: DM, 4500HP

Contractor: \_\_\_\_\_

Dates Test Represents: 9/3/2024 through 9/9/2024

MDOT No.: \_\_\_\_\_

Agg. Class	Pit #	Source	Weight (SSD)	ft <sup>3</sup>	Specific Gravity	% Contribution
6AA	58-003	Stoneco	1475	8.79	2.69	50.0
26A	58-003	Stoneco	325	1.94	2.69	11.0
2NS	81-019	Pleasant Lake	1150	6.95	2.65	39.0
<b>Total Wt</b>			<b>2950</b>	<b>17.68</b>		<b>100.0</b>

<----- Verify this number is 100%



**Superior Materials, LLC**  
 30701 W. 10 Mile Rd.  
 Suite 500  
 Farmington Hills, MI 48336

Sieve	6AA	26A	2NS	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	100.0	100.0	100.0	0.0	0.0
1.5"	100.0	100.0	100.0	100.0	0.0	0.0
1"	100.0	100.0	100.0	100.0	0.0	0.0
3/4"	82.8	100.0	100.0	91.4	8.6	8.6
1/2"	41.4	98.6	100.0	70.5	20.9	29.5
3/8"	19.9	87.6	100.0	58.6	12.0	41.4
#4	2.8	14.6	97.3	40.9	17.6	59.1
#8	1.4	4.8	83.4	33.7	7.2	66.3
#16	1.0	3.0	63.7	25.7	8.1	74.3
#30	1.0	2.3	42.9	17.5	8.2	82.5
#50	0.9	2.1	21.7	9.1	8.3	90.9
#100	0.9	2.0	4.8	2.5	6.6	97.5
LBW	0.7	1.8	0.6	0.8	1.8	99.2


\*Maximum % Retained must be above the 3/8" sieve.  
 \*Any two adjacent sieves must equal 10% except max., nom. max., #100 and #200 sieves.  
 \*% Retained must be at least 4% for each sieve except max., nom. max., #100 and #200 sieves.  
 \*% Retained must be at least 4% for the 3/4" sieve when a 1.5" max. size (nom. Max. 1.0") aggregate is used.

Production Gradation  Batch Plant Gradations  Aggregate Supplier Gradations  Adjusted WF Initial Production Sample (IPS)

<b>Coarseness Factor:</b>	<b>63</b>	<b>Workability Factor:</b>	<b>34</b>	<b>36.2</b>
---------------------------	-----------	----------------------------	-----------	-------------

<b>Coarseness Factor:</b>	<b>61</b>
---------------------------	-----------

<b>Workability Factor:</b>	<b>36</b>
----------------------------	-----------

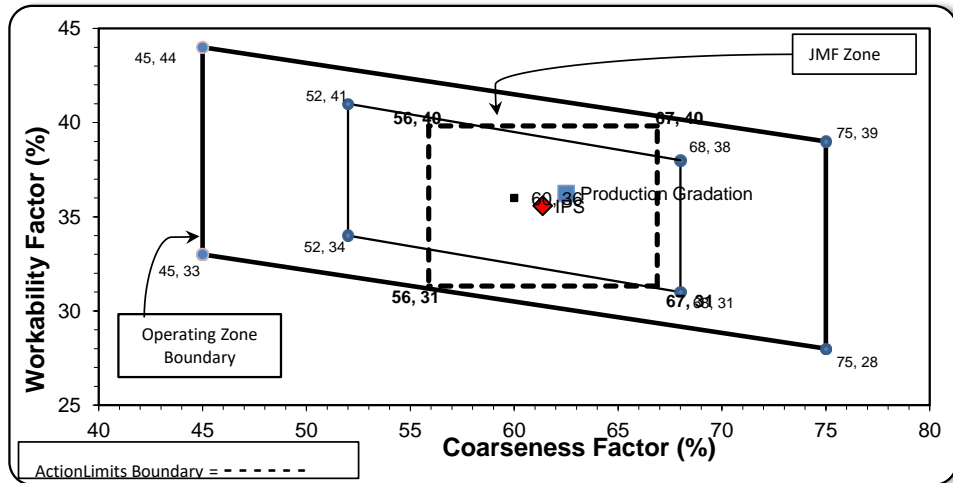

Sieve	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	0.0	0.0
1.5"	100.0	0.0	0.0
1"	99.3	0.7	0.7
3/4"	89.1	10.2	10.9
1/2"	70.5	18.6	29.5
3/8"	60.5	10.0	39.5
#4	44.1	16.4	55.9
#8	35.6	8.5	64.4
#16	27.7	7.9	72.3
#30	20.6	7.1	79.4
#50	8.7	11.8	91.3
#100	1.6	7.1	98.4
LBW	1.1	0.6	98.9

PREPARED BY:  
 SM, LLC Technical Service

Approved By:

# Aggregate Optimization Chart

# Production Gradation Report

**PLANT #:** **P-02**

Sample Date: 9/2/24

Concrete Grade: DM, 4500HP

Contractor: \_\_\_\_\_

Dates Test Represents: 9/3/2024 through 9/9/2024

MDOT No.: \_\_\_\_\_

Agg. Class	Pit #	Source	Weight (SSD)	ft <sup>3</sup>	Specific Gravity	% Contribution
6AA	71-47	Presque Isle	1450	8.87	2.62	49.9
26A	71-47	Presque Isle	305	1.87	2.62	10.5
2NS	63-115	Ray Rd	1150	6.95	2.65	39.6
<b>Total Wt</b>			<b>2905</b>	<b>17.69</b>		<b>100.0</b>

<----- Verify this number is 100%



**Superior Materials, LLC**  
 30701 W. 10 Mile Rd.  
 Suite 500  
 Farmington Hills, MI 48336

Sieve	6AA	26A	2NS	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	100.0	100.0	100.0	0.0	0.0
1.5"	100.0	100.0	100.0	100.0	0.0	0.0
1"	94.8	100.0	100.0	97.4	2.6	2.6
3/4"	71.9	100.0	100.0	86.0	11.4	14.0
1/2"	28.0	94.6	100.0	63.5	22.5	36.5
3/8"	14.2	81.1	100.0	55.2	8.3	44.8
#4	3.0	14.1	96.9	41.3	13.9	58.7
#8	1.8	3.2	79.3	32.6	8.7	67.4
#16	1.7	1.9	62.9	25.9	6.7	74.1
#30	1.6	1.7	47.5	19.8	6.2	80.2
#50	1.6	1.6	26.3	11.4	8.4	88.6
#100	1.5	1.6	6.9	3.6	7.7	96.4
LBW	1.3	1.4	0.8	1.1	2.5	98.9


\*Maximum % Retained must be above the 3/8" sieve.  
 \*Any two adjacent sieves must equal 10% except max., nom. max., #100 and #200 sieves.  
 \*% Retained must be at least 4% for each sieve except max., nom. max., #100 and #200 sieves.  
 \*% Retained must be at least 4% for the 3/4" sieve when a 1.5" max. size (nom. Max. 1.0") aggregate is used.

Production Gradation  Batch Plant Gradations  Aggregate Supplier Gradations  Adjusted WF Initial Production Sample (IPS)

<b>Coarseness Factor:</b>	<b>67</b>	<b>Workability Factor:</b>	<b>33</b>	<b>35.1</b>
---------------------------	-----------	----------------------------	-----------	-------------

<b>Coarseness Factor:</b>	<b>63</b>
---------------------------	-----------

<b>Workability Factor:</b>	<b>35</b>
----------------------------	-----------

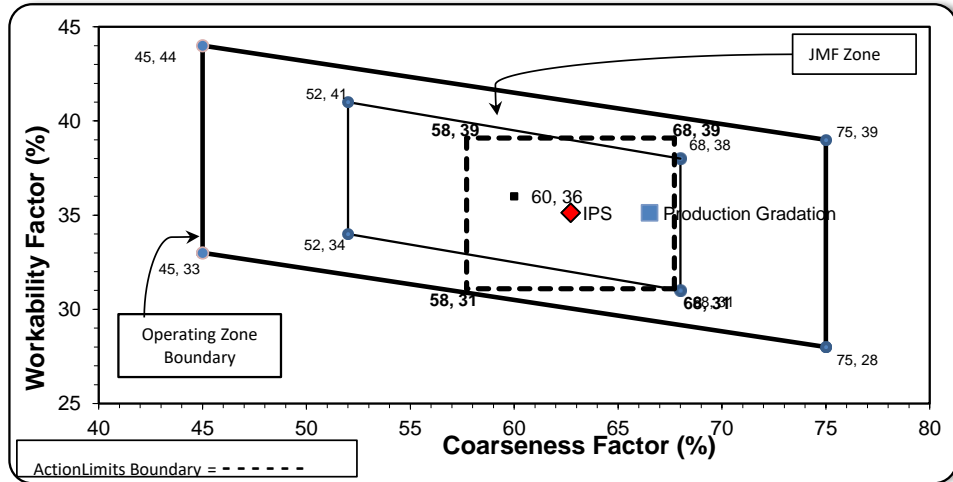

Sieve	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	0.0	0.0
1.5"	100.0	0.0	0.0
1"	100.0	0.0	0.0
3/4"	95.1	4.9	4.9
1/2"	74.6	20.5	25.4
3/8"	59.3	15.3	40.7
#4	42.1	17.2	57.9
#8	35.1	7.1	64.9
#16	29.2	5.9	70.8
#30	21.9	7.3	78.1
#50	9.6	12.4	90.4
#100	2.4	7.2	97.6
LBW	0.9	1.5	99.1

PREPARED BY:  
 SM, LLC Technical Service

Approved By:
