

# Aggregate Optimization Chart

**PLANT #:** **P-102**

Sample Date: 9/9/24

Concrete Grade: **S2M, 3500HP**

Dates Test Represents: 9/10/2024 through 9/16/2024

Contractor: \_\_\_\_\_

MDOT No.: \_\_\_\_\_

Agg. Class	Pit #	Source	Weight (SSD)	ft <sup>3</sup>	Specific Gravity	% Contribution
6AA	58-003	Stoneco	1600	9.53	2.69	51.6
26A	58-003	Stoneco	300	1.79	2.69	9.7
2NS	63-114	Highland	1200	7.26	2.65	38.7
<b>Total Wt</b>			<b>3100</b>	<b>18.58</b>		<b>100.0</b>

<----- Verify this number is 100%




**Superior Materials, LLC**  
 30701 W. 10 Mile Rd.  
 Suite 500  
 Farmington Hills, MI 48336

Sieve	6AA	26A	2NS	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	100.0	100.0	100.0	0.0	0.0
1.5"	100.0	100.0	100.0	100.0	0.0	0.0
1"	100.0	100.0	100.0	100.0	0.0	0.0
3/4"	86.0	100.0	100.0	92.8	7.2	7.2
1/2"	45.2	98.5	100.0	71.6	21.2	28.4
3/8"	18.5	87.0	100.0	56.7	14.9	43.3
#4	3.4	5.8	99.2	40.7	16.0	59.3
#8	2.0	1.9	85.9	34.5	6.2	65.5
#16	1.4	1.4	69.6	27.8	6.7	72.2
#30	1.3	1.2	50.9	20.5	7.3	79.5
#50	1.2	1.2	22.4	9.4	11.1	90.6
#100	1.1	1.1	3.9	2.2	7.2	97.8
LBW	1.2	1.0	0.6	0.9	1.2	99.1

\*Maximum % Retained must be above the 3/8" sieve.  
 \*Any two adjacent sieves must equal 10% except max., nom. max., #100 and #200 sieves.  
 \*% Retained must be at least 4% for each sieve except max., nom. max., #100 and #200 sieves.  
 \*% Retained must be at least 4% for the 3/4" sieve when a 1.5" max. size (nom. Max. 1.0") aggregate is used.

Production Gradation  Batch Plant Gradations  Aggregate Supplier Gradations

**Coarseness Factor:** **66**      **Workability Factor:** **34**

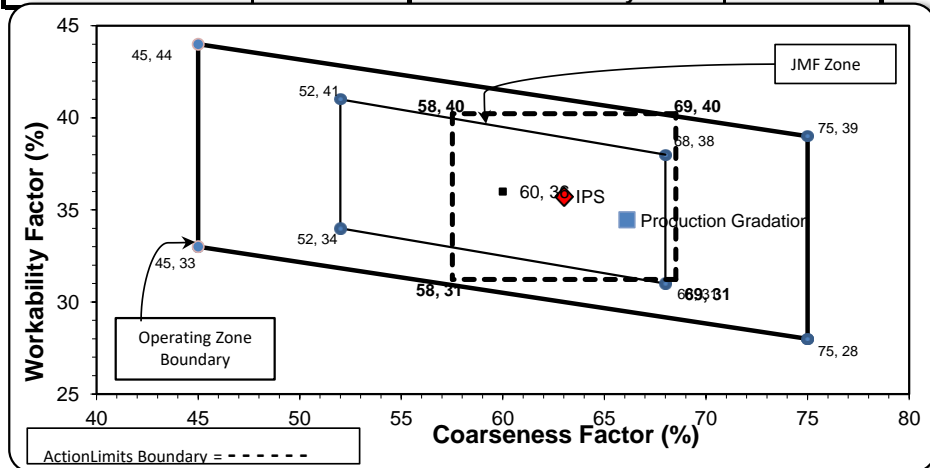

Initial Production Sample (IPS)

**Coarseness Factor:** **63**  
**Workability Factor:** **36**

Sieve	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	0.0	0.0
1.5"	100.0	0.0	0.0
1"	99.2	0.8	0.8
3/4"	90.9	8.3	9.1
1/2"	71.3	19.6	28.7
3/8"	59.5	11.8	40.5
#4	43.8	15.7	56.2
#8	35.7	8.1	64.3
#16	27.0	8.7	73.0
#30	18.6	8.4	81.4
#50	6.8	11.8	93.2
#100	1.4	5.4	98.6
LBW	0.6	0.8	99.4

PREPARED BY:  
 SM, LLC Technical Service

Approved By:

# Aggregate Optimization Chart

**PLANT #:** **P-103**

Sample Date: 9/9/24

Concrete Grade: **S2M, 3500HP**

Dates Test Represents: 9/10/2024 through 9/16/2024

Contractor: \_\_\_\_\_

MDOT No.: \_\_\_\_\_

Agg. Class	Pit #	Source	Weight (SSD)	ft <sup>3</sup>	Specific Gravity	% Contribution
6AA	58-003	Stoneco	1600	9.53	2.69	51.6
26A	58-003	Stoneco	300	1.79	2.69	9.7
2NS	63-114	Highland	1200	7.26	2.65	38.7
<b>Total Wt</b>			<b>3100</b>	<b>18.58</b>		<b>100.0</b>

<----- Verify this number is 100%




**Superior Materials, LLC**  
 30701 W. 10 Mile Rd.  
 Suite 500  
 Farmington Hills, MI 48336

Sieve	6AA	26A	2NS	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	100.0	100.0	100.0	0.0	0.0
1.5"	100.0	100.0	100.0	100.0	0.0	0.0
1"	100.0	100.0	100.0	100.0	0.0	0.0
3/4"	86.0	100.0	100.0	92.8	7.2	7.2
1/2"	45.2	98.5	100.0	71.6	21.2	28.4
3/8"	18.5	87.0	100.0	56.7	14.9	43.3
#4	3.4	5.8	99.2	40.7	16.0	59.3
#8	2.0	1.9	85.9	34.5	6.2	65.5
#16	1.4	1.4	69.6	27.8	6.7	72.2
#30	1.3	1.2	50.9	20.5	7.3	79.5
#50	1.2	1.2	22.4	9.4	11.1	90.6
#100	1.1	1.1	3.9	2.2	7.2	97.8
LBW	1.2	1.0	0.6	0.9	1.2	99.1

\*Maximum % Retained must be above the 3/8" sieve.  
 \*Any two adjacent sieves must equal 10% except max., nom. max., #100 and #200 sieves.  
 \*% Retained must be at least 4% for each sieve except max., nom. max., #100 and #200 sieves.  
 \*% Retained must be at least 4% for the 3/4" sieve when a 1.5" max. size (nom. Max. 1.0") aggregate is used.

Production Gradation  Batch Plant Gradations  Aggregate Supplier Gradations

**Coarseness Factor:** **66**      **Workability Factor:** **34**

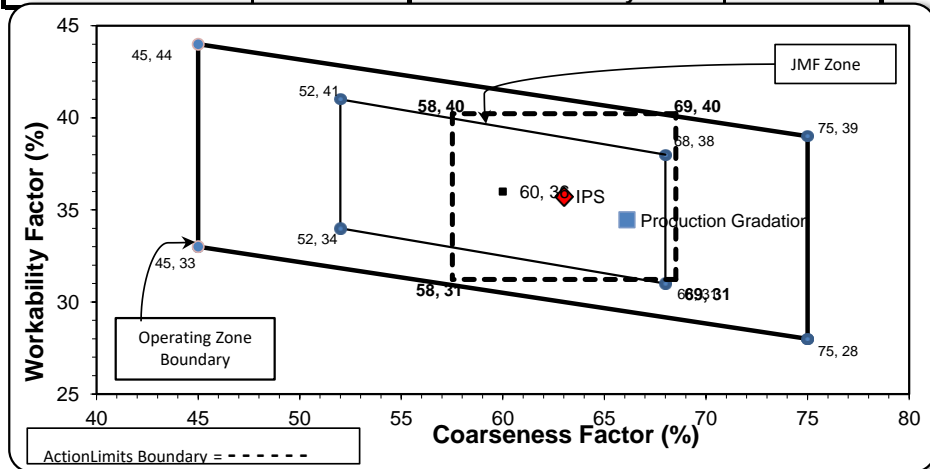

Initial Production Sample (IPS)

**Coarseness Factor:** **63**  
**Workability Factor:** **36**

Sieve	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	0.0	0.0
1.5"	100.0	0.0	0.0
1"	99.2	0.8	0.8
3/4"	90.9	8.3	9.1
1/2"	71.3	19.6	28.7
3/8"	59.5	11.8	40.5
#4	43.8	15.7	56.2
#8	35.7	8.1	64.3
#16	27.0	8.7	73.0
#30	18.6	8.4	81.4
#50	6.8	11.8	93.2
#100	1.4	5.4	98.6
LBW	0.6	0.8	99.4

PREPARED BY:  
 SM, LLC Technical Service

Approved BY:

# Aggregate Optimization Chart

**PLANT #:** 12

Sample Date: 9/9/24

Concrete Grade: **S2M, 3500HP**

Dates Test Represents: 9/10/2024 through 9/16/2024

Contractor: \_\_\_\_\_

MDOT No.: \_\_\_\_\_

Agg. Class	Pit #	Source	Weight (SSD)	ft <sup>3</sup>	Specific Gravity	% Contribution
6AA	71-47	Presque Isle	1470	8.99	2.62	48.2
26A	71-47	Presque Isle	350	2.14	2.62	11.5
2NS	63-115	Ray Rd	1230	7.44	2.65	40.3
<b>Total Wt</b>			<b>3050</b>	<b>18.57</b>		<b>100.0</b>

<----- Verify this number is 100%




**Superior Materials, LLC**  
 30701 W. 10 Mile Rd.  
 Suite 500  
 Farmington Hills, MI 48336

Sieve	6AA	26A	2NS	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	100.0	100.0	100.0	0.0	0.0
1.5"	100.0	100.0	100.0	100.0	0.0	0.0
1"	95.6	100.0	100.0	97.9	2.1	2.1
3/4"	69.6	100.0	100.0	85.3	12.5	14.7
1/2"	24.2	91.6	100.0	62.5	22.8	37.5
3/8"	10.7	77.6	100.0	54.4	8.1	45.6
#4	1.8	14.2	97.8	41.9	12.5	58.1
#8	1.5	3.3	79.1	33.0	8.9	67.0
#16	1.4	1.9	62.8	26.2	6.8	73.8
#30	1.4	1.6	46.9	19.8	6.4	80.2
#50	1.4	1.5	25.1	11.0	8.8	89.0
#100	1.3	1.4	6.1	3.2	7.7	96.8
LBW	0.9	1.3	0.7	0.9	2.4	99.1

\*Maximum % Retained must be above the 3/8" sieve.  
 \*Any two adjacent sieves must equal 10% except max., nom. max., #100 and #200 sieves.  
 \*% Retained must be at least 4% for each sieve except max., nom. max., #100 and #200 sieves.  
 \*% Retained must be at least 4% for the 3/4" sieve when a 1.5" max. size (nom. Max. 1.0") aggregate is used.

Production Gradation  Batch Plant Gradations  Aggregate Supplier Gradations

<b>Coarseness Factor:</b>	<b>68</b>	<b>Workability Factor:</b>	<b>33</b>
---------------------------	-----------	----------------------------	-----------

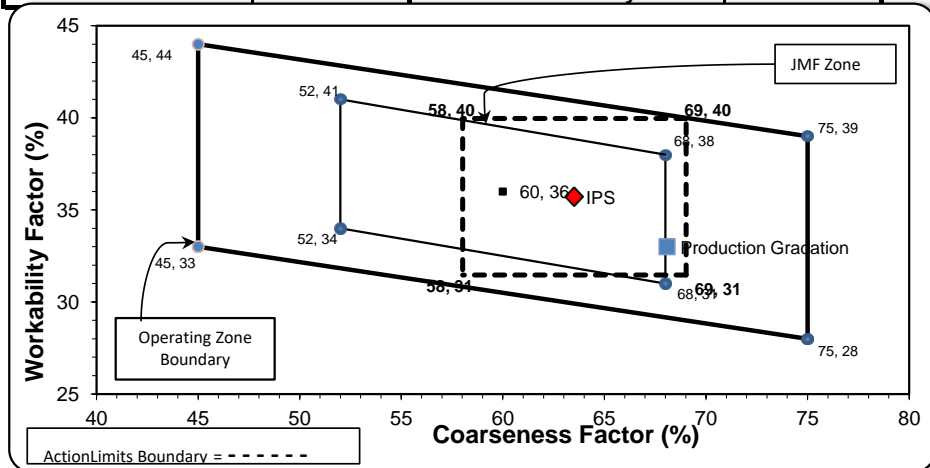

Initial Production Sample (IPS)

Sieve	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	0.0	0.0
1.5"	100.0	0.0	0.0
1"	99.2	0.8	0.8
3/4"	90.9	8.3	9.1
1/2"	71.3	19.6	28.7
3/8"	59.2	12.1	40.8
#4	41.5	17.7	58.5
#8	35.7	5.8	64.3
#16	27.9	7.9	72.1
#30	18.3	9.5	81.7
#50	7.3	11.0	92.7
#100	2.0	5.3	98.0
LBW	0.9	1.1	99.1

PREPARED BY:  
 SM, LLC Technical Service

Approved By:

# Aggregate Optimization Chart

**PLANT #:** p11

Sample Date: 9/9/24

Concrete Grade: **S2M, 3500HP**

Dates Test Represents: 9/10/2024 through 9/16/2024

Contractor: \_\_\_\_\_

MDOT No.: \_\_\_\_\_

Agg. Class	Pit #	Source	Weight (SSD)	ft <sup>3</sup>	Specific Gravity	% Contribution
6AA	71-47	Presque Isle	1420	8.69	2.62	46.6
26A	71-47	Presque Isle	400	2.45	2.62	13.1
2NS	63-115	Ray Rd	1230	7.44	2.65	40.3
<b>Total Wt</b>			<b>3050</b>	<b>18.57</b>		<b>100.0</b>

<----- Verify this number is 100%




**Superior Materials, LLC**  
 30701 W. 10 Mile Rd.  
 Suite 500  
 Farmington Hills, MI 48336

Sieve	6AA	26A	2NS	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	100.0	100.0	100.0	0.0	0.0
1.5"	100.0	100.0	100.0	100.0	0.0	0.0
1"	95.6	100.0	100.0	98.0	2.0	2.0
3/4"	69.6	100.0	100.0	85.8	12.1	14.2
1/2"	24.2	91.6	100.0	63.6	22.2	36.4
3/8"	10.7	77.6	100.0	55.5	8.1	44.5
#4	1.8	14.2	97.8	42.1	13.3	57.9
#8	1.5	3.3	79.1	33.0	9.1	67.0
#16	1.4	1.9	62.8	26.2	6.8	73.8
#30	1.4	1.6	46.9	19.8	6.5	80.2
#50	1.4	1.5	25.1	11.0	8.8	89.0
#100	1.3	1.4	6.1	3.2	7.7	96.8
LBW	0.9	1.3	0.7	0.9	2.4	99.1

\*Maximum % Retained must be above the 3/8" sieve.  
 \*Any two adjacent sieves must equal 10% except max., nom. max., #100 and #200 sieves.  
 \*% Retained must be at least 4% for each sieve except max., nom. max., #100 and #200 sieves.  
 \*% Retained must be at least 4% for the 3/4" sieve when a 1.5" max. size (nom. Max. 1.0") aggregate is used.

Production Gradation  Batch Plant Gradations  Aggregate Supplier Gradations

**Coarseness Factor:** 66      **Workability Factor:** 33

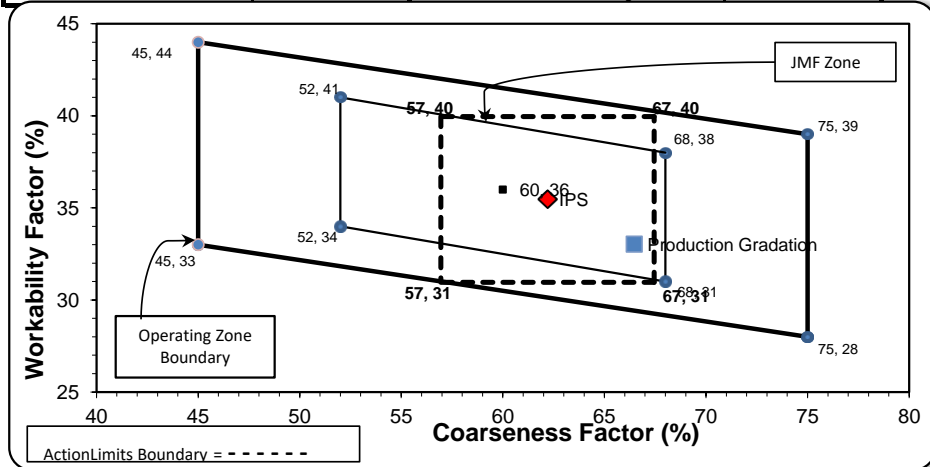

Initial Production Sample (IPS)

**Coarseness Factor:** 62  
**Workability Factor:** 35

Sieve	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	0.0	0.0
1.5"	100.0	0.0	0.0
1"	100.0	0.0	0.0
3/4"	94.0	6.0	6.0
1/2"	70.2	23.7	29.8
3/8"	59.9	10.4	40.1
#4	42.7	17.2	57.3
#8	35.5	7.2	64.5
#16	28.4	7.0	71.6
#30	19.2	9.2	80.8
#50	8.9	10.3	91.1
#100	3.1	5.9	96.9
LBW	1.4	1.7	98.6

PREPARED BY:  
 SM, LLC Technical Service

Approved By:

# Aggregate Optimization Chart

**PLANT #:** P-35

Sample Date: 9/9/24

Concrete Grade: **S2M, 3500HP**

Dates Test Represents: 9/10/2024 through 9/16/2024

Contractor: \_\_\_\_\_

MDOT No.: \_\_\_\_\_

Agg. Class	Pit #	Source	Weight (SSD)	ft <sup>3</sup>	Specific Gravity	% Contribution
6AA	58-003	Stoneco	1600	9.53	2.69	51.6
26A	58-003	Stoneco	300	1.79	2.69	9.7
2NS	81-019	Pleasant Lake	1200	7.26	2.65	38.7
<b>Total Wt</b>			<b>3100</b>	<b>18.58</b>		<b>100.0</b>

<----- Verify this number is 100%




**Superior Materials, LLC**  
 30701 W. 10 Mile Rd.  
 Suite 500  
 Farmington Hills, MI 48336

Sieve	6AA	26A	2NS	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	100.0	100.0	100.0	0.0	0.0
1.5"	100.0	100.0	100.0	100.0	0.0	0.0
1"	100.0	100.0	100.0	100.0	0.0	0.0
3/4"	86.0	100.0	100.0	92.8	7.2	7.2
1/2"	45.2	98.5	100.0	71.6	21.2	28.4
3/8"	18.5	87.0	100.0	56.7	14.9	43.3
#4	3.4	5.8	97.8	40.2	16.5	59.8
#8	2.0	1.9	84.0	33.7	6.4	66.3
#16	1.4	1.4	62.7	25.1	8.6	74.9
#30	1.3	1.2	40.6	16.5	8.6	83.5
#50	1.2	1.2	19.2	8.2	8.3	91.8
#100	1.1	1.1	3.7	2.1	6.1	97.9
LBW	1.2	1.0	0.6	0.9	1.2	99.1

\*Maximum % Retained must be above the 3/8" sieve.  
 \*Any two adjacent sieves must equal 10% except max., nom. max., #100 and #200 sieves.  
 \*% Retained must be at least 4% for each sieve except max., nom. max., #100 and #200 sieves.  
 \*% Retained must be at least 4% for the 3/4" sieve when a 1.5" max. size (nom. Max. 1.0") aggregate is used.

Production Gradation  Batch Plant Gradations  Aggregate Supplier Gradations

Coarseness Factor: 65      Workability Factor: 34

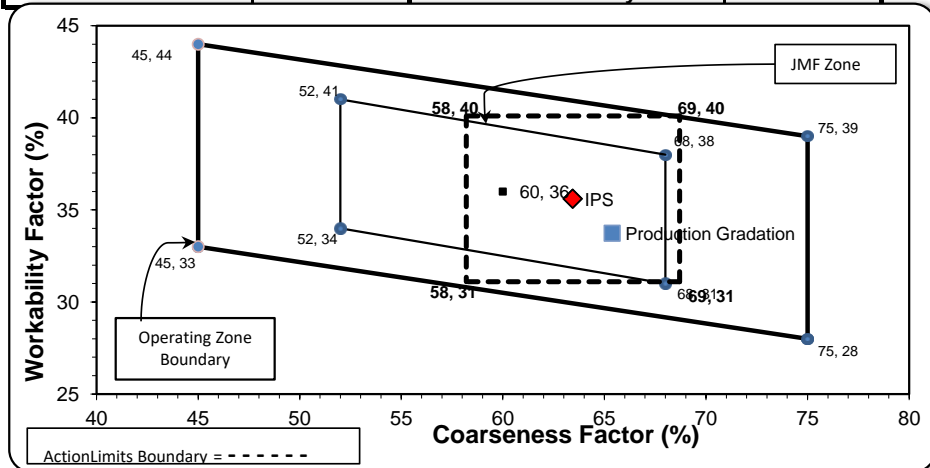

Initial Production Sample (IPS)

Coarseness Factor: 63  
 Workability Factor: 36

Sieve	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	0.0	0.0
1.5"	100.0	0.0	0.0
1"	100.0	0.0	0.0
3/4"	93.1	6.9	6.9
1/2"	70.0	23.1	30.0
3/8"	59.1	10.9	40.9
#4	46.0	13.1	54.0
#8	35.6	10.4	64.4
#16	27.2	8.4	72.8
#30	19.8	7.4	80.2
#50	10.1	9.7	89.9
#100	2.5	7.6	97.5
LBW	0.9	1.6	99.1

PREPARED BY:  
 SM, LLC Technical Service

Approved By:

# Aggregate Optimization Chart

**PLANT #:** **P-38**

Sample Date: 9/9/24

Concrete Grade: **S2M, 3500HP**

Dates Test Represents: 9/10/2024 through 9/16/2024

Contractor: \_\_\_\_\_

MDOT No.: \_\_\_\_\_

Agg. Class	Pit #	Source	Weight (SSD)	ft <sup>3</sup>	Specific Gravity	% Contribution
6AA	58-003	Stoneco	1600	9.53	2.69	51.6
26A	58-003	Stoneco	300	1.79	2.69	9.7
2NS	81-019	Pleasant Lake	1200	7.26	2.65	38.7
<b>Total Wt</b>			<b>3100</b>	<b>18.58</b>		<b>100.0</b>

<----- Verify this number is 100%




**Superior Materials, LLC**  
 30701 W. 10 Mile Rd.  
 Suite 500  
 Farmington Hills, MI 48336

Sieve	6AA	26A	2NS	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	100.0	100.0	100.0	0.0	0.0
1.5"	100.0	100.0	100.0	100.0	0.0	0.0
1"	100.0	100.0	100.0	100.0	0.0	0.0
3/4"	86.0	100.0	100.0	92.8	7.2	7.2
1/2"	45.2	98.5	100.0	71.6	21.2	28.4
3/8"	18.5	87.0	100.0	56.7	14.9	43.3
#4	3.4	5.8	97.8	40.2	16.5	59.8
#8	2.0	1.9	84.0	33.7	6.4	66.3
#16	1.4	1.4	62.7	25.1	8.6	74.9
#30	1.3	1.2	40.6	16.5	8.6	83.5
#50	1.2	1.2	19.2	8.2	8.3	91.8
#100	1.1	1.1	3.7	2.1	6.1	97.9
LBW	1.2	1.0	0.6	0.9	1.2	99.1

\*Maximum % Retained must be above the 3/8" sieve.  
 \*Any two adjacent sieves must equal 10% except max., nom. max., #100 and #200 sieves.  
 \*% Retained must be at least 4% for each sieve except max., nom. max., #100 and #200 sieves.  
 \*% Retained must be at least 4% for the 3/4" sieve when a 1.5" max. size (nom. Max. 1.0") aggregate is used.

Production Gradation  Batch Plant Gradations  Aggregate Supplier Gradations

<b>Coarseness Factor:</b>	<b>65</b>	<b>Workability Factor:</b>	<b>34</b>
---------------------------	-----------	----------------------------	-----------

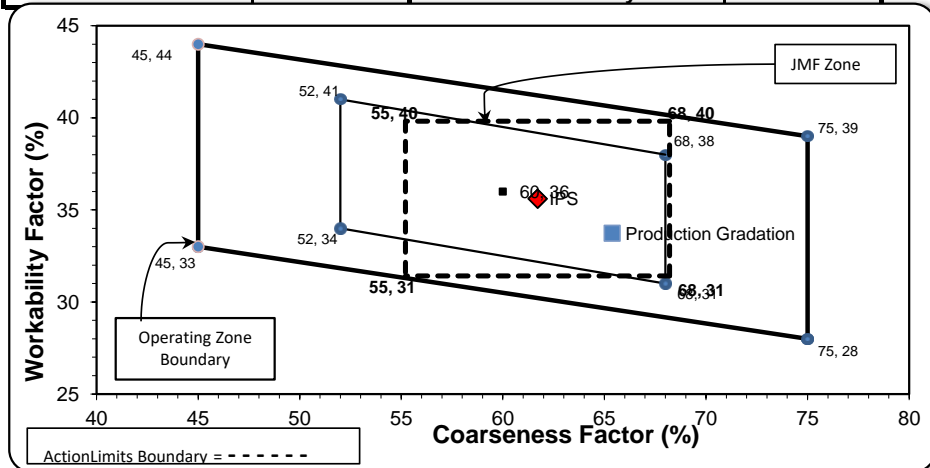

Initial Production Sample (IPS)

<b>Coarseness Factor:</b>	<b>62</b>		
<b>Workability Factor:</b>	<b>36</b>		
Sieve	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	0.0	0.0
1.5"	100.0	0.0	0.0
1"	99.2	0.8	0.8
3/4"	91.1	8.1	8.9
1/2"	72.0	19.1	28.0
3/8"	60.3	11.7	39.7
#4	43.4	16.9	56.6
#8	35.6	7.8	64.4
#16	28.4	7.2	71.6
#30	21.8	6.7	78.2
#50	9.1	12.6	90.9
#100	1.7	7.4	98.3
LBW	1.1	0.6	98.9

PREPARED BY:  
 SM, LLC Technical Service

Approved By:

# Aggregate Optimization Chart

**PLANT #:** P-02

Sample Date: 9/9/24

Concrete Grade: S2M, 3500HP

Dates Test Represents: 9/10/2024 through 9/16/2024

Contractor: \_\_\_\_\_

MDOT No.: \_\_\_\_\_



**Superior Materials, LLC**  
 30701 W. 10 Mile Rd.  
 Suite 500  
 Farmington Hills, MI 48336

Agg. Class	Pit #	Source	Weight (SSD)	ft <sup>3</sup>	Specific Gravity	% Contribution
6AA	71-47	Presque Isle	1470	8.99	2.62	48.2
26A	71-47	Presque Isle	350	2.14	2.62	11.5
2NS	63-115	Ray Rd	1230	7.44	2.65	40.3
<b>Total Wt</b>			<b>3050</b>	<b>18.57</b>		<b>100.0</b>


<----- Verify this number is 100%

Sieve	6AA	26A	2NS	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	100.0	100.0	100.0	0.0	0.0
1.5"	100.0	100.0	100.0	100.0	0.0	0.0
1"	95.6	100.0	100.0	97.9	2.1	2.1
3/4"	69.6	100.0	100.0	85.3	12.5	14.7
1/2"	24.2	91.6	100.0	62.5	22.8	37.5
3/8"	10.7	77.6	100.0	54.4	8.1	45.6
#4	1.8	14.2	97.8	41.9	12.5	58.1
#8	1.5	3.3	79.1	33.0	8.9	67.0
#16	1.4	1.9	62.8	26.2	6.8	73.8
#30	1.4	1.6	46.9	19.8	6.4	80.2
#50	1.4	1.5	25.1	11.0	8.8	89.0
#100	1.3	1.4	6.1	3.2	7.7	96.8
LBW	0.9	1.3	0.7	0.9	2.4	99.1

\*Maximum % Retained must be above the 3/8" sieve.  
 \*Any two adjacent sieves must equal 10% except max., nom. max., #100 and #200 sieves.  
 \*% Retained must be at least 4% for each sieve except max., nom. max., #100 and #200 sieves.  
 \*% Retained must be at least 4% for the 3/4" sieve when a 1.5" max. size (nom. Max. 1.0") aggregate is used.

Production Gradation  Batch Plant Gradations  Aggregate Supplier Gradations

**Coarseness Factor:** 68      **Workability Factor:** 33

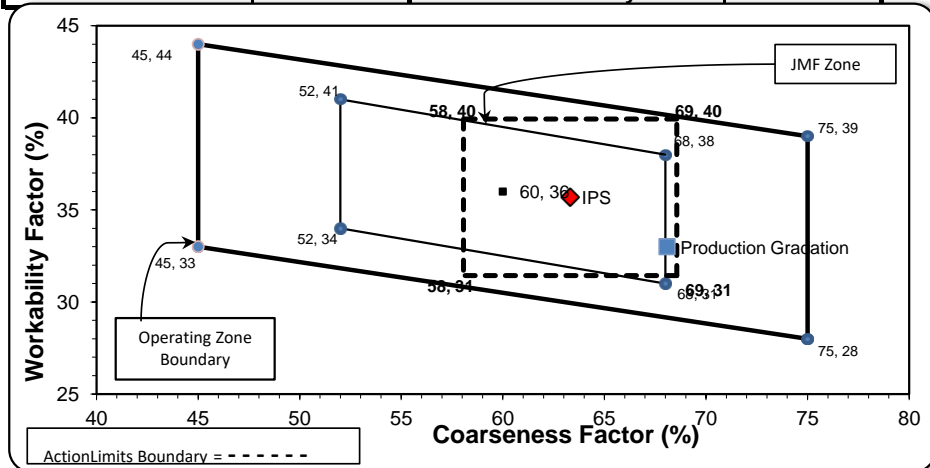

Intial Production Sample (IPS)

**Coarseness Factor:** 63  
**Workability Factor:** 36

Sieve	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	0.0	0.0
1.5"	100.0	0.0	0.0
1"	100.0	0.0	0.0
3/4"	95.6	4.4	4.4
1/2"	73.1	22.6	26.9
3/8"	59.3	13.8	40.7
#4	42.8	16.5	57.2
#8	35.7	7.1	64.3
#16	28.9	6.8	71.1
#30	20.7	8.2	79.3
#50	9.9	10.8	90.1
#100	2.1	7.8	97.9
LBW	0.9	1.2	99.1

PREPARED BY:  
 SM, LLC Technical Service

Approved By:
