

# Aggregate Optimization Chart

## Production Gradation Report

**PLANT #:** **P-101**

Sample Date: 4/20/20

Concrete Grade: **DM**

Contractor: \_\_\_\_\_

Dates Test Represents: 4/21/2020 through 4/27/2020

MDOT No.: \_\_\_\_\_

Agg. Class	Pit #	Source	Weight (SSD)	ft <sup>3</sup>	Specific Gravity	% Contribution
6AA	71-47	Presque Isle	1660	10.15	2.62	57.0
26A	71-47	Presque Isle	100	0.61	2.62	3.4
2NS	75-051	Mid-Michigan	1150	6.93	2.66	39.5
<b>Total Wt</b>			<b>2910</b>	<b>17.69</b>		<b>100.0</b>

<----- Verify this number is 100%



**Superior Materials, LLC**  
 30701 W. 10 Mile Rd.  
 Suite 500  
 Farmington Hills, MI 48336

Sieve	6AA	26A	2NS	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	100.0	100.0	100.0	0.0	0.0
1.5"	100.0	100.0	100.0	100.0	0.0	0.0
1"	100.0	100.0	100.0	100.0	0.0	0.0
3/4"	84.1	100.0	100.0	90.9	9.1	9.1
1/2"	41.7	100.0	100.0	66.7	24.2	33.3
3/8"	22.2	88.4	100.0	55.2	11.5	44.8
#4	4.4	23.9	96.7	41.5	13.7	58.5
#8	2.1	7.2	79.5	32.9	8.7	67.1
#16	1.9	3.7	64.8	26.8	6.0	73.2
#30	1.8	3.1	49.9	20.9	6.0	79.1
#50	1.8	2.8	27.5	12.0	8.9	88.0
#100	1.7	2.6	7.8	4.1	7.8	95.9
LBW	1.5	2.3	1.4	1.5	2.7	98.5

\*Maximum % Retained must be above the 3/8" sieve.  
 \*Any two adjacent sieves must equal 10% except max., nom. max., #100 and #200 sieves.  
 \*% Retained must be at least 4% for each sieve except max., nom. max., #100 and #200 sieves.  
 \*% Retained must be at least 8% for the 1" sieve when a 2" max. size (nom. Max. 1.5") aggregate is used.


Production Gradation  Batch Plant Gradations  Aggregate Supplier Gradations

Adjusted WF Initial Production Sample (IPS)

<b>Coarseness Factor:</b>	<b>67</b>	<b>Workability Factor:</b>	<b>33</b>	<b>Adjusted WF</b>	<b>35.4</b>
---------------------------	-----------	----------------------------	-----------	--------------------	-------------

<b>Coarseness Factor:</b>	<b>62</b>
<b>Workability Factor:</b>	<b>35</b>

Sieve	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	0.0	0.0
1.5"	100.0	0.0	0.0
1"	100.0	0.0	0.0
3/4"	95.0	5.0	5.0
1/2"	70.5	24.5	29.5
3/8"	60.0	10.5	40.0
#4	44.4	15.6	55.6
#8	35.5	9.0	64.5
#16	28.5	7.0	71.5
#30	21.5	7.0	78.5
#50	10.2	11.3	89.8
#100	3.1	7.1	96.9
LBW	1.3	1.8	98.7

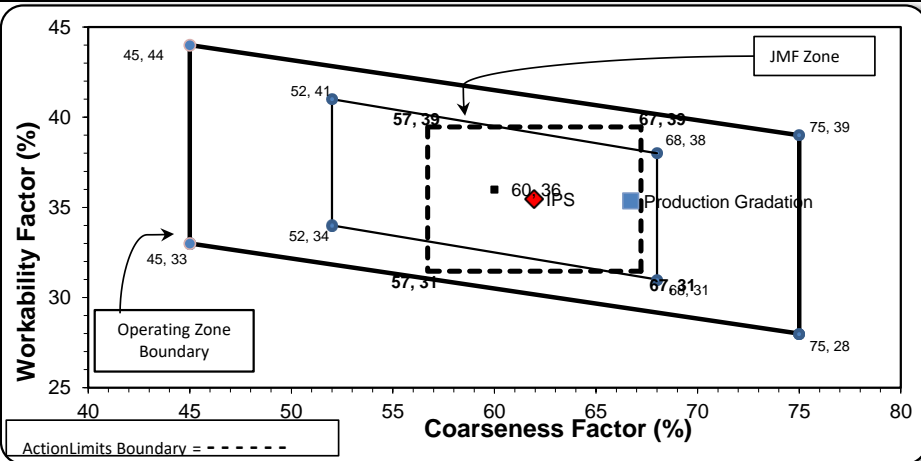

PREPARED BY:  
 SM, LLC Technical Service

Approved By:

# Aggregate Optimization Chart

**PLANT #:** **P-102**

Sample Date: 4/20/20

Concrete Grade: **DM**

Contractor: \_\_\_\_\_

Dates Test Represents: 4/21/2020 through 4/27/2020

MDOT No.: \_\_\_\_\_

Agg. Class	Pit #	Source	Weight (SSD)	ft <sup>3</sup>	Specific Gravity	% Contribution
6AA	58-003	Stoneco	1500	8.94	2.69	50.8
26A	58-003	Stoneco	305	1.82	2.69	10.3
2NS	63-114	Highland	1150	6.95	2.65	38.9
<b>Total Wt</b>			<b>2955</b>	<b>17.71</b>		<b>100.0</b>

<----- Verify this number is 100%



**Superior Materials, LLC**  
 30701 W. 10 Mile Rd.  
 Suite 500  
 Farmington Hills, MI 48336

Sieve	6AA	26A	2NS	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	100.0	100.0	100.0	0.0	0.0
1.5"	100.0	100.0	100.0	100.0	0.0	0.0
1"	100.0	100.0	100.0	100.0	0.0	0.0
3/4"	88.9	100.0	100.0	94.4	5.6	5.6
1/2"	49.7	99.5	100.0	74.4	20.0	25.6
3/8"	26.0	84.5	100.0	60.8	13.6	39.2
#4	4.3	18.2	99.0	42.6	18.2	57.4
#8	1.7	4.1	83.8	33.9	8.7	66.1
#16	1.4	2.0	65.7	26.5	7.4	73.5
#30	1.3	1.6	47.9	19.5	7.0	80.5
#50	1.1	1.5	24.4	10.2	9.3	89.8
#100	1.0	1.4	3.9	2.2	8.0	97.8
LBW	0.9	1.1	0.4	0.7	1.4	99.3


\*Maximum % Retained must be above the 3/8" sieve.  
 \*Any two adjacent sieves must equal 10% except max., nom. max., #100 and #200 sieves.  
 \*% Retained must be at least 4% for each sieve except max., nom. max., #100 and #200 sieves.  
 \*% Retained must be at least 8% for the 1" sieve when a 2" max. size (nom. Max. 1.5") aggregate is used.

Production Gradation  Batch Plant Gradations  Aggregate Supplier Gradations

Adjusted WF Initial Production Sample (IPS)

<b>Coarseness Factor:</b>	<b>59</b>	<b>Workability Factor:</b>	<b>34</b>	<b>36.4</b>	<b>Coarseness Factor:</b>	<b>61</b>
---------------------------	-----------	----------------------------	-----------	-------------	---------------------------	-----------

<b>Workability Factor:</b>	<b>36</b>
----------------------------	-----------

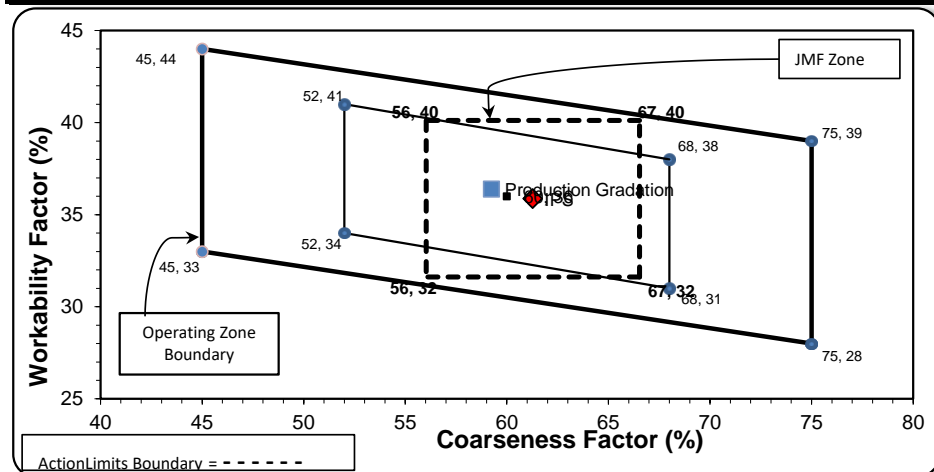

Sieve	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	0.0	0.0
1.5"	100.0	0.0	0.0
1"	99.3	0.7	0.7
3/4"	89.2	10.1	10.8
1/2"	70.7	18.5	29.3
3/8"	60.7	10.0	39.3
#4	44.4	16.3	55.6
#8	35.9	8.5	64.1
#16	27.3	8.6	72.7
#30	19.1	8.2	80.9
#50	7.4	11.7	92.6
#100	1.9	5.6	98.1
LBW	0.7	1.2	99.3

PREPARED BY:  
 SM, LLC Technical Service

Approved By:

# Aggregate Optimization Chart

**PLANT #:** **P-12**

Sample Date: 4/20/20

Concrete Grade: **DM**

Contractor: \_\_\_\_\_

Dates Test Represents: 4/21/2020 through 4/27/2020

MDOT No.: \_\_\_\_\_

Agg. Class	Pit #	Source	Weight (SSD)	ft <sup>3</sup>	Specific Gravity	% Contribution
6AA	71-47	Presque Isle	1555	9.51	2.62	53.5
26A	71-47	Presque Isle	200	1.22	2.62	6.9
2NS	63-115	Ray Rd	1150	6.95	2.65	39.6
<b>Total Wt</b>			<b>2905</b>	<b>17.69</b>		<b>100.0</b>

<----- Verify this number is 100%



**Superior Materials, LLC**  
 30701 W. 10 Mile Rd.  
 Suite 500  
 Farmington Hills, MI 48336

Sieve	6AA	26A	2NS	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	100.0	100.0	100.0	0.0	0.0
1.5"	100.0	100.0	100.0	100.0	0.0	0.0
1"	96.7	100.0	100.0	98.2	1.8	1.8
3/4"	76.0	100.0	100.0	87.2	11.1	12.8
1/2"	43.2	97.9	100.0	69.5	17.7	30.5
3/8"	25.2	90.3	100.0	59.3	10.2	40.7
#4	3.8	26.7	98.7	42.9	16.3	57.1
#8	2.2	8.0	80.1	33.4	9.5	66.6
#16	2.0	4.1	62.5	26.1	7.3	73.9
#30	1.9	3.4	46.7	19.7	6.4	80.3
#50	1.8	3.1	23.8	10.6	9.1	89.4
#100	1.6	2.9	4.9	3.0	7.6	97.0
LBW	1.2	2.1	0.6	1.0	2.0	99.0


\*Maximum % Retained must be above the 3/8" sieve.  
 \*Any two adjacent sieves must equal 10% except max., nom. max., #100 and #200 sieves.  
 \*% Retained must be at least 4% for each sieve except max., nom. max., #100 and #200 sieves.  
 \*% Retained must be at least 8% for the 1" sieve when a 2" max. size (nom. Max. 1.5") aggregate is used.

Production Gradation  Batch Plant Gradations  Aggregate Supplier Gradations

Adjusted WF Initial Production Sample (IPS)

Coarseness Factor: **61** Workability Factor: **33** Adjusted WF: **35.9**

Coarseness Factor: **63**  
 Workability Factor: **36**

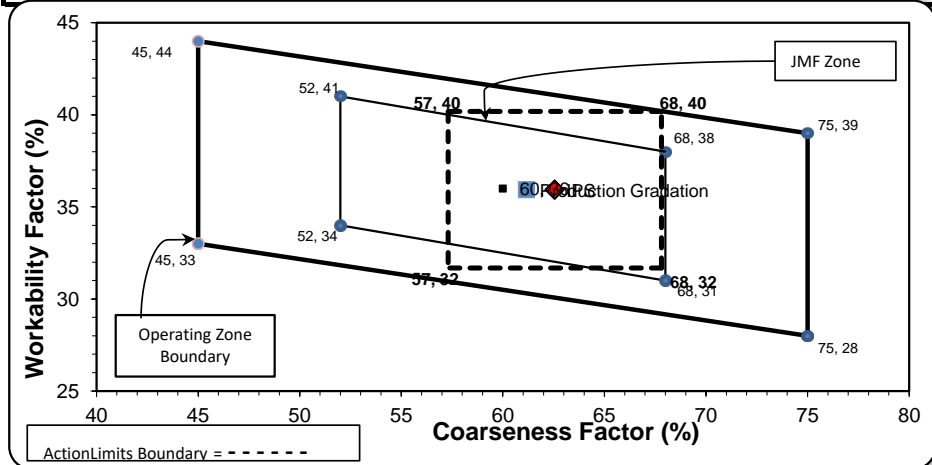

Sieve	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	0.0	0.0
1.5"	100.0	0.0	0.0
1"	99.3	0.7	0.7
3/4"	89.0	10.3	11.0
1/2"	70.3	18.7	29.7
3/8"	59.9	10.4	40.1
#4	41.9	18.0	58.1
#8	35.9	6.0	64.1
#16	27.8	8.2	72.2
#30	18.9	8.8	81.1
#50	6.3	12.6	93.7
#100	1.7	4.6	98.3
LBW	1.0	0.7	99.0

PREPARED BY:  
 SM, LLC Technical Service

Approved By:

# Aggregate Optimization Chart

**PLANT #:** **P-32**

Sample Date: 4/20/20

Concrete Grade: **DM**

Contractor: \_\_\_\_\_

Dates Test Represents: 4/21/2020 through 4/27/2020

MDOT No.: \_\_\_\_\_

Agg. Class	Pit #	Source	Weight (SSD)	ft <sup>3</sup>	Specific Gravity	% Contribution
6AA	71-47	Presque Isle	1450	8.87	2.62	49.9
26A	71-47	Presque Isle	305	1.87	2.62	10.5
2NS	63-115	Ray Rd	1150	6.95	2.65	39.6
<b>Total Wt</b>			<b>2905</b>	<b>17.69</b>		<b>100.0</b>

<----- Verify this number is 100%



**Superior Materials, LLC**  
 30701 W. 10 Mile Rd.  
 Suite 500  
 Farmington Hills, MI 48336

Sieve	6AA	26A	2NS	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	100.0	100.0	100.0	0.0	0.0
1.5"	100.0	100.0	100.0	100.0	0.0	0.0
1"	96.7	100.0	100.0	98.4	1.6	1.6
3/4"	77.9	100.0	100.0	89.0	9.4	11.0
1/2"	39.0	97.9	100.0	69.3	19.6	30.7
3/8"	21.7	90.3	100.0	59.9	9.4	40.1
#4	4.6	26.7	98.7	44.2	15.7	55.8
#8	2.9	8.0	80.1	34.0	10.2	66.0
#16	2.6	4.1	62.5	26.5	7.5	73.5
#30	2.5	3.4	46.7	20.1	6.4	79.9
#50	2.3	3.1	23.8	10.9	9.2	89.1
#100	2.1	2.9	4.9	3.3	7.6	96.7
LBW	1.7	2.1	0.6	1.3	2.0	98.7


\*Maximum % Retained must be above the 3/8" sieve.  
 \*Any two adjacent sieves must equal 10% except max., nom. max., #100 and #200 sieves.  
 \*% Retained must be at least 4% for each sieve except max., nom. max., #100 and #200 sieves.  
 \*% Retained must be at least 8% for the 1" sieve when a 2" max. size (nom. Max. 1.5") aggregate is used.

Production Gradation  Batch Plant Gradations  Aggregate Supplier Gradations

Adjusted WF Initial Production Sample (IPS)

<b>Coarseness Factor:</b>	<b>61</b>	<b>Workability Factor:</b>	<b>34</b>	<b>Adjusted WF</b>	<b>36.5</b>
---------------------------	-----------	----------------------------	-----------	--------------------	-------------

<b>Coarseness Factor:</b>	<b>62</b>
<b>Workability Factor:</b>	<b>36</b>

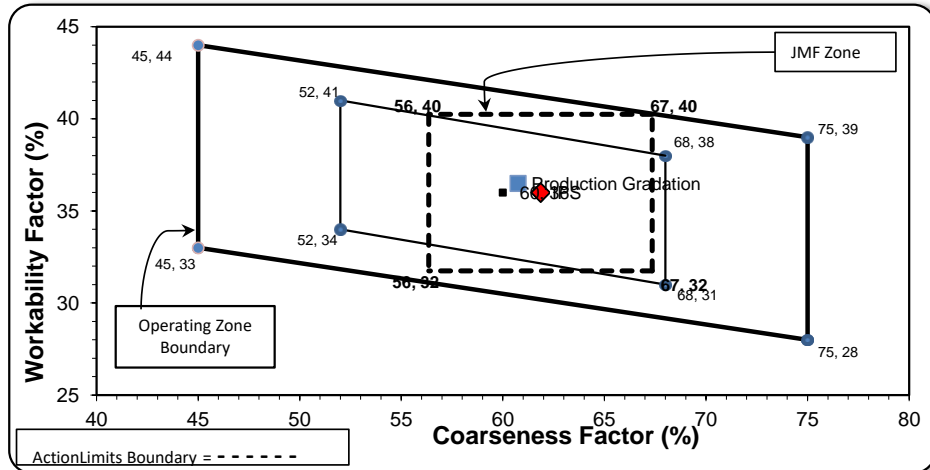

Sieve	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	0.0	0.0
1.5"	100.0	0.0	0.0
1"	100.0	0.0	0.0
3/4"	95.0	5.0	5.0
1/2"	72.3	22.8	27.7
3/8"	60.4	11.8	39.6
#4	42.6	17.8	57.4
#8	36.0	6.6	64.0
#16	29.5	6.5	70.5
#30	20.3	9.2	79.7
#50	9.5	10.8	90.5
#100	3.4	6.1	96.6
LBW	1.3	2.1	98.7

PREPARED BY:  
 SM, LLC Technical Service

Approved By:

# Aggregate Optimization Chart

**PLANT #:** **P-35**

Sample Date: 4/20/20

Concrete Grade: **DM**

Contractor: \_\_\_\_\_

Dates Test Represents: 4/21/2020 through 4/27/2020

MDOT No.: \_\_\_\_\_

Agg. Class	Pit #	Source	Weight (SSD)	ft <sup>3</sup>	Specific Gravity	% Contribution
6AA	58-003	Stoneco	1555	9.26	2.69	52.6
26A	58-003	Stoneco	300	1.79	2.69	10.2
2NS	81-093	Burmeister	1100	6.65	2.65	37.2
<b>Total Wt</b>			<b>2955</b>	<b>17.70</b>		<b>100.0</b>

<----- Verify this number is 100%



**Superior Materials, LLC**  
 30701 W. 10 Mile Rd.  
 Suite 500  
 Farmington Hills, MI 48336

Sieve	6AA	26A	2NS	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	100.0	100.0	100.0	0.0	0.0
1.5"	100.0	100.0	100.0	100.0	0.0	0.0
1"	100.0	100.0	100.0	100.0	0.0	0.0
3/4"	88.9	100.0	100.0	94.2	5.8	5.8
1/2"	49.7	99.5	100.0	73.5	20.7	26.5
3/8"	26.0	84.5	100.0	59.5	14.0	40.5
#4	4.3	18.2	97.5	40.4	19.1	59.6
#8	1.7	4.1	87.4	33.8	6.6	66.2
#16	1.4	2.0	60.5	23.5	10.4	76.5
#30	1.3	1.6	41.8	16.4	7.1	83.6
#50	1.1	1.5	17.2	7.1	9.3	92.9
#100	1.0	1.4	2.8	1.7	5.4	98.3
LBW	0.9	1.1	0.8	0.9	0.8	99.1


\*Maximum % Retained must be above the 3/8" sieve.  
 \*Any two adjacent sieves must equal 10% except max., nom. max., #100 and #200 sieves.  
 \*% Retained must be at least 4% for each sieve except max., nom. max., #100 and #200 sieves.  
 \*% Retained must be at least 8% for the 1" sieve when a 2" max. size (nom. Max. 1.5") aggregate is used.

Production Gradation  Batch Plant Gradations  Aggregate Supplier Gradations

Adjusted WF Initial Production Sample (IPS)

<b>Coarseness Factor:</b>	<b>61</b>	<b>Workability Factor:</b>	<b>34</b>	<b>36.3</b>
---------------------------	-----------	----------------------------	-----------	-------------

<b>Coarseness Factor:</b>	<b>61</b>
<b>Workability Factor:</b>	<b>36</b>

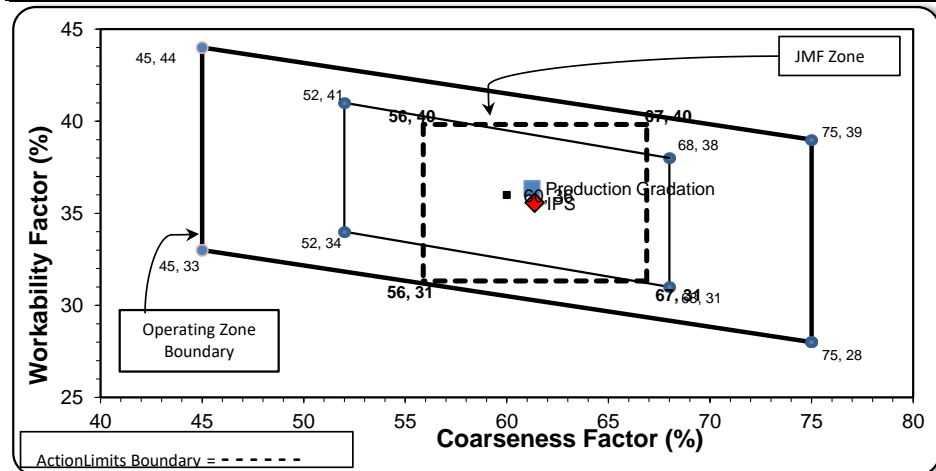

Sieve	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	0.0	0.0
1.5"	100.0	0.0	0.0
1"	99.3	0.7	0.7
3/4"	89.1	10.2	10.9
1/2"	70.5	18.6	29.5
3/8"	60.5	10.0	39.5
#4	44.1	16.4	55.9
#8	35.6	8.5	64.4
#16	27.7	7.9	72.3
#30	20.6	7.1	79.4
#50	8.7	11.8	91.3
#100	1.6	7.1	98.4
LBW	1.1	0.6	98.9

PREPARED BY:  
 SM, LLC Technical Service

Approved By:

# Aggregate Optimization Chart

**PLANT #:** **P-36**

Sample Date: 4/20/20

Concrete Grade: **DM**

Contractor: \_\_\_\_\_

Dates Test Represents: 4/21/2020 through 4/27/2020

MDOT No.: \_\_\_\_\_

Agg. Class	Pit #	Source	Weight (SSD)	ft <sup>3</sup>	Specific Gravity	% Contribution
6AA	71-47	Presque Isle	1600	9.79	2.62	55.1
26A	71-47	Presque Isle	205	1.25	2.62	7.1
2NS	63-92	Grange Hall	1100	6.65	2.65	37.9
<b>Total Wt</b>			<b>2905</b>	<b>17.69</b>		<b>100.0</b>

<----- Verify this number is 100%



**Superior Materials, LLC**  
 30701 W. 10 Mile Rd.  
 Suite 500  
 Farmington Hills, MI 48336

Sieve	6AA	26A	2NS	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	100.0	100.0	100.0	0.0	0.0
1.5"	100.0	100.0	100.0	100.0	0.0	0.0
1"	96.7	100.0	100.0	98.2	1.8	1.8
3/4"	76.0	100.0	100.0	86.8	11.4	13.2
1/2"	43.2	97.9	100.0	68.6	18.2	31.4
3/8"	25.2	90.3	100.0	58.1	10.5	41.9
#4	3.8	26.7	97.2	40.8	17.3	59.2
#8	2.2	8.0	84.8	33.9	6.9	66.1
#16	2.0	4.1	69.7	27.8	6.1	72.2
#30	1.9	3.4	50.7	20.5	7.3	79.5
#50	1.8	3.1	23.6	10.1	10.3	89.9
#100	1.6	2.9	3.9	2.6	7.6	97.4
LBW	1.2	2.1	0.5	1.0	1.6	99.0


\*Maximum % Retained must be above the 3/8" sieve.  
 \*Any two adjacent sieves must equal 10% except max., nom. max., #100 and #200 sieves.  
 \*% Retained must be at least 4% for each sieve except max., nom. max., #100 and #200 sieves.  
 \*% Retained must be at least 8% for the 1" sieve when a 2" max. size (nom. Max. 1.5") aggregate is used.

Production Gradation  Batch Plant Gradations  Aggregate Supplier Gradations

Adjusted WF Initial Production Sample (IPS)

<b>Coarseness Factor:</b>	<b>63</b>	<b>Workability Factor:</b>	<b>34</b>	<b>Adjusted WF</b>	<b>36.4</b>
---------------------------	-----------	----------------------------	-----------	--------------------	-------------

<b>Coarseness Factor:</b>	<b>63</b>
<b>Workability Factor:</b>	<b>35</b>

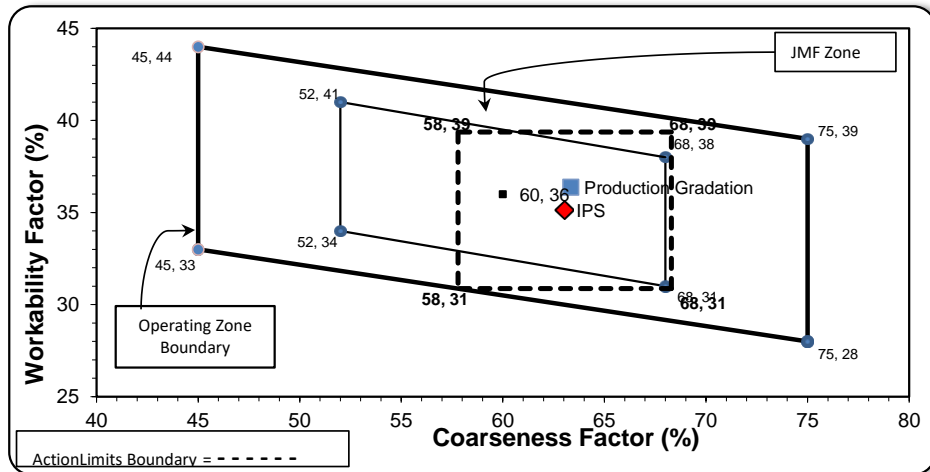

Sieve	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	0.0	0.0
1.5"	100.0	0.0	0.0
1"	99.1	0.9	0.9
3/4"	90.3	8.8	9.7
1/2"	69.2	21.1	30.8
3/8"	59.1	10.1	40.9
#4	41.8	17.3	58.2
#8	35.1	6.6	64.9
#16	28.5	6.6	71.5
#30	21.2	7.3	78.8
#50	8.7	12.5	91.3
#100	1.8	7.0	98.2
LBW	0.7	1.0	99.3

PREPARED BY:  
 SM, LLC Technical Service

Approved By:

# Aggregate Optimization Chart

**PLANT #:** **P-39**

Sample Date: 4/20/20 Concrete Grade: **DM**  
 Dates Test Represents: 4/21/2020 through 4/27/2020

Contractor: \_\_\_\_\_

MDOT No.: \_\_\_\_\_

Agg. Class	Pit #	Source	Weight (SSD)	ft <sup>3</sup>	Specific Gravity	% Contribution
6AA	71-47	Presque Isle	1605	9.82	2.62	55.2
26A	71-47	Presque Isle	200	1.22	2.62	6.9
2NS	63-92	Grange Hall	1100	6.65	2.65	37.9
<b>Total Wt</b>			<b>2905</b>	<b>17.69</b>		<b>100.0</b>

<----- Verify this number is 100%



**Superior Materials, LLC**  
 30701 W. 10 Mile Rd.  
 Suite 500  
 Farmington Hills, MI 48336


Sieve	6AA	26A	2NS	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	100.0	100.0	100.0	0.0	0.0
1.5"	100.0	100.0	100.0	100.0	0.0	0.0
1"	100.0	100.0	100.0	100.0	0.0	0.0
3/4"	84.1	100.0	100.0	91.2	8.8	8.8
1/2"	41.7	100.0	100.0	67.8	23.4	32.2
3/8"	22.2	88.4	100.0	56.2	11.6	43.8
#4	4.4	23.9	97.2	40.9	15.3	59.1
#8	2.1	7.2	84.8	33.8	7.1	66.2
#16	1.9	3.7	69.7	27.7	6.1	72.3
#30	1.8	3.1	50.7	20.4	7.3	79.6
#50	1.8	2.8	23.6	10.1	10.3	89.9
#100	1.7	2.6	3.9	2.6	7.5	97.4
LBW	1.5	2.3	0.5	1.2	1.4	98.8

\*Maximum % Retained must be above the 3/8" sieve.  
 \*Any two adjacent sieves must equal 10% except max., nom. max., #100 and #200 sieves.  
 \*% Retained must be at least 4% for each sieve except max., nom. max., #100 and #200 sieves.  
 \*% Retained must be at least 8% for the 1" sieve when a 2" max. size (nom. Max. 1.5") aggregate is used.

Production Gradation  Batch Plant Gradations  Aggregate Supplier Gradations  Adjusted WF Initial Production Sample (IPS)

<b>Coarseness Factor:</b>	<b>66</b>	<b>Workability Factor:</b>	<b>34</b>	<b>Adjusted WF</b>	<b>36.3</b>
---------------------------	-----------	----------------------------	-----------	--------------------	-------------

<b>Coarseness Factor:</b>	<b>63</b>
<b>Workability Factor:</b>	<b>36</b>

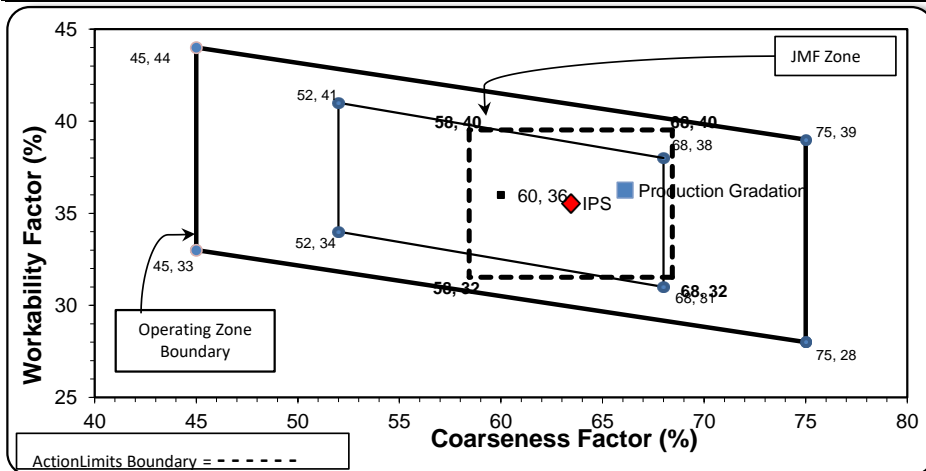

Sieve	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	0.0	0.0
1.5"	100.0	0.0	0.0
1"	100.0	0.0	0.0
3/4"	89.7	10.3	10.3
1/2"	70.3	19.4	29.7
3/8"	59.1	11.2	40.9
#4	42.8	16.3	57.2
#8	35.5	7.3	64.5
#16	29.0	6.5	71.0
#30	21.2	7.7	78.8
#50	9.8	11.5	90.2
#100	3.7	6.1	96.3
LBW	1.2	2.5	98.8

PREPARED BY:  
 SM, LLC Technical Service

Approved By:

# Aggregate Optimization Chart

**PLANT #:** **P-02**

Sample Date: 4/20/20

Concrete Grade: **DM**

Contractor: \_\_\_\_\_

Dates Test Represents: 4/21/2020 through 4/27/2020

MDOT No.: \_\_\_\_\_

Agg. Class	Pit #	Source	Weight (SSD)	ft <sup>3</sup>	Specific Gravity	% Contribution
6AA	71-47	Presque Isle	1555	9.51	2.62	53.5
26A	71-47	Presque Isle	200	1.22	2.62	6.9
2NS	63-115	Ray Rd	1150	6.95	2.65	39.6
<b>Total Wt</b>			<b>2905</b>	<b>17.69</b>		<b>100.0</b>

<----- Verify this number is 100%



**Superior Materials, LLC**  
 30701 W. 10 Mile Rd.  
 Suite 500  
 Farmington Hills, MI 48336

Sieve	6AA	26A	2NS	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	100.0	100.0	100.0	0.0	0.0
1.5"	100.0	100.0	100.0	100.0	0.0	0.0
1"	96.7	100.0	100.0	98.2	1.8	1.8
3/4"	76.0	100.0	100.0	87.2	11.1	12.8
1/2"	43.2	97.9	100.0	69.5	17.7	30.5
3/8"	25.2	90.3	100.0	59.3	10.2	40.7
#4	3.8	26.7	98.7	42.9	16.3	57.1
#8	2.2	8.0	80.1	33.4	9.5	66.6
#16	2.0	4.1	62.5	26.1	7.3	73.9
#30	1.9	3.4	46.7	19.7	6.4	80.3
#50	1.8	3.1	23.8	10.6	9.1	89.4
#100	1.6	2.9	4.9	3.0	7.6	97.0
LBW	1.2	2.1	0.6	1.0	2.0	99.0


\*Maximum % Retained must be above the 3/8" sieve.  
 \*Any two adjacent sieves must equal 10% except max., nom. max., #100 and #200 sieves.  
 \*% Retained must be at least 4% for each sieve except max., nom. max., #100 and #200 sieves.  
 \*% Retained must be at least 8% for the 1" sieve when a 2" max. size (nom. Max. 1.5") aggregate is used.

Production Gradation  Batch Plant Gradations  Aggregate Supplier Gradations

Adjusted WF Initial Production Sample (IPS)

<b>Coarseness Factor:</b>	<b>61</b>	<b>Workability Factor:</b>	<b>33</b>	<b>Adjusted WF</b>	<b>35.9</b>
---------------------------	-----------	----------------------------	-----------	--------------------	-------------

<b>Coarseness Factor:</b>	<b>63</b>
<b>Workability Factor:</b>	<b>35</b>

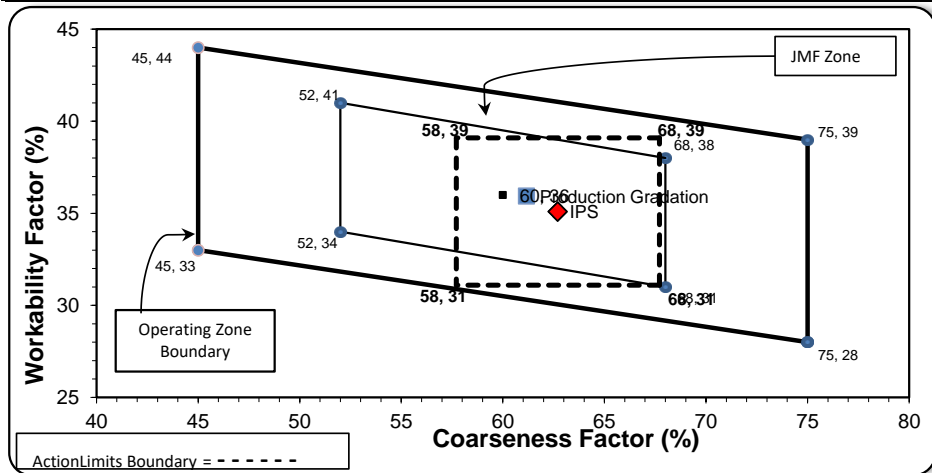

Sieve	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	0.0	0.0
1.5"	100.0	0.0	0.0
1"	100.0	0.0	0.0
3/4"	95.1	4.9	4.9
1/2"	74.6	20.5	25.4
3/8"	59.3	15.3	40.7
#4	42.1	17.2	57.9
#8	35.1	7.1	64.9
#16	29.2	5.9	70.8
#30	21.9	7.3	78.1
#50	9.6	12.4	90.4
#100	2.4	7.2	97.6
LBW	0.9	1.5	99.1

PREPARED BY:  
 SM, LLC Technical Service

Approved By:
