

Aggregate Optimization Chart

PLANT #: **P-101**

Sample Date: 10/3/22

Concrete Grade: **S2M, 3500HP**

Dates Test Represents: 10/4/2022 through 10/10/2022

Contractor: _____

MDOT No.: _____

Agg. Class	Pit #	Source	Weight (SSD)	ft ³	Specific Gravity	% Contribution
6AA	71-47	Presque Isle	1570	9.60	2.62	51.4
26A	71-47	Presque Isle	255	1.56	2.62	8.3
2NS	75-051	Mid Michigan	1230	7.41	2.66	40.3
Total Wt			3055	18.57		100.0

<---- Verify this number is 100%



Superior Materials, LLC
 30701 W. 10 Mile Rd.
 Suite 500
 Farmington Hills, MI 48336

Sieve	6AA	26A	2NS	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	100.0	100.0	100.0	0.0	0.0
1.5"	100.0	100.0	100.0	100.0	0.0	0.0
1"	97.9	100.0	100.0	98.9	1.1	1.1
3/4"	86.5	100.0	100.0	93.1	5.9	6.9
1/2"	48.4	94.1	100.0	73.0	20.1	27.0
3/8"	29.9	80.1	100.0	62.3	10.7	37.7
#4	5.5	23.7	99.0	44.7	17.6	55.3
#8	2.6	7.7	85.2	36.3	8.4	63.7
#16	2.1	4.1	69.1	29.2	7.0	70.8
#30	1.9	3.2	51.2	21.9	7.4	78.1
#50	1.8	2.9	23.0	10.4	11.4	89.6
#100	1.7	2.7	5.8	3.4	7.0	96.6
LBW	1.6	2.5	1.0	1.4	2.0	98.6


*Maximum % Retained must be above the 3/8" sieve.
 *Any two adjacent sieves must equal 10% except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 4% for each sieve except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 8% for the 1" sieve when a 2" max. size (nom. Max. 1.5") aggregate is used.

Production Gradation Batch Plant Gradations Aggregate Supplier Gradations

Coarseness Factor:	59	Workability Factor:	36
---------------------------	-----------	----------------------------	-----------

Initial Production Sample (IPS)

Coarseness Factor:	64		
Workability Factor:	35		
Sieve	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	0.0	0.0
1.5"	100.0	0.0	0.0
1"	100.0	0.0	0.0
3/4"	93.9	6.1	6.1
1/2"	71.4	22.5	28.6
3/8"	59.0	12.4	41.0
#4	45.1	13.9	54.9
#8	35.5	9.6	64.5
#16	28.3	7.2	71.7
#30	21.3	6.9	78.7
#50	11.0	10.3	89.0
#100	3.4	7.6	96.6
LBW	1.1	2.3	98.9

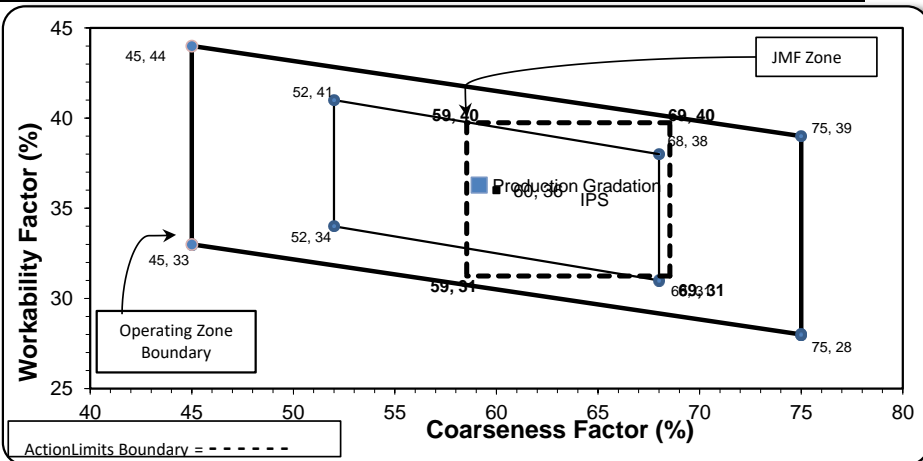

PREPARED BY:
 SM, LLC Technical Service

Approved By:

Aggregate Optimization Chart

PLANT #: **P-102**

Sample Date: 10/3/22

Concrete Grade: **S2M, 3500HP**

Dates Test Represents: 10/4/2022 through 10/10/2022

Contractor: _____

MDOT No.: _____

Agg. Class	Pit #	Source	Weight (SSD)	ft ³	Specific Gravity	% Contribution
6AA	58-003	Stoneco	1650	9.83	2.69	53.2
26A	58-003	Stoneco	250	1.49	2.69	8.1
2NS	81-019	Pleasant Lake	1200	7.26	2.65	38.7
Total Wt			3100	18.58		100.0

<----- Verify this number is 100%




Superior Materials, LLC
 30701 W. 10 Mile Rd.
 Suite 500
 Farmington Hills, MI 48336

Sieve	6AA	26A	2NS	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	100.0	100.0	100.0	0.0	0.0
1.5"	100.0	100.0	100.0	100.0	0.0	0.0
1"	99.7	100.0	100.0	99.8	0.2	0.2
3/4"	88.1	100.0	100.0	93.7	6.2	6.3
1/2"	49.8	99.8	100.0	73.3	20.4	26.7
3/8"	26.2	84.4	100.0	59.5	13.8	40.5
#4	5.4	20.3	98.9	42.8	16.7	57.2
#8	2.7	5.6	83.2	34.1	8.7	65.9
#16	2.7	3.1	65.5	27.0	7.1	73.0
#30	2.3	2.4	47.2	19.7	7.4	80.3
#50	2.0	2.3	23.9	10.5	9.2	89.5
#100	1.6	2.2	7.3	3.9	6.6	96.1
LBW	1.0	2.0	1.4	1.2	2.6	98.8

*Maximum % Retained must be above the 3/8" sieve.
 *Any two adjacent sieves must equal 10% except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 4% for each sieve except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 8% for the 1" sieve when a 2" max. size (nom. Max. 1.5") aggregate is used.

Production Gradation Batch Plant Gradations Aggregate Supplier Gradations

Coarseness Factor:	62	Workability Factor:	34
---------------------------	-----------	----------------------------	-----------

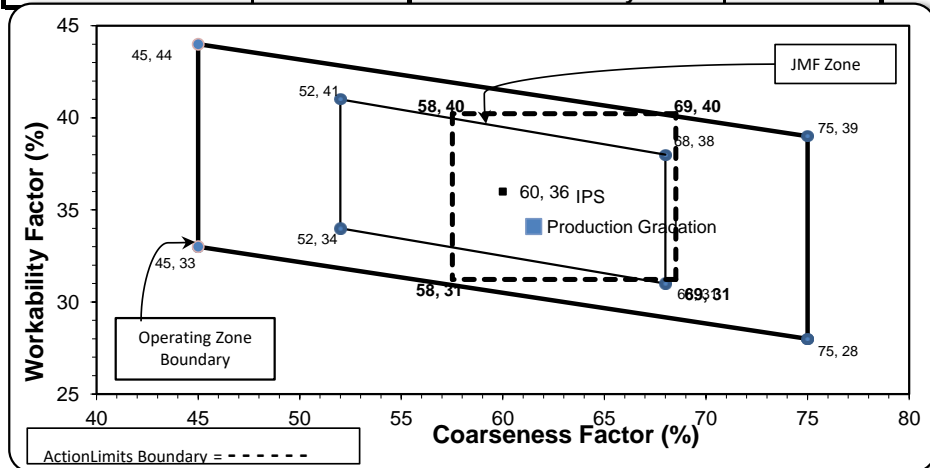

Initial Production Sample (IPS)

Coarseness Factor:	63
Workability Factor:	36

Sieve	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	0.0	0.0
1.5"	100.0	0.0	0.0
1"	99.2	0.8	0.8
3/4"	90.9	8.3	9.1
1/2"	71.3	19.6	28.7
3/8"	59.5	11.8	40.5
#4	43.8	15.7	56.2
#8	35.7	8.1	64.3
#16	27.0	8.7	73.0
#30	18.6	8.4	81.4
#50	6.8	11.8	93.2
#100	1.4	5.4	98.6
LBW	0.6	0.8	99.4

PREPARED BY:
 SM, LLC Technical Service

Approved By:

Aggregate Optimization Chart

PLANT #: **P-103**

Sample Date: 10/3/22

Concrete Grade: **S2M, 3500HP**

Dates Test Represents: 10/4/2022 through 10/10/2022

Contractor: _____

MDOT No.: _____

Agg. Class	Pit #	Source	Weight (SSD)	ft ³	Specific Gravity	% Contribution
6AA	58-003	Stoneco	1650	9.83	2.69	53.2
26A	58-003	Stoneco	250	1.49	2.69	8.1
2NS	81-019	Pleasant Lake	1200	7.26	2.65	38.7
Total Wt			3100	18.58		100.0

<----- Verify this number is 100%




Superior Materials, LLC
 30701 W. 10 Mile Rd.
 Suite 500
 Farmington Hills, MI 48336

Sieve	6AA	26A	2NS	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	100.0	100.0	100.0	0.0	0.0
1.5"	100.0	100.0	100.0	100.0	0.0	0.0
1"	99.7	100.0	100.0	99.8	0.2	0.2
3/4"	88.1	100.0	100.0	93.7	6.2	6.3
1/2"	49.8	99.8	100.0	73.3	20.4	26.7
3/8"	26.2	84.4	100.0	59.5	13.8	40.5
#4	5.4	20.3	98.9	42.8	16.7	57.2
#8	2.7	5.6	83.2	34.1	8.7	65.9
#16	2.7	3.1	65.5	27.0	7.1	73.0
#30	2.3	2.4	47.2	19.7	7.4	80.3
#50	2.0	2.3	23.9	10.5	9.2	89.5
#100	1.6	2.2	7.3	3.9	6.6	96.1
LBW	1.0	2.0	1.4	1.2	2.6	98.8

*Maximum % Retained must be above the 3/8" sieve.
 *Any two adjacent sieves must equal 10% except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 4% for each sieve except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 8% for the 1" sieve when a 2" max. size (nom. Max. 1.5") aggregate is used.

Production Gradation Batch Plant Gradations Aggregate Supplier Gradations

Coarseness Factor:	62	Workability Factor:	34
---------------------------	-----------	----------------------------	-----------

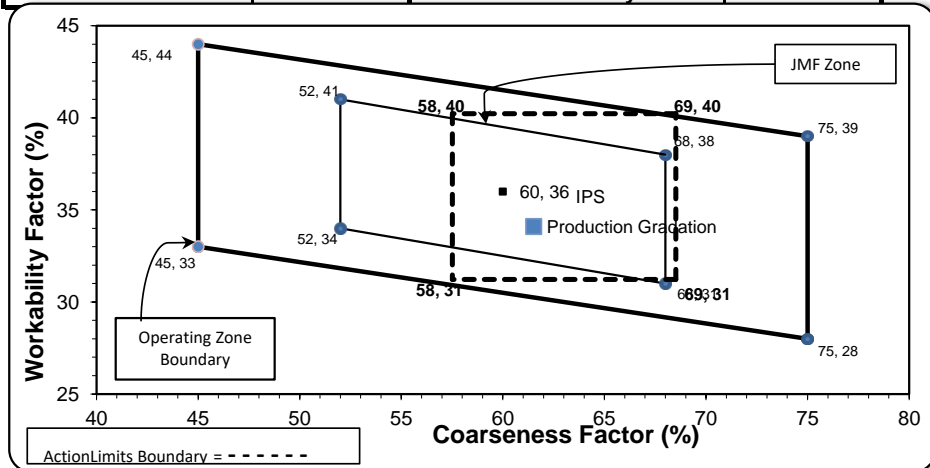

Initial Production Sample (IPS)

Coarseness Factor:	63		
Workability Factor:	36		
Sieve	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	0.0	0.0
1.5"	100.0	0.0	0.0
1"	99.2	0.8	0.8
3/4"	90.9	8.3	9.1
1/2"	71.3	19.6	28.7
3/8"	59.5	11.8	40.5
#4	43.8	15.7	56.2
#8	35.7	8.1	64.3
#16	27.0	8.7	73.0
#30	18.6	8.4	81.4
#50	6.8	11.8	93.2
#100	1.4	5.4	98.6
LBW	0.6	0.8	99.4

PREPARED BY:
 SM, LLC Technical Service

Approved BY:

Aggregate Optimization Chart

PLANT #: **P-14**

Sample Date: 10/3/22

Concrete Grade: **S2M, 3500HP**

Dates Test Represents: 10/4/2022 through 10/10/2022

Contractor: _____

MDOT No.: _____

Agg. Class	Pit #	Source	Weight (SSD)	ft ³	Specific Gravity	% Contribution
6AA	58-003	Stoneco	1620	9.65	2.69	52.1
26A	58-003	Stoneco	280	1.67	2.69	9.0
2NS	19-55	Schlegel	1210	7.26	2.67	38.9
Total Wt			3110	18.58		100.0

<----- Verify this number is 100%




Builders Redi-Mix
 30701 W. 10 Mile Rd.
 Suite 500
 Farmington Hills, MI 48336

Sieve	6AA	26A	2NS	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	100.0	100.0	100.0	0.0	0.0
1.5"	100.0	100.0	100.0	100.0	0.0	0.0
1"	99.7	100.0	100.0	99.8	0.2	0.2
3/4"	88.1	100.0	100.0	93.8	6.0	6.2
1/2"	49.8	99.8	100.0	73.8	20.0	26.2
3/8"	26.2	84.4	100.0	60.2	13.7	39.8
#4	5.4	20.3	100.0	43.5	16.6	56.5
#8	2.7	5.6	91.3	37.4	6.1	62.6
#16	2.7	3.1	71.6	29.5	7.9	70.5
#30	2.3	2.4	47.8	20.0	9.5	80.0
#50	2.0	2.3	15.8	7.4	12.6	92.6
#100	1.6	2.2	3.2	2.3	5.1	97.7
LBW	1.0	2.0	0.5	0.9	1.4	99.1

*Maximum % Retained must be above the 3/8" sieve.
 *Any two adjacent sieves must equal 10% except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 4% for each sieve except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 8% for the 1" sieve when a 2" max. size (nom. Max. 1.5") aggregate is used.

Production Gradation Batch Plant Gradations Aggregate Supplier Gradations

Coarseness Factor:	64	Workability Factor:	37
---------------------------	-----------	----------------------------	-----------

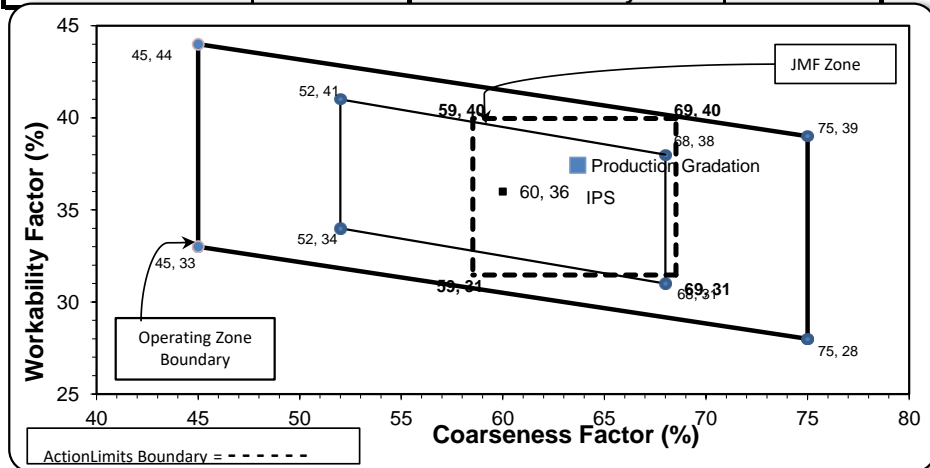

Initial Production Sample (IPS)

Coarseness Factor:	64		
Workability Factor:	36		
Sieve	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	0.0	0.0
1.5"	100.0	0.0	0.0
1"	99.2	0.8	0.8
3/4"	90.9	8.3	9.1
1/2"	71.3	19.6	28.7
3/8"	59.2	12.1	40.8
#4	41.5	17.7	58.5
#8	35.7	5.8	64.3
#16	27.9	7.9	72.1
#30	18.3	9.5	81.7
#50	7.3	11.0	92.7
#100	2.0	5.3	98.0
LBW	0.9	1.1	99.1

PREPARED BY:
 SM, LLC Technical Service

Approved By:

Aggregate Optimization Chart

PLANT #: 11

Sample Date: 10/3/22

Concrete Grade: **S2M, 3500HP**

Dates Test Represents: 10/4/2022 through 10/10/2022

Contractor: _____

MDOT No.: _____

Agg. Class	Pit #	Source	Weight (SSD)	ft ³	Specific Gravity	% Contribution
6AA	71-47	Presque Isle	1420	8.69	2.62	46.6
26A	71-47	Presque Isle	400	2.45	2.62	13.1
2NS	95-013	Smelter Bay	1230	7.44	2.65	40.3
Total Wt			3050	18.57		100.0

<----- Verify this number is 100%




Superior Materials, LLC
 30701 W. 10 Mile Rd.
 Suite 500
 Farmington Hills, MI 48336

Sieve	6AA	26A	2NS	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	100.0	100.0	100.0	0.0	0.0
1.5"	100.0	100.0	100.0	100.0	0.0	0.0
1"	99.2	100.0	100.0	99.6	0.4	0.4
3/4"	83.4	100.0	100.0	92.3	7.4	7.7
1/2"	41.9	96.5	100.0	72.5	19.8	27.5
3/8"	20.5	88.3	100.0	61.5	11.0	38.5
#4	3.7	27.7	96.1	44.1	17.3	55.9
#8	2.1	8.2	84.4	36.1	8.0	63.9
#16	1.9	3.4	69.8	29.5	6.6	70.5
#30	1.8	2.6	50.8	21.7	7.8	78.3
#50	1.7	2.4	24.9	11.1	10.5	88.9
#100	1.6	2.2	7.3	4.0	7.2	96.0
LBW	1.3	1.9	1.4	1.4	2.6	98.6

*Maximum % Retained must be above the 3/8" sieve.
 *Any two adjacent sieves must equal 10% except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 4% for each sieve except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 8% for the 1" sieve when a 2" max. size (nom. Max. 1.5") aggregate is used.

Production Gradation Batch Plant Gradations Aggregate Supplier Gradations

Coarseness Factor: 60 **Workability Factor:** 36

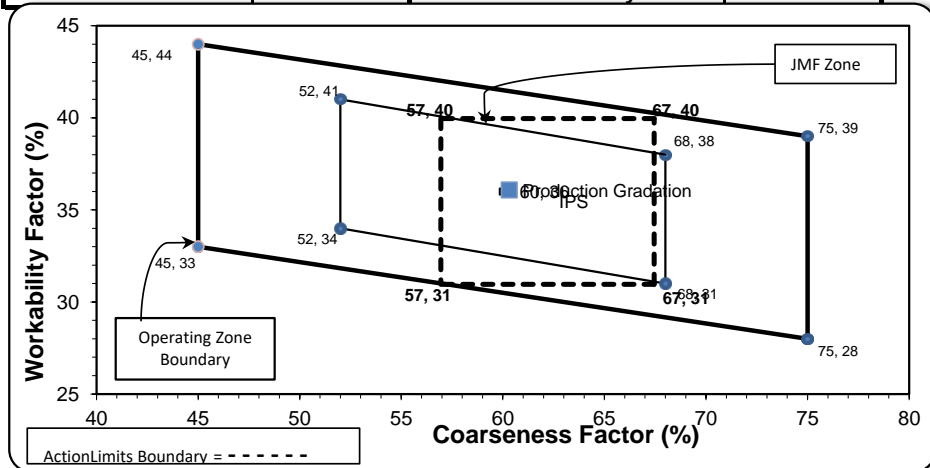

Initial Production Sample (IPS)

Coarseness Factor: 62
Workability Factor: 35

Sieve	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	0.0	0.0
1.5"	100.0	0.0	0.0
1"	100.0	0.0	0.0
3/4"	94.0	6.0	6.0
1/2"	70.2	23.7	29.8
3/8"	59.9	10.4	40.1
#4	42.7	17.2	57.3
#8	35.5	7.2	64.5
#16	28.4	7.0	71.6
#30	19.2	9.2	80.8
#50	8.9	10.3	91.1
#100	3.1	5.9	96.9
LBW	1.4	1.7	98.6

PREPARED BY:
 SM, LLC Technical Service

Approved By:

Aggregate Optimization Chart

PLANT #: **P-32**

Sample Date: 10/3/22

Concrete Grade: **S2M, 3500HP**

Dates Test Represents: 10/4/2022 through 10/10/2022

Contractor: _____

MDOT No.: _____

Agg. Class	Pit #	Source	Weight (SSD)	ft ³	Specific Gravity	% Contribution
6AA	71-47	Presque Isle	1420	8.69	2.62	46.6
26A	71-47	Presque Isle	400	2.45	2.62	13.1
2NS	95-013	Smelter Bay	1230	7.44	2.65	40.3
Total Wt			3050	18.57		100.0

<----- Verify this number is 100%




Superior Materials, LLC
 30701 W. 10 Mile Rd.
 Suite 500
 Farmington Hills, MI 48336

Sieve	6AA	26A	2NS	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	100.0	100.0	100.0	0.0	0.0
1.5"	100.0	100.0	100.0	100.0	0.0	0.0
1"	99.2	100.0	100.0	99.6	0.4	0.4
3/4"	83.4	100.0	100.0	92.3	7.4	7.7
1/2"	41.9	96.5	100.0	72.5	19.8	27.5
3/8"	20.5	88.3	100.0	61.5	11.0	38.5
#4	3.7	27.7	96.1	44.1	17.3	55.9
#8	2.1	8.2	84.4	36.1	8.0	63.9
#16	1.9	3.4	69.8	29.5	6.6	70.5
#30	1.8	2.6	50.8	21.7	7.8	78.3
#50	1.7	2.4	24.9	11.1	10.5	88.9
#100	1.6	2.2	7.3	4.0	7.2	96.0
LBW	1.3	1.9	1.4	1.4	2.6	98.6

*Maximum % Retained must be above the 3/8" sieve.
 *Any two adjacent sieves must equal 10% except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 4% for each sieve except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 8% for the 1" sieve when a 2" max. size (nom. Max. 1.5") aggregate is used.

Production Gradation Batch Plant Gradations Aggregate Supplier Gradations

Coarseness Factor: **60** **Workability Factor:** **36**

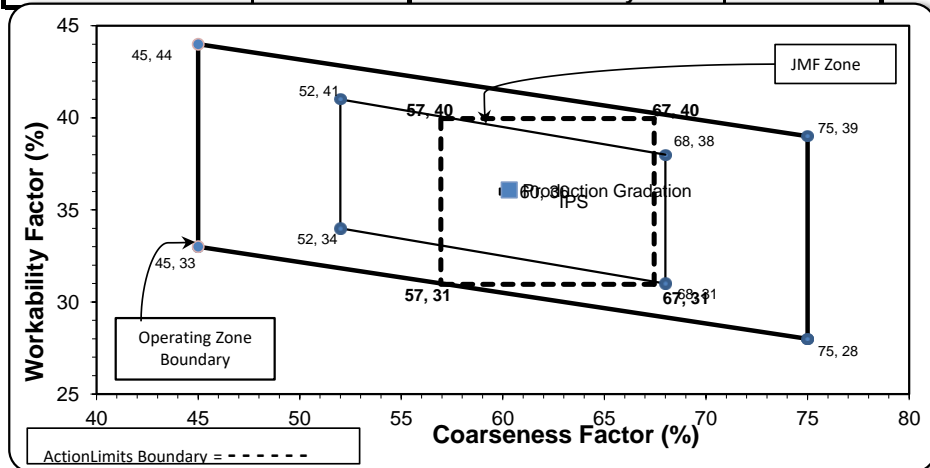

Initial Production Sample (IPS)

Coarseness Factor: **62**
Workability Factor: **35**

Sieve	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	0.0	0.0
1.5"	100.0	0.0	0.0
1"	100.0	0.0	0.0
3/4"	94.0	6.0	6.0
1/2"	70.2	23.7	29.8
3/8"	59.9	10.4	40.1
#4	42.7	17.2	57.3
#8	35.5	7.2	64.5
#16	28.4	7.0	71.6
#30	19.2	9.2	80.8
#50	8.9	10.3	91.1
#100	3.1	5.9	96.9
LBW	1.4	1.7	98.6

PREPARED BY:
 SM, LLC Technical Service

Approved By:

Aggregate Optimization Chart

PLANT #: **P-35**

Sample Date: 10/3/22

Concrete Grade: **S2M, 3500HP**

Dates Test Represents: 10/4/2022 through 10/10/2022

Contractor: _____

MDOT No.: _____

Agg. Class	Pit #	Source	Weight (SSD)	ft ³	Specific Gravity	% Contribution
6AA	58-003	Stoneco	1650	9.83	2.69	53.2
26A	58-003	Stoneco	250	1.49	2.69	8.1
2NS	81-019	Pleasant Lake	1200	7.26	2.65	38.7
Total Wt			3100	18.58		100.0

<----- Verify this number is 100%




Superior Materials, LLC
 30701 W. 10 Mile Rd.
 Suite 500
 Farmington Hills, MI 48336

Sieve	6AA	26A	2NS	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	100.0	100.0	100.0	0.0	0.0
1.5"	100.0	100.0	100.0	100.0	0.0	0.0
1"	99.7	100.0	100.0	99.8	0.2	0.2
3/4"	88.1	100.0	100.0	93.7	6.2	6.3
1/2"	49.8	99.8	100.0	73.3	20.4	26.7
3/8"	26.2	84.4	100.0	59.5	13.8	40.5
#4	5.4	20.3	98.9	42.8	16.7	57.2
#8	2.7	5.6	83.2	34.1	8.7	65.9
#16	2.7	3.1	65.5	27.0	7.1	73.0
#30	2.3	2.4	47.2	19.7	7.4	80.3
#50	2.0	2.3	23.9	10.5	9.2	89.5
#100	1.6	2.2	7.3	3.9	6.6	96.1
LBW	1.0	2.0	1.4	1.2	2.6	98.8

*Maximum % Retained must be above the 3/8" sieve.
 *Any two adjacent sieves must equal 10% except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 4% for each sieve except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 8% for the 1" sieve when a 2" max. size (nom. Max. 1.5") aggregate is used.

Production Gradation Batch Plant Gradations Aggregate Supplier Gradations

Coarseness Factor:	62	Workability Factor:	34
---------------------------	-----------	----------------------------	-----------

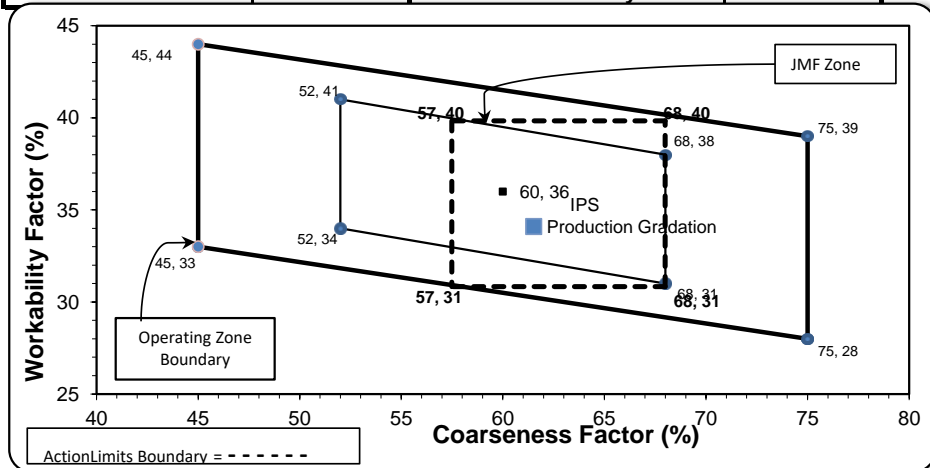

Initial Production Sample (IPS)

Coarseness Factor:	63		
Workability Factor:	35		
Sieve	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	0.0	0.0
1.5"	100.0	0.0	0.0
1"	99.2	0.8	0.8
3/4"	90.9	8.3	9.1
1/2"	71.3	19.6	28.7
3/8"	59.4	11.9	40.6
#4	43.0	16.5	57.0
#8	35.3	7.6	64.7
#16	28.2	7.1	71.8
#30	21.6	6.6	78.4
#50	9.1	12.5	90.9
#100	1.7	7.4	98.3
LBW	1.1	0.6	98.9

PREPARED BY:
 SM, LLC Technical Service

Approved By:

Aggregate Optimization Chart

PLANT #: **P-36**

Sample Date: 10/3/22

Concrete Grade: **S2M, 3500HP**

Dates Test Represents: 10/4/2022 through 10/10/2022

Contractor: _____

MDOT No.: _____

Agg. Class	Pit #	Source	Weight (SSD)	ft ³	Specific Gravity	% Contribution
6AA	71-47	Presque Isle	1550	9.48	2.62	50.8
26A	71-47	Presque Isle	300	1.83	2.62	9.8
2NS	63-92	Grange Hall	1200	7.26	2.65	39.3
Total Wt			3050	18.57		100.0

<----- Verify this number is 100%




Superior Materials, LLC
 30701 W. 10 Mile Rd.
 Suite 500
 Farmington Hills, MI 48336

Sieve	6AA	26A	2NS	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	100.0	100.0	100.0	0.0	0.0
1.5"	100.0	100.0	100.0	100.0	0.0	0.0
1"	97.6	100.0	100.0	98.8	1.2	1.2
3/4"	76.3	100.0	100.0	88.0	10.8	12.0
1/2"	32.5	96.5	100.0	65.4	22.6	34.6
3/8"	15.9	88.3	100.0	56.1	9.2	43.9
#4	3.5	27.7	97.2	42.7	13.4	57.3
#8	2.1	8.2	82.7	34.4	8.3	65.6
#16	1.9	3.4	69.2	28.5	5.9	71.5
#30	1.8	2.6	52.3	21.7	6.8	78.3
#50	1.7	2.4	22.2	9.8	11.9	90.2
#100	1.6	2.2	4.4	2.8	7.1	97.2
LBW	1.3	1.9	1.1	1.3	1.5	98.7

*Maximum % Retained must be above the 3/8" sieve.
 *Any two adjacent sieves must equal 10% except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 4% for each sieve except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 8% for the 1" sieve when a 2" max. size (nom. Max. 1.5") aggregate is used.

Production Gradation Batch Plant Gradations Aggregate Supplier Gradations

Coarseness Factor: **67** **Workability Factor:** **34**

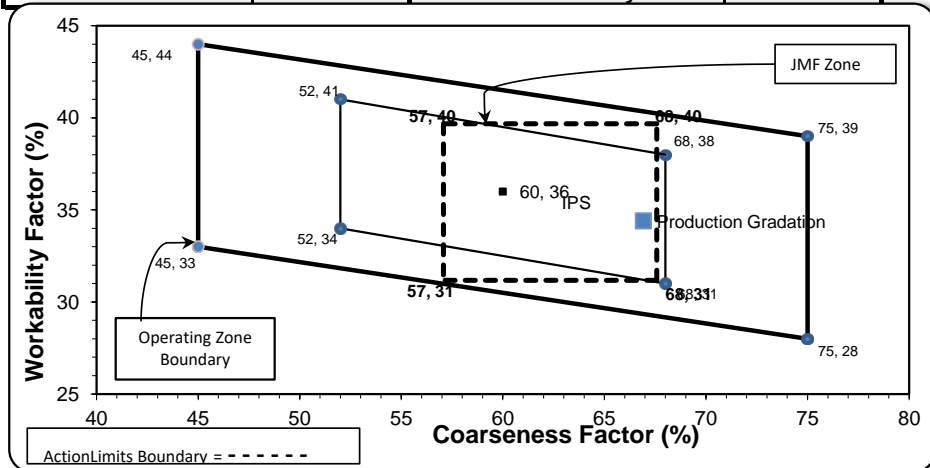

Initial Production Sample (IPS)

Coarseness Factor: **62**
Workability Factor: **35**

Sieve	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	0.0	0.0
1.5"	100.0	0.0	0.0
1"	99.1	0.9	0.9
3/4"	90.5	8.6	9.5
1/2"	69.8	20.7	30.2
3/8"	59.8	10.0	40.2
#4	42.2	17.6	57.8
#8	35.4	6.7	64.6
#16	28.8	6.7	71.2
#30	21.4	7.4	78.6
#50	8.8	12.6	91.2
#100	1.8	7.0	98.2
LBW	0.7	1.0	99.3

PREPARED BY:
 SM, LLC Technical Service

Approved By:

Aggregate Optimization Chart

PLANT #: **P-39**

Sample Date: 10/3/22

Concrete Grade: **S2M, 3500HP**

Dates Test Represents: 10/4/2022 through 10/10/2022

Contractor: _____

MDOT No.: _____

Agg. Class	Pit #	Source	Weight (SSD)	ft ³	Specific Gravity	% Contribution
6AA	71-47	Presque Isle	1600	9.79	2.62	52.5
26A	71-47	Presque Isle	200	1.22	2.62	6.6
2NS	44-051	Krake Willis Rd	1250	7.56	2.65	41.0
Total Wt			3050	18.57		100.0

<----- Verify this number is 100%




Superior Materials, LLC
 30701 W. 10 Mile Rd.
 Suite 500
 Farmington Hills, MI 48336

Sieve	6AA	26A	2NS	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	100.0	100.0	100.0	0.0	0.0
1.5"	100.0	100.0	100.0	100.0	0.0	0.0
1"	97.9	100.0	100.0	98.9	1.1	1.1
3/4"	86.5	100.0	100.0	92.9	6.0	7.1
1/2"	48.4	94.1	100.0	72.5	20.4	27.5
3/8"	29.9	80.1	100.0	61.9	10.6	38.1
#4	5.5	23.7	96.2	43.9	18.1	56.1
#8	2.6	7.7	80.6	34.9	9.0	65.1
#16	2.1	4.1	65.9	28.4	6.5	71.6
#30	1.9	3.2	50.9	22.1	6.3	77.9
#50	1.8	2.9	27.6	12.4	9.6	87.6
#100	1.7	2.7	8.4	4.5	7.9	95.5
LBW	1.6	2.5	1.6	1.7	2.9	98.3

*Maximum % Retained must be above the 3/8" sieve.
 *Any two adjacent sieves must equal 10% except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 4% for each sieve except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 8% for the 1" sieve when a 2" max. size (nom. Max. 1.5") aggregate is used.

Production Gradation Batch Plant Gradations Aggregate Supplier Gradations

Coarseness Factor:	58	Workability Factor:	35
---------------------------	-----------	----------------------------	-----------

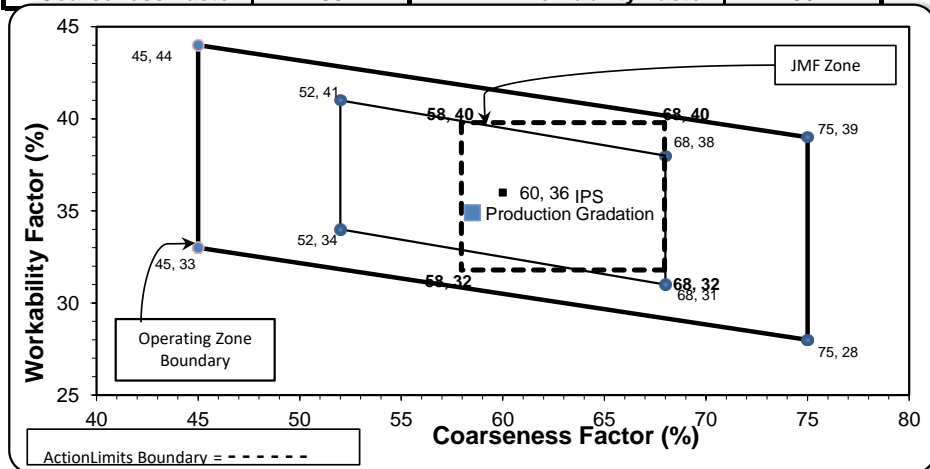

Initial Production Sample (IPS)

Coarseness Factor:	63		
Workability Factor:	36		
Sieve	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	0.0	0.0
1.5"	100.0	0.0	0.0
1"	100.0	0.0	0.0
3/4"	89.8	10.2	10.2
1/2"	70.7	19.1	29.3
3/8"	59.6	11.1	40.4
#4	43.2	16.4	56.8
#8	35.8	7.4	64.2
#16	29.2	6.6	70.8
#30	21.4	7.8	78.6
#50	9.8	11.6	90.2
#100	3.7	6.1	96.3
LBW	1.2	2.5	98.8

PREPARED BY:
 SM, LLC Technical Service

Approved By:

Aggregate Optimization Chart

PLANT #: **P-O2**

Sample Date: 10/3/22

Concrete Grade: **S2M, 3500HP**

Dates Test Represents: 10/4/2022 through 10/10/2022

Contractor: _____

MDOT No.: _____

Agg. Class	Pit #	Source	Weight (SSD)	ft ³	Specific Gravity	% Contribution
6AA	71-47	Presque Isle	1620	9.91	2.62	53.1
26A	71-47	Presque Isle	200	1.22	2.62	6.6
2NS	63-115	Ray Rd	1230	7.44	2.65	40.3
Total Wt			3050	18.57		100.0

<----- Verify this number is 100%




Superior Materials, LLC
 30701 W. 10 Mile Rd.
 Suite 500
 Farmington Hills, MI 48336

Sieve	6AA	26A	2NS	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	100.0	100.0	100.0	0.0	0.0
1.5"	100.0	100.0	100.0	100.0	0.0	0.0
1"	97.6	100.0	100.0	98.7	1.3	1.3
3/4"	76.3	100.0	100.0	87.4	11.3	12.6
1/2"	32.5	96.5	100.0	63.9	23.5	36.1
3/8"	15.9	88.3	100.0	54.6	9.4	45.4
#4	3.5	27.7	96.9	42.8	11.8	57.2
#8	2.1	8.2	79.9	33.9	8.9	66.1
#16	1.9	3.4	64.5	27.2	6.6	72.8
#30	1.8	2.6	49.2	21.0	6.3	79.0
#50	1.7	2.4	26.8	11.9	9.1	88.1
#100	1.6	2.2	6.5	3.6	8.3	96.4
LBW	1.3	1.9	0.8	1.1	2.5	98.9

*Maximum % Retained must be above the 3/8" sieve.
 *Any two adjacent sieves must equal 10% except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 4% for each sieve except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 8% for the 1" sieve when a 2" max. size (nom. Max. 1.5") aggregate is used.

Production Gradation Batch Plant Gradations Aggregate Supplier Gradations

Coarseness Factor: 69 **Workability Factor:** 34

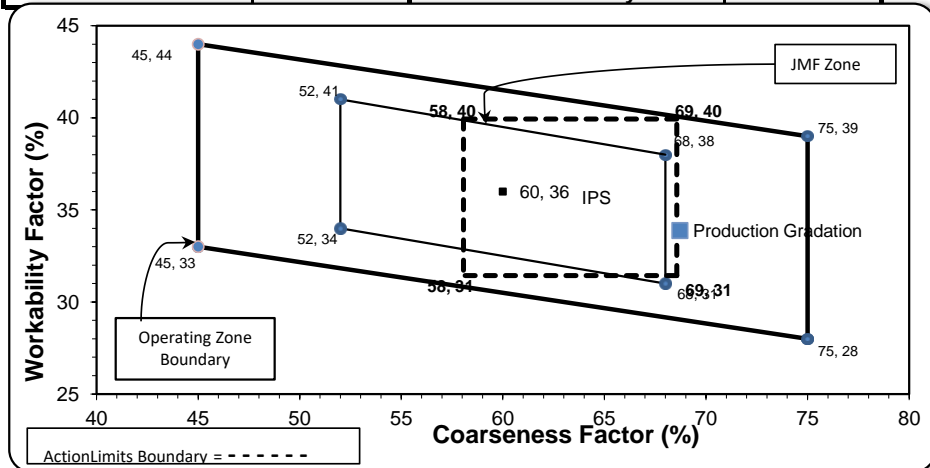

Initial Production Sample (IPS)

Coarseness Factor: 63
Workability Factor: 36

Sieve	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	0.0	0.0
1.5"	100.0	0.0	0.0
1"	100.0	0.0	0.0
3/4"	95.6	4.4	4.4
1/2"	73.1	22.6	26.9
3/8"	59.3	13.8	40.7
#4	42.8	16.5	57.2
#8	35.7	7.1	64.3
#16	28.9	6.8	71.1
#30	20.7	8.2	79.3
#50	9.9	10.8	90.1
#100	2.1	7.8	97.9
LBW	0.9	1.2	99.1

PREPARED BY:
 SM, LLC Technical Service

Approved By:
