

Aggregate Optimization Chart

PLANT #: 11

Sample Date: 11/28/22

Concrete Grade: **S2M, 3500HP**

Dates Test Represents: 11/29/2022 through 12/5/2022

Contractor: _____

MDOT No.: _____

Agg. Class	Pit #	Source	Weight (SSD)	ft ³	Specific Gravity	% Contribution
6AA	71-47	Presque Isle	1520	9.30	2.62	49.8
26A	71-47	Presque Isle	300	1.83	2.62	9.8
2NS	95-013	Smelter Bay	1230	7.44	2.65	40.3
Total Wt			3050	18.57		100.0

<----- Verify this number is 100%




Superior Materials, LLC
 30701 W. 10 Mile Rd.
 Suite 500
 Farmington Hills, MI 48336

Sieve	6AA	26A	2NS	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	100.0	100.0	100.0	0.0	0.0
1.5"	100.0	100.0	100.0	100.0	0.0	0.0
1"	98.8	100.0	100.0	99.4	0.6	0.6
3/4"	88.1	100.0	100.0	94.1	5.3	5.9
1/2"	48.6	98.6	100.0	74.2	19.8	25.8
3/8"	26.6	89.4	100.0	62.4	11.9	37.6
#4	4.7	25.1	95.9	43.5	18.9	56.5
#8	2.6	5.8	84.0	35.7	7.7	64.3
#16	2.3	2.9	68.8	29.2	6.6	70.8
#30	2.2	2.2	49.9	21.4	7.7	78.6
#50	2.1	2.1	24.4	11.1	10.3	88.9
#100	2.0	2.0	6.7	3.9	7.2	96.1
LBW	1.8	1.7	1.4	1.6	2.3	98.4

*Maximum % Retained must be above the 3/8" sieve.
 *Any two adjacent sieves must equal 10% except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 4% for each sieve except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 8% for the 1" sieve when a 2" max. size (nom. Max. 1.5") aggregate is used.

Production Gradation Batch Plant Gradations Aggregate Supplier Gradations

Coarseness Factor:	59	Workability Factor:	36
---------------------------	-----------	----------------------------	-----------

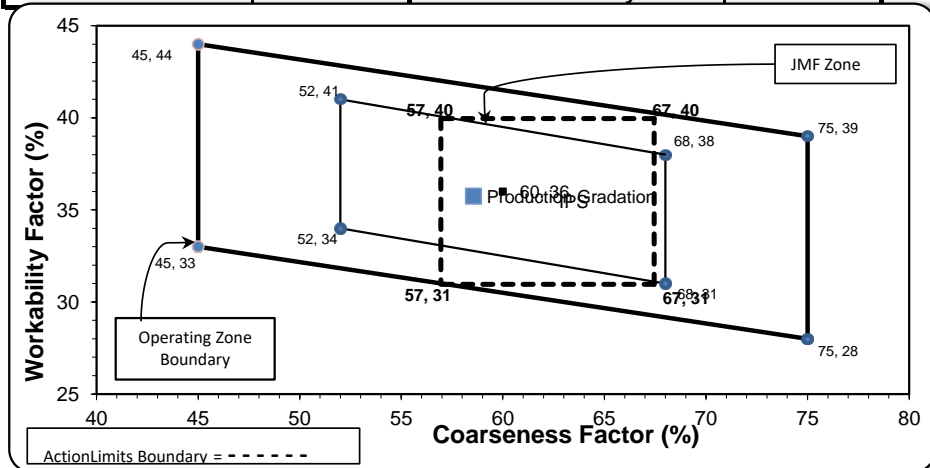

Initial Production Sample (IPS)

Coarseness Factor:	62
Workability Factor:	35

Sieve	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	0.0	0.0
1.5"	100.0	0.0	0.0
1"	100.0	0.0	0.0
3/4"	94.0	6.0	6.0
1/2"	70.2	23.7	29.8
3/8"	59.9	10.4	40.1
#4	42.7	17.2	57.3
#8	35.5	7.2	64.5
#16	28.4	7.0	71.6
#30	19.2	9.2	80.8
#50	8.9	10.3	91.1
#100	3.1	5.9	96.9
LBW	1.4	1.7	98.6

PREPARED BY:
 SM, LLC Technical Service

Approved By:

Aggregate Optimization Chart

PLANT #: **P-32**

Sample Date: 11/28/22

Concrete Grade: **S2M, 3500HP**

Dates Test Represents: 11/29/2022 through 12/5/2022

Contractor: _____

MDOT No.: _____

Agg. Class	Pit #	Source	Weight (SSD)	ft ³	Specific Gravity	% Contribution
6AA	71-47	Presque Isle	1520	9.30	2.62	49.8
26A	71-47	Presque Isle	300	1.83	2.62	9.8
2NS	95-013	Smelter Bay	1230	7.44	2.65	40.3
Total Wt			3050	18.57		100.0

<----- Verify this number is 100%




Superior Materials, LLC
 30701 W. 10 Mile Rd.
 Suite 500
 Farmington Hills, MI 48336

Sieve	6AA	26A	2NS	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	100.0	100.0	100.0	0.0	0.0
1.5"	100.0	100.0	100.0	100.0	0.0	0.0
1"	98.8	100.0	100.0	99.4	0.6	0.6
3/4"	88.1	100.0	100.0	94.1	5.3	5.9
1/2"	48.6	98.6	100.0	74.2	19.8	25.8
3/8"	26.6	89.4	100.0	62.4	11.9	37.6
#4	4.7	25.1	95.9	43.5	18.9	56.5
#8	2.6	5.8	84.0	35.7	7.7	64.3
#16	2.3	2.9	68.8	29.2	6.6	70.8
#30	2.2	2.2	49.9	21.4	7.7	78.6
#50	2.1	2.1	24.4	11.1	10.3	88.9
#100	2.0	2.0	6.7	3.9	7.2	96.1
LBW	1.8	1.7	1.4	1.6	2.3	98.4

*Maximum % Retained must be above the 3/8" sieve.
 *Any two adjacent sieves must equal 10% except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 4% for each sieve except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 8% for the 1" sieve when a 2" max. size (nom. Max. 1.5") aggregate is used.

Production Gradation Batch Plant Gradations Aggregate Supplier Gradations

Coarseness Factor: **59** **Workability Factor:** **36**

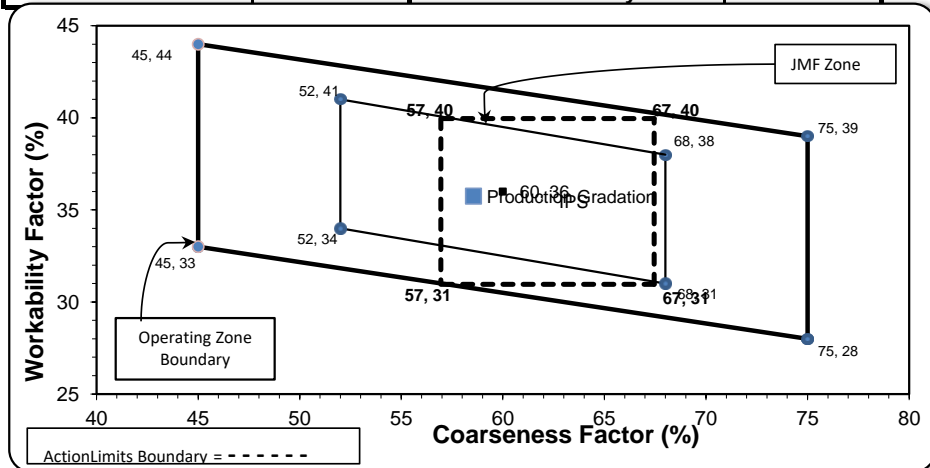

Initial Production Sample (IPS)

Coarseness Factor: **62**
Workability Factor: **35**

Sieve	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	0.0	0.0
1.5"	100.0	0.0	0.0
1"	100.0	0.0	0.0
3/4"	94.0	6.0	6.0
1/2"	70.2	23.7	29.8
3/8"	59.9	10.4	40.1
#4	42.7	17.2	57.3
#8	35.5	7.2	64.5
#16	28.4	7.0	71.6
#30	19.2	9.2	80.8
#50	8.9	10.3	91.1
#100	3.1	5.9	96.9
LBW	1.4	1.7	98.6

PREPARED BY:
 SM, LLC Technical Service

Approved By:

Aggregate Optimization Chart

PLANT #: P-02

Sample Date: 11/28/22

Concrete Grade: S2M, 3500HP

Dates Test Represents: 11/29/2022 through 12/5/2022

Contractor: _____

MDOT No.: _____

Agg. Class	Pit #	Source	Weight (SSD)	ft ³	Specific Gravity	% Contribution
6AA	71-47	Presque Isle	1570	9.60	2.62	51.5
26A	71-47	Presque Isle	250	1.53	2.62	8.2
2NS	63-115	Ray Rd	1230	7.44	2.65	40.3
Total Wt			3050	18.57		100.0

<----- Verify this number is 100%




Superior Materials, LLC
 30701 W. 10 Mile Rd.
 Suite 500
 Farmington Hills, MI 48336

Sieve	6AA	26A	2NS	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	100.0	100.0	100.0	0.0	0.0
1.5"	100.0	100.0	100.0	100.0	0.0	0.0
1"	98.1	100.0	100.0	99.0	1.0	1.0
3/4"	78.5	100.0	100.0	88.9	10.1	11.1
1/2"	38.7	98.6	100.0	68.3	20.6	31.7
3/8"	17.7	89.4	100.0	56.8	11.6	43.2
#4	3.5	25.1	96.8	42.9	13.9	57.1
#8	2.3	5.8	80.1	34.0	8.9	66.0
#16	2.0	2.9	63.9	27.0	6.9	73.0
#30	1.8	2.2	48.5	20.7	6.4	79.3
#50	1.7	2.1	26.0	11.5	9.1	88.5
#100	1.6	2.0	5.2	3.1	8.4	96.9
LBW	1.2	1.7	0.8	1.1	2.0	98.9

*Maximum % Retained must be above the 3/8" sieve.
 *Any two adjacent sieves must equal 10% except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 4% for each sieve except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 8% for the 1" sieve when a 2" max. size (nom. Max. 1.5") aggregate is used.

Production Gradation Batch Plant Gradations Aggregate Supplier Gradations

Coarseness Factor: 65 **Workability Factor:** 34

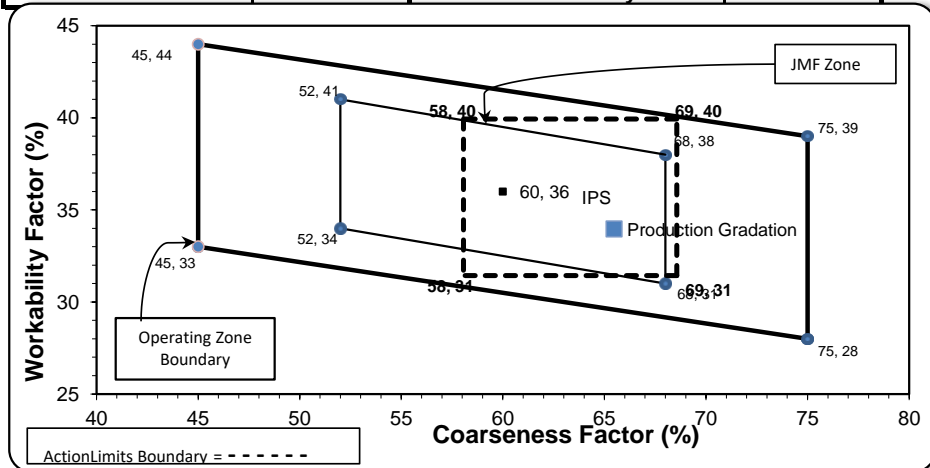

Initial Production Sample (IPS)

Coarseness Factor: 63
Workability Factor: 36

Sieve	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	0.0	0.0
1.5"	100.0	0.0	0.0
1"	100.0	0.0	0.0
3/4"	95.6	4.4	4.4
1/2"	73.1	22.6	26.9
3/8"	59.3	13.8	40.7
#4	42.8	16.5	57.2
#8	35.7	7.1	64.3
#16	28.9	6.8	71.1
#30	20.7	8.2	79.3
#50	9.9	10.8	90.1
#100	2.1	7.8	97.9
LBW	0.9	1.2	99.1

PREPARED BY:
 SM, LLC Technical Service

Approved By:
