

# Aggregate Optimization Chart

**PLANT #:** **P-101**

Sample Date: 5/9/22

Concrete Grade: **S2M, 3500HP**

Dates Test Represents: 5/10/2022 through 5/16/2022

Contractor: \_\_\_\_\_

MDOT No.: \_\_\_\_\_

Agg. Class	Pit #	Source	Weight (SSD)	ft <sup>3</sup>	Specific Gravity	% Contribution
6AA	71-47	Presque Isle	1550	9.48	2.62	50.7
26A	71-47	Presque Isle	275	1.68	2.62	9.0
2NS	75-051	Mid Michigan	1230	7.41	2.66	40.3
<b>Total Wt</b>			<b>3055</b>	<b>18.57</b>		<b>100.0</b>

<---- Verify this number is 100%



**Superior Materials, LLC**  
 30701 W. 10 Mile Rd.  
 Suite 500  
 Farmington Hills, MI 48336

Sieve	6AA	26A	2NS	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	100.0	100.0	100.0	0.0	0.0
1.5"	100.0	100.0	100.0	100.0	0.0	0.0
1"	99.0	100.0	100.0	99.5	0.5	0.5
3/4"	86.3	100.0	100.0	93.0	6.4	7.0
1/2"	39.4	98.3	100.0	69.1	23.9	30.9
3/8"	20.9	87.6	100.0	58.8	10.3	41.2
#4	2.9	17.3	98.5	42.7	16.1	57.3
#8	1.9	3.7	83.3	34.8	7.9	65.2
#16	1.7	2.3	68.3	28.6	6.3	71.4
#30	1.6	2.2	53.3	22.5	6.1	77.5
#50	1.5	2.0	29.2	12.7	9.8	87.3
#100	1.4	1.9	7.3	3.8	8.9	96.2
LBW	1.2	1.8	0.6	1.0	2.8	99.0

\*Maximum % Retained must be above the 3/8" sieve.  
 \*Any two adjacent sieves must equal 10% except max., nom. max., #100 and #200 sieves.  
 \*% Retained must be at least 4% for each sieve except max., nom. max., #100 and #200 sieves.  
 \*% Retained must be at least 8% for the 1" sieve when a 2" max. size (nom. Max. 1.5") aggregate is used.


Production Gradation  Batch Plant Gradations  Aggregate Supplier Gradations

<b>Coarseness Factor:</b>	<b>63</b>	<b>Workability Factor:</b>	<b>35</b>
---------------------------	-----------	----------------------------	-----------

Initial Production Sample (IPS)

<b>Coarseness Factor:</b>	<b>64</b>
<b>Workability Factor:</b>	<b>35</b>

Sieve	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	0.0	0.0
1.5"	100.0	0.0	0.0
1"	100.0	0.0	0.0
3/4"	93.9	6.1	6.1
1/2"	71.4	22.5	28.6
3/8"	59.0	12.4	41.0
#4	45.1	13.9	54.9
#8	35.5	9.6	64.5
#16	28.3	7.2	71.7
#30	21.3	6.9	78.7
#50	11.0	10.3	89.0
#100	3.4	7.6	96.6
LBW	1.1	2.3	98.9

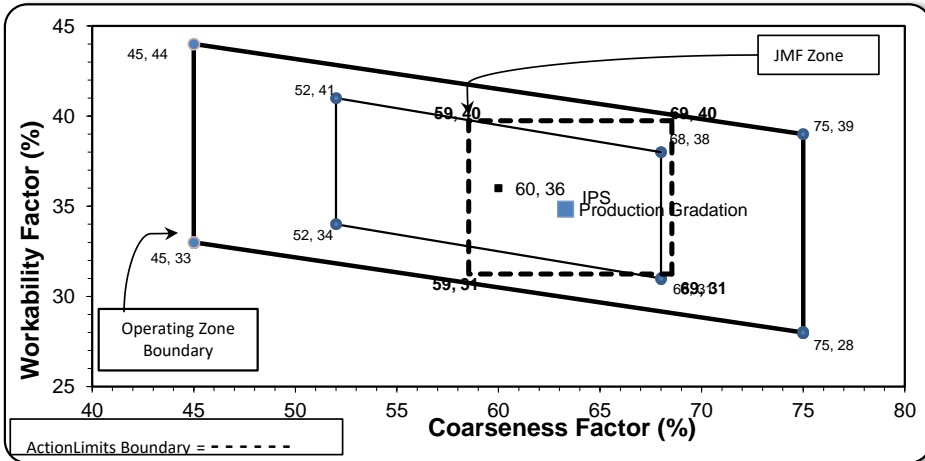

PREPARED BY:  
 SM, LLC Technical Service

Approved By:

# Aggregate Optimization Chart

**PLANT #:** **P-102**

Sample Date: 5/9/22

Concrete Grade: **S2M, 3500HP**

Dates Test Represents: 5/10/2022 through 5/16/2022

Contractor: \_\_\_\_\_

MDOT No.: \_\_\_\_\_

Agg. Class	Pit #	Source	Weight (SSD)	ft <sup>3</sup>	Specific Gravity	% Contribution
6AA	58-003	Stoneco	1650	9.83	2.69	53.2
26A	58-003	Stoneco	250	1.49	2.69	8.1
2NS	81-019	Pleasant Lake	1200	7.26	2.65	38.7
<b>Total Wt</b>			<b>3100</b>	<b>18.58</b>		<b>100.0</b>

<---- Verify this number is 100%




**Superior Materials, LLC**  
 30701 W. 10 Mile Rd.  
 Suite 500  
 Farmington Hills, MI 48336

Sieve	6AA	26A	2NS	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	100.0	100.0	100.0	0.0	0.0
1.5"	100.0	100.0	100.0	100.0	0.0	0.0
1"	100.0	100.0	100.0	100.0	0.0	0.0
3/4"	82.8	100.0	100.0	90.8	9.2	9.2
1/2"	42.6	99.6	100.0	69.4	21.4	30.6
3/8"	21.4	84.9	100.0	56.9	12.5	43.1
#4	3.2	24.9	96.6	41.1	15.8	58.9
#8	1.2	7.2	79.8	32.1	9.0	67.9
#16	0.9	3.5	61.5	24.6	7.5	75.4
#30	0.8	2.7	43.6	17.5	7.0	82.5
#50	0.6	2.4	20.9	8.6	8.9	91.4
#100	0.6	2.3	6.5	3.0	5.6	97.0
LBW	0.5	2.0	0.8	0.7	2.3	99.3

\*Maximum % Retained must be above the 3/8" sieve.  
 \*Any two adjacent sieves must equal 10% except max., nom. max., #100 and #200 sieves.  
 \*% Retained must be at least 4% for each sieve except max., nom. max., #100 and #200 sieves.  
 \*% Retained must be at least 8% for the 1" sieve when a 2" max. size (nom. Max. 1.5") aggregate is used.

Production Gradation  Batch Plant Gradations  Aggregate Supplier Gradations

**Coarseness Factor:** **63**      **Workability Factor:** **32**

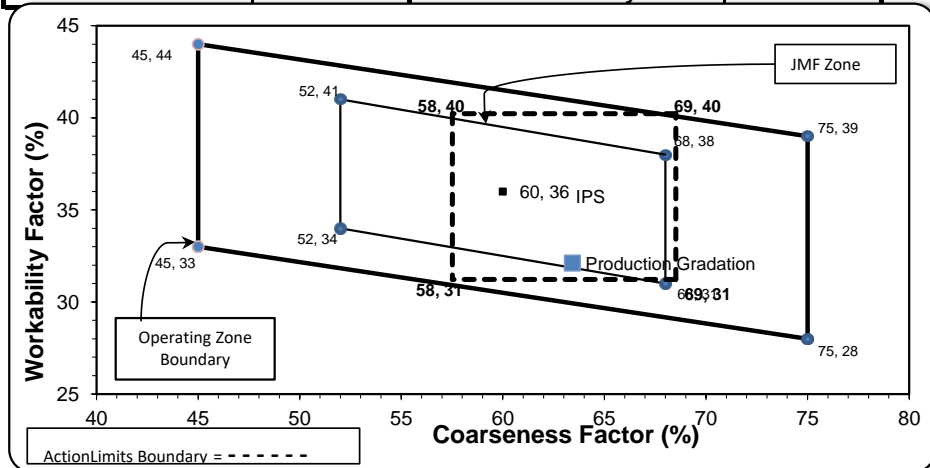

Initial Production Sample (IPS)

**Coarseness Factor:** **63**  
**Workability Factor:** **36**

Sieve	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	0.0	0.0
1.5"	100.0	0.0	0.0
1"	99.2	0.8	0.8
3/4"	90.9	8.3	9.1
1/2"	71.3	19.6	28.7
3/8"	59.5	11.8	40.5
#4	43.8	15.7	56.2
#8	35.7	8.1	64.3
#16	27.0	8.7	73.0
#30	18.6	8.4	81.4
#50	6.8	11.8	93.2
#100	1.4	5.4	98.6
LBW	0.6	0.8	99.4

PREPARED BY:  
 SM, LLC Technical Service

Approved By:

# Aggregate Optimization Chart

**PLANT #:** **P-32**

Sample Date: 5/9/22

Concrete Grade: **S2M, 3500HP**

Dates Test Represents: 5/10/2022 through 5/16/2022

Contractor: \_\_\_\_\_

MDOT No.: \_\_\_\_\_



**Superior Materials, LLC**  
 30701 W. 10 Mile Rd.  
 Suite 500  
 Farmington Hills, MI 48336

Agg. Class	Pit #	Source	Weight (SSD)	ft <sup>3</sup>	Specific Gravity	% Contribution
6AA	71-47	Presque Isle	1600	9.79	2.62	52.5
26A	71-47	Presque Isle	220	1.35	2.62	7.2
2NS	95-013	Smelter Bay	1230	7.44	2.65	40.3
<b>Total Wt</b>			<b>3050</b>	<b>18.57</b>		<b>100.0</b>


<----- Verify this number is 100%

Sieve	6AA	26A	2NS	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	100.0	100.0	100.0	0.0	0.0
1.5"	100.0	100.0	100.0	100.0	0.0	0.0
1"	99.4	100.0	100.0	99.7	0.3	0.3
3/4"	88.9	100.0	100.0	94.2	5.5	5.8
1/2"	52.3	95.0	100.0	74.6	19.6	25.4
3/8"	30.6	82.9	100.0	62.4	12.3	37.6
#4	5.0	24.2	97.2	43.6	18.8	56.4
#8	2.6	7.4	85.2	36.3	7.3	63.7
#16	2.2	3.4	70.8	30.0	6.3	70.0
#30	2.1	2.4	51.8	22.2	7.8	77.8
#50	2.0	2.1	25.3	11.4	10.8	88.6
#100	2.0	2.0	7.4	4.2	7.2	95.8
LBW	1.7	1.5	1.7	1.7	2.5	98.3

\*Maximum % Retained must be above the 3/8" sieve.  
 \*Any two adjacent sieves must equal 10% except max., nom. max., #100 and #200 sieves.  
 \*% Retained must be at least 4% for each sieve except max., nom. max., #100 and #200 sieves.  
 \*% Retained must be at least 8% for the 1" sieve when a 2" max. size (nom. Max. 1.5") aggregate is used.

Production Gradation  Batch Plant Gradations  Aggregate Supplier Gradations

**Coarseness Factor:** **59**      **Workability Factor:** **36**

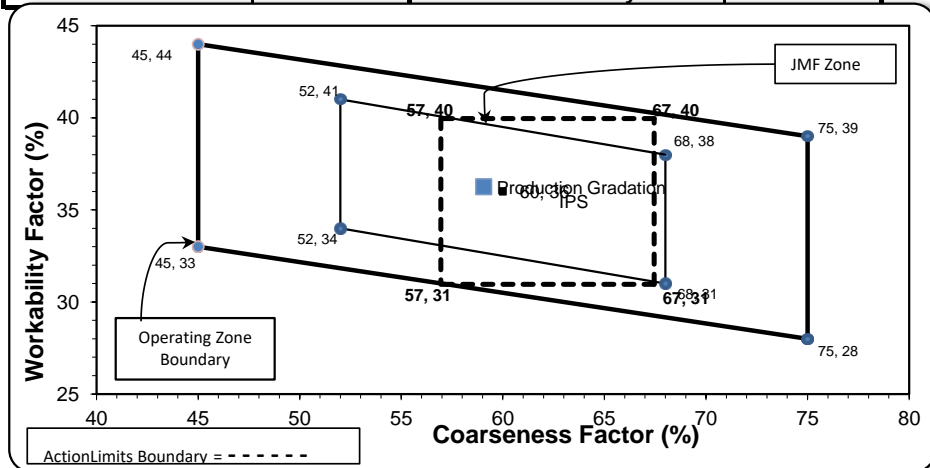

Initial Production Sample (IPS)

**Coarseness Factor:** **62**  
**Workability Factor:** **35**

Sieve	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	0.0	0.0
1.5"	100.0	0.0	0.0
1"	100.0	0.0	0.0
3/4"	94.0	6.0	6.0
1/2"	70.2	23.7	29.8
3/8"	59.9	10.4	40.1
#4	42.7	17.2	57.3
#8	35.5	7.2	64.5
#16	28.4	7.0	71.6
#30	19.2	9.2	80.8
#50	8.9	10.3	91.1
#100	3.1	5.9	96.9
LBW	1.4	1.7	98.6

PREPARED BY:  
 SM, LLC Technical Service

Approved By:

# Aggregate Optimization Chart

**PLANT #:** **P-35**

Sample Date: 5/9/22

Concrete Grade: **S2M, 3500HP**

Contractor: \_\_\_\_\_

Dates Test Represents: 5/10/2022 through 5/16/2022

MDOT No.: \_\_\_\_\_

Agg. Class	Pit #	Source	Weight (SSD)	ft <sup>3</sup>	Specific Gravity	% Contribution
6AA	58-003	Stoneco	1650	9.83	2.69	53.2
26A	58-003	Stoneco	250	1.49	2.69	8.1
2NS	81-019	Pleasant Lake	1200	7.26	2.65	38.7
<b>Total Wt</b>			<b>3100</b>	<b>18.58</b>		<b>100.0</b>

<----- Verify this number is 100%




**Superior Materials, LLC**  
 30701 W. 10 Mile Rd.  
 Suite 500  
 Farmington Hills, MI 48336

Sieve	6AA	26A	2NS	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	100.0	100.0	100.0	0.0	0.0
1.5"	100.0	100.0	100.0	100.0	0.0	0.0
1"	100.0	100.0	100.0	100.0	0.0	0.0
3/4"	82.8	100.0	100.0	90.8	9.2	9.2
1/2"	42.6	99.6	100.0	69.4	21.4	30.6
3/8"	21.4	84.9	100.0	56.9	12.5	43.1
#4	3.2	24.9	96.6	41.1	15.8	58.9
#8	1.2	7.2	79.8	32.1	9.0	67.9
#16	0.9	3.5	61.5	24.6	7.5	75.4
#30	0.8	2.7	43.6	17.5	7.0	82.5
#50	0.6	2.4	20.9	8.6	8.9	91.4
#100	0.6	2.3	6.5	3.0	5.6	97.0
LBW	0.5	2.0	0.8	0.7	2.3	99.3

\*Maximum % Retained must be above the 3/8" sieve.  
 \*Any two adjacent sieves must equal 10% except max., nom. max., #100 and #200 sieves.  
 \*% Retained must be at least 4% for each sieve except max., nom. max., #100 and #200 sieves.  
 \*% Retained must be at least 8% for the 1" sieve when a 2" max. size (nom. Max. 1.5") aggregate is used.

Production Gradation  Batch Plant Gradations  Aggregate Supplier Gradations

**Coarseness Factor:** **63**      **Workability Factor:** **32**

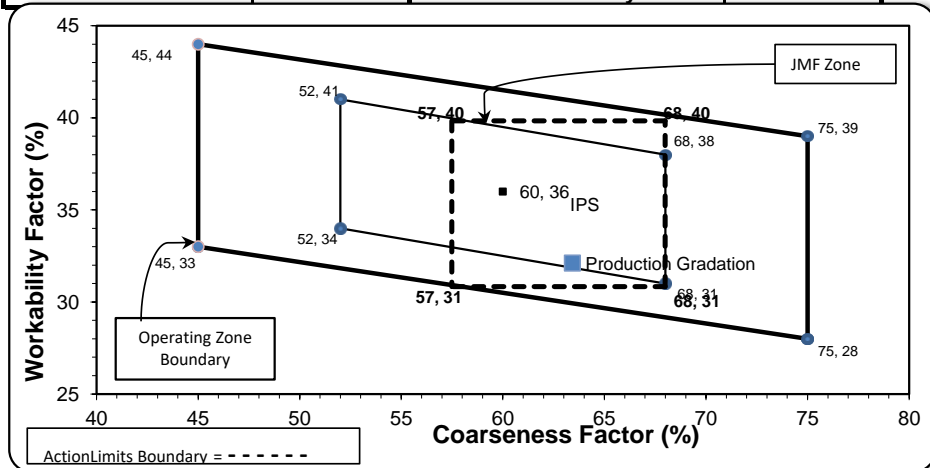

Initial Production Sample (IPS)

**Coarseness Factor:** **63**  
**Workability Factor:** **35**

Sieve	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	0.0	0.0
1.5"	100.0	0.0	0.0
1"	99.2	0.8	0.8
3/4"	90.9	8.3	9.1
1/2"	71.3	19.6	28.7
3/8"	59.4	11.9	40.6
#4	43.0	16.5	57.0
#8	35.3	7.6	64.7
#16	28.2	7.1	71.8
#30	21.6	6.6	78.4
#50	9.1	12.5	90.9
#100	1.7	7.4	98.3
LBW	1.1	0.6	98.9

PREPARED BY:  
 SM, LLC Technical Service

Approved By:

# Aggregate Optimization Chart

**PLANT #:** **P-39**

Sample Date: 5/9/22

Concrete Grade: **S2M, 3500HP**

Dates Test Represents: 5/10/2022 through 5/16/2022

Contractor: \_\_\_\_\_

MDOT No.: \_\_\_\_\_

Agg. Class	Pit #	Source	Weight (SSD)	ft <sup>3</sup>	Specific Gravity	% Contribution
6AA	71-47	Presque Isle	1550	9.48	2.62	50.8
26A	71-47	Presque Isle	250	1.53	2.62	8.2
2NS	44-051	Krake Willis Rd	1250	7.56	2.65	41.0
<b>Total Wt</b>			<b>3050</b>	<b>18.57</b>		<b>100.0</b>

<----- Verify this number is 100%




**Superior Materials, LLC**  
 30701 W. 10 Mile Rd.  
 Suite 500  
 Farmington Hills, MI 48336

Sieve	6AA	26A	2NS	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	100.0	100.0	100.0	0.0	0.0
1.5"	100.0	100.0	100.0	100.0	0.0	0.0
1"	99.0	100.0	100.0	99.5	0.5	0.5
3/4"	86.3	100.0	100.0	93.0	6.5	7.0
1/2"	39.4	98.3	100.0	69.1	24.0	30.9
3/8"	20.9	87.6	100.0	58.8	10.3	41.2
#4	2.9	17.3	96.5	42.4	16.3	57.6
#8	1.9	3.7	79.6	33.9	8.5	66.1
#16	1.7	2.3	63.2	27.0	6.9	73.0
#30	1.6	2.2	47.0	20.3	6.7	79.7
#50	1.5	2.0	26.4	11.7	8.5	88.3
#100	1.4	1.9	9.6	4.8	6.9	95.2
LBW	1.2	1.8	1.0	1.2	3.6	98.8

\*Maximum % Retained must be above the 3/8" sieve.  
 \*Any two adjacent sieves must equal 10% except max., nom. max., #100 and #200 sieves.  
 \*% Retained must be at least 4% for each sieve except max., nom. max., #100 and #200 sieves.  
 \*% Retained must be at least 8% for the 1" sieve when a 2" max. size (nom. Max. 1.5") aggregate is used.

Production Gradation  Batch Plant Gradations  Aggregate Supplier Gradations

<b>Coarseness Factor:</b>	<b>62</b>	<b>Workability Factor:</b>	<b>34</b>
---------------------------	-----------	----------------------------	-----------

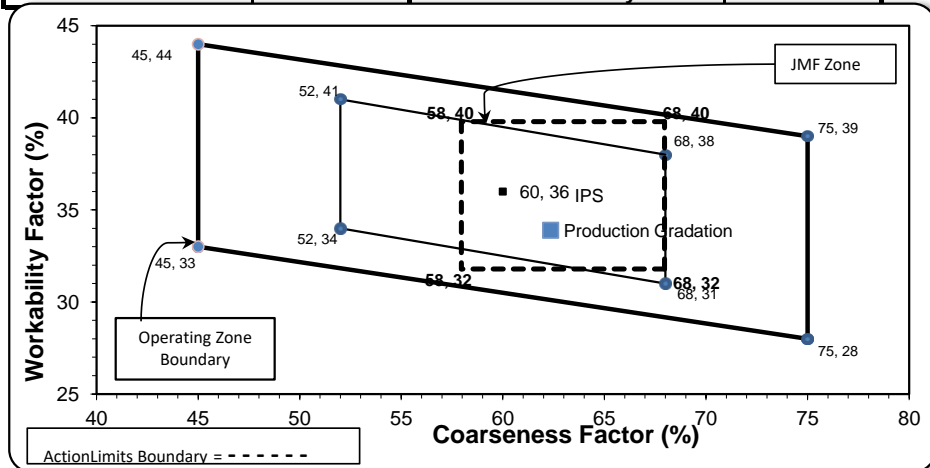

Initial Production Sample (IPS)

<b>Coarseness Factor:</b>	<b>63</b>		
<b>Workability Factor:</b>	<b>36</b>		
Sieve	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	0.0	0.0
1.5"	100.0	0.0	0.0
1"	100.0	0.0	0.0
3/4"	89.8	10.2	10.2
1/2"	70.7	19.1	29.3
3/8"	59.6	11.1	40.4
#4	43.2	16.4	56.8
#8	35.8	7.4	64.2
#16	29.2	6.6	70.8
#30	21.4	7.8	78.6
#50	9.8	11.6	90.2
#100	3.7	6.1	96.3
LBW	1.2	2.5	98.8

PREPARED BY:  
 SM, LLC Technical Service

Approved By:

# Aggregate Optimization Chart

**PLANT #:** **P-02**

Sample Date: 5/9/22

Concrete Grade: **S2M, 3500HP**

Dates Test Represents: 5/10/2022 through 5/16/2022

Contractor: \_\_\_\_\_

MDOT No.: \_\_\_\_\_

Agg. Class	Pit #	Source	Weight (SSD)	ft <sup>3</sup>	Specific Gravity	% Contribution
6AA	71-47	Presque Isle	1550	9.48	2.62	50.8
26A	71-47	Presque Isle	250	1.53	2.62	8.2
2NS	63-115	Ray Rd	1250	7.56	2.65	41.0
<b>Total Wt</b>			<b>3050</b>	<b>18.57</b>		<b>100.0</b>

<----- Verify this number is 100%




**Superior Materials, LLC**  
 30701 W. 10 Mile Rd.  
 Suite 500  
 Farmington Hills, MI 48336

Sieve	6AA	26A	2NS	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	100.0	100.0	100.0	0.0	0.0
1.5"	100.0	100.0	100.0	100.0	0.0	0.0
1"	99.4	100.0	100.0	99.7	0.3	0.3
3/4"	85.8	100.0	100.0	92.8	6.9	7.2
1/2"	47.2	95.0	100.0	72.8	20.0	27.2
3/8"	26.6	82.9	100.0	61.3	11.5	38.7
#4	4.4	24.2	96.2	43.6	17.7	56.4
#8	2.7	7.4	78.5	34.2	9.5	65.8
#16	2.4	3.4	62.5	27.1	7.0	72.9
#30	2.3	2.4	46.8	20.5	6.6	79.5
#50	2.2	2.1	24.2	11.2	9.3	88.8
#100	2.1	2.0	4.3	3.0	8.2	97.0
LBW	1.6	1.5	0.8	1.3	1.7	98.7

\*Maximum % Retained must be above the 3/8" sieve.  
 \*Any two adjacent sieves must equal 10% except max., nom. max., #100 and #200 sieves.  
 \*% Retained must be at least 4% for each sieve except max., nom. max., #100 and #200 sieves.  
 \*% Retained must be at least 8% for the 1" sieve when a 2" max. size (nom. Max. 1.5") aggregate is used.

Production Gradation  Batch Plant Gradations  Aggregate Supplier Gradations

**Coarseness Factor:** **59**      **Workability Factor:** **34**

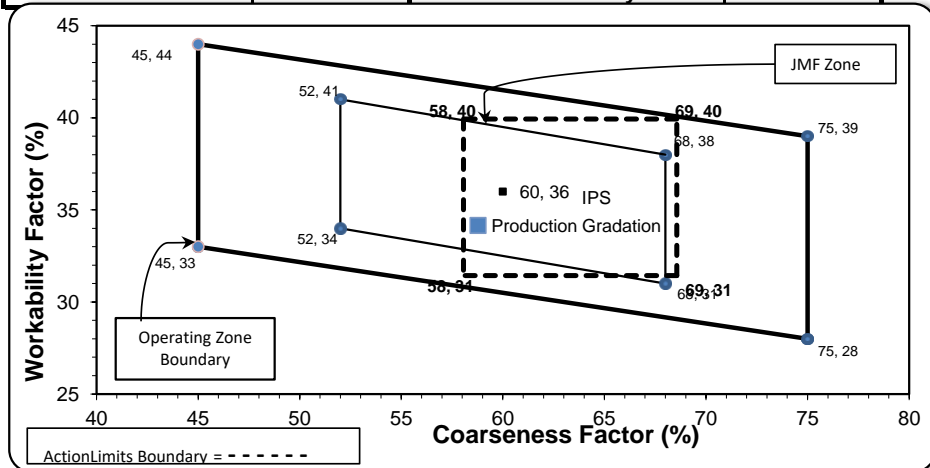

Initial Production Sample (IPS)

**Coarseness Factor:** **63**  
**Workability Factor:** **36**

Sieve	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	0.0	0.0
1.5"	100.0	0.0	0.0
1"	100.0	0.0	0.0
3/4"	95.6	4.4	4.4
1/2"	73.1	22.6	26.9
3/8"	59.3	13.8	40.7
#4	42.8	16.5	57.2
#8	35.7	7.1	64.3
#16	28.9	6.8	71.1
#30	20.7	8.2	79.3
#50	9.9	10.8	90.1
#100	2.1	7.8	97.9
LBW	0.9	1.2	99.1

PREPARED BY:  
 SM, LLC Technical Service

Approved By:
