

Aggregate Optimization Chart

PLANT #: **P-101**

Sample Date: 8/1/22

Concrete Grade: **S2M, 3500HP**

Dates Test Represents: 8/2/2022 through 8/8/2022

Contractor: _____

MDOT No.: _____

Agg. Class	Pit #	Source	Weight (SSD)	ft ³	Specific Gravity	% Contribution
6AA	71-47	Presque Isle	1625	9.94	2.62	53.2
26A	71-47	Presque Isle	200	1.22	2.62	6.5
2NS	75-051	Mid Michigan	1230	7.41	2.66	40.3
Total Wt			3055	18.57		100.0

<---- Verify this number is 100%



Superior Materials, LLC
 30701 W. 10 Mile Rd.
 Suite 500
 Farmington Hills, MI 48336

Sieve	6AA	26A	2NS	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	100.0	100.0	100.0	0.0	0.0
1.5"	100.0	100.0	100.0	100.0	0.0	0.0
1"	97.8	100.0	100.0	98.8	1.2	1.2
3/4"	85.3	100.0	100.0	92.2	6.6	7.8
1/2"	43.6	98.2	100.0	69.9	22.3	30.1
3/8"	21.9	86.2	100.0	57.6	12.3	42.4
#4	3.3	24.6	99.0	43.2	14.3	56.8
#8	2.0	5.8	85.3	35.8	7.4	64.2
#16	1.8	3.2	70.1	29.4	6.4	70.6
#30	1.6	2.6	53.2	22.4	6.9	77.6
#50	1.5	2.3	26.3	11.5	10.9	88.5
#100	1.4	2.1	6.8	3.6	7.9	96.4
LBW	1.3	1.8	1.0	1.2	2.4	98.8


*Maximum % Retained must be above the 3/8" sieve.
 *Any two adjacent sieves must equal 10% except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 4% for each sieve except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 8% for the 1" sieve when a 2" max. size (nom. Max. 1.5") aggregate is used.

Production Gradation Batch Plant Gradations Aggregate Supplier Gradations

Coarseness Factor:	66	Workability Factor:	36
---------------------------	-----------	----------------------------	-----------

Initial Production Sample (IPS)

Coarseness Factor:	64
Workability Factor:	35

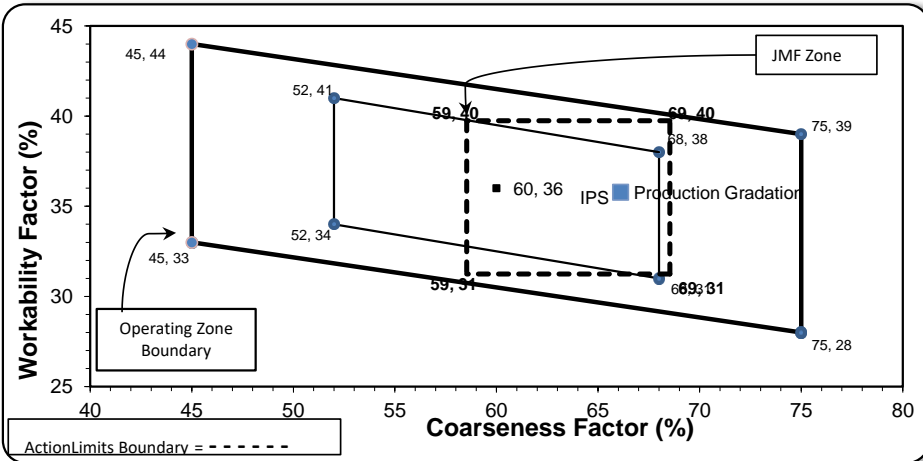

Sieve	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	0.0	0.0
1.5"	100.0	0.0	0.0
1"	100.0	0.0	0.0
3/4"	93.9	6.1	6.1
1/2"	71.4	22.5	28.6
3/8"	59.0	12.4	41.0
#4	45.1	13.9	54.9
#8	35.5	9.6	64.5
#16	28.3	7.2	71.7
#30	21.3	6.9	78.7
#50	11.0	10.3	89.0
#100	3.4	7.6	96.6
LBW	1.1	2.3	98.9

PREPARED BY:
 SM, LLC Technical Service

Approved By:

Aggregate Optimization Chart

PLANT #: P-102

Sample Date: 8/1/22

Concrete Grade: **S2M, 3500HP**

Dates Test Represents: 8/2/2022 through 8/8/2022

Contractor: _____

MDOT No.: _____

Agg. Class	Pit #	Source	Weight (SSD)	ft ³	Specific Gravity	% Contribution
6AA	58-003	Stoneco	1650	9.83	2.69	53.2
26A	58-003	Stoneco	250	1.49	2.69	8.1
2NS	81-019	Pleasant Lake	1200	7.26	2.65	38.7
Total Wt			3100	18.58		100.0

<----- Verify this number is 100%




Superior Materials, LLC
 30701 W. 10 Mile Rd.
 Suite 500
 Farmington Hills, MI 48336

Sieve	6AA	26A	2NS	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	100.0	100.0	100.0	0.0	0.0
1.5"	100.0	100.0	100.0	100.0	0.0	0.0
1"	100.0	100.0	100.0	100.0	0.0	0.0
3/4"	79.7	100.0	100.0	89.2	10.8	10.8
1/2"	46.8	99.5	100.0	71.6	17.6	28.4
3/8"	17.8	84.0	100.0	55.0	16.7	45.0
#4	1.3	14.3	99.1	40.2	14.8	59.8
#8	0.9	4.6	85.3	33.9	6.3	66.1
#16	0.6	2.9	68.1	26.9	7.0	73.1
#30	0.5	2.2	51.0	20.2	6.7	79.8
#50	0.4	2.0	27.0	10.8	9.4	89.2
#100	0.4	1.9	8.8	3.8	7.1	96.2
LBW	0.4	1.6	1.6	1.0	2.8	99.0

*Maximum % Retained must be above the 3/8" sieve.
 *Any two adjacent sieves must equal 10% except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 4% for each sieve except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 8% for the 1" sieve when a 2" max. size (nom. Max. 1.5") aggregate is used.

Production Gradation Batch Plant Gradations Aggregate Supplier Gradations

Coarseness Factor:	68	Workability Factor:	34
---------------------------	-----------	----------------------------	-----------

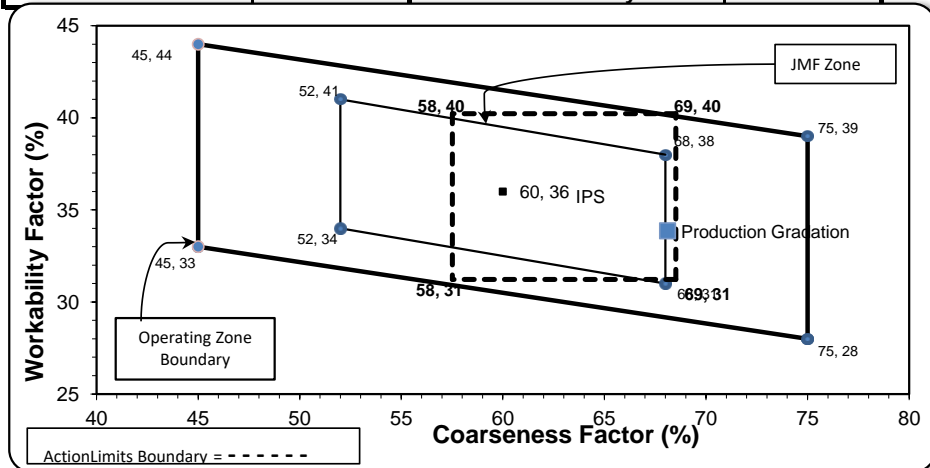

Initial Production Sample (IPS)

Coarseness Factor:	63		
Workability Factor:	36		
Sieve	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	0.0	0.0
1.5"	100.0	0.0	0.0
1"	99.2	0.8	0.8
3/4"	90.9	8.3	9.1
1/2"	71.3	19.6	28.7
3/8"	59.5	11.8	40.5
#4	43.8	15.7	56.2
#8	35.7	8.1	64.3
#16	27.0	8.7	73.0
#30	18.6	8.4	81.4
#50	6.8	11.8	93.2
#100	1.4	5.4	98.6
LBW	0.6	0.8	99.4

PREPARED BY:
 SM, LLC Technical Service

Approved By:

Aggregate Optimization Chart

PLANT #: **P-103**

Sample Date: 8/1/22

Concrete Grade: **S2M, 3500HP**

Dates Test Represents: 8/2/2022 through 8/8/2022

Contractor: _____

MDOT No.: _____

Agg. Class	Pit #	Source	Weight (SSD)	ft ³	Specific Gravity	% Contribution
6AA	58-003	Stoneco	1650	9.83	2.69	53.2
26A	58-003	Stoneco	250	1.49	2.69	8.1
2NS	81-019	Pleasant Lake	1200	7.26	2.65	38.7
Total Wt			3100	18.58		100.0

<----- Verify this number is 100%




Superior Materials, LLC
 30701 W. 10 Mile Rd.
 Suite 500
 Farmington Hills, MI 48336

Sieve	6AA	26A	2NS	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	100.0	100.0	100.0	0.0	0.0
1.5"	100.0	100.0	100.0	100.0	0.0	0.0
1"	100.0	100.0	100.0	100.0	0.0	0.0
3/4"	79.7	100.0	100.0	89.2	10.8	10.8
1/2"	46.8	99.5	100.0	71.6	17.6	28.4
3/8"	17.8	84.0	100.0	55.0	16.7	45.0
#4	1.3	14.3	99.1	40.2	14.8	59.8
#8	0.9	4.6	85.3	33.9	6.3	66.1
#16	0.6	2.9	68.1	26.9	7.0	73.1
#30	0.5	2.2	51.0	20.2	6.7	79.8
#50	0.4	2.0	27.0	10.8	9.4	89.2
#100	0.4	1.9	8.8	3.8	7.1	96.2
LBW	0.4	1.6	1.6	1.0	2.8	99.0

*Maximum % Retained must be above the 3/8" sieve.
 *Any two adjacent sieves must equal 10% except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 4% for each sieve except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 8% for the 1" sieve when a 2" max. size (nom. Max. 1.5") aggregate is used.

Production Gradation Batch Plant Gradations Aggregate Supplier Gradations

Coarseness Factor:	68	Workability Factor:	34
---------------------------	-----------	----------------------------	-----------

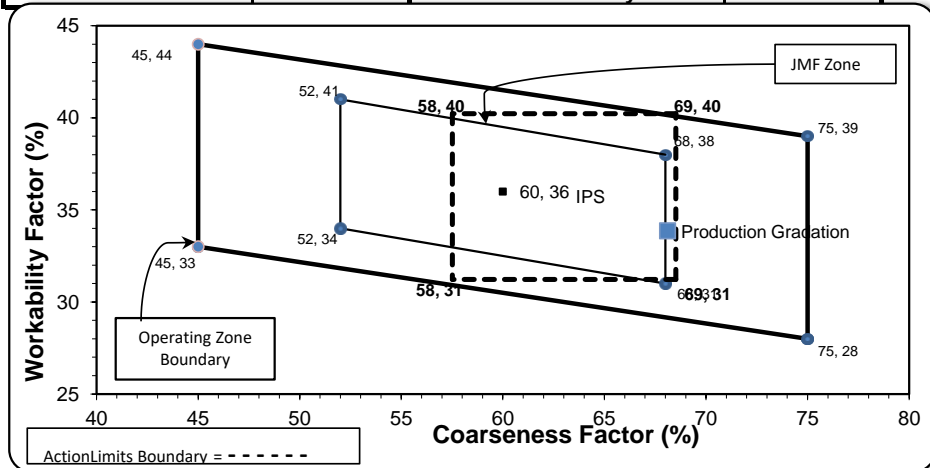

Initial Production Sample (IPS)

Coarseness Factor:	63		
Workability Factor:	36		
Sieve	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	0.0	0.0
1.5"	100.0	0.0	0.0
1"	99.2	0.8	0.8
3/4"	90.9	8.3	9.1
1/2"	71.3	19.6	28.7
3/8"	59.5	11.8	40.5
#4	43.8	15.7	56.2
#8	35.7	8.1	64.3
#16	27.0	8.7	73.0
#30	18.6	8.4	81.4
#50	6.8	11.8	93.2
#100	1.4	5.4	98.6
LBW	0.6	0.8	99.4

PREPARED BY:
 SM, LLC Technical Service

Approved BY:

Aggregate Optimization Chart

PLANT #: **P-32**

Sample Date: **8/1/22**

Concrete Grade: **S2M, 3500HP**

Dates Test Represents: **8/2/2022** through **8/8/2022**

Contractor: _____

MDOT No.: _____

Agg. Class	Pit #	Source	Weight (SSD)	ft ³	Specific Gravity	% Contribution
6AA	71-47	Presque Isle	1620	9.91	2.62	53.1
26A	71-47	Presque Isle	200	1.22	2.62	6.6
2NS	95-013	Smelter Bay	1230	7.44	2.65	40.3
Total Wt			3050	18.57		100.0

<----- Verify this number is 100%




Superior Materials, LLC
 30701 W. 10 Mile Rd.
 Suite 500
 Farmington Hills, MI 48336

Sieve	6AA	26A	2NS	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	100.0	100.0	100.0	0.0	0.0
1.5"	100.0	100.0	100.0	100.0	0.0	0.0
1"	97.4	100.0	100.0	98.6	1.4	1.4
3/4"	84.8	100.0	100.0	91.9	6.7	8.1
1/2"	45.5	95.5	100.0	70.8	21.2	29.2
3/8"	22.7	85.9	100.0	58.0	12.7	42.0
#4	3.9	28.8	96.0	42.7	15.3	57.3
#8	2.4	8.1	82.3	35.0	7.7	65.0
#16	2.0	3.7	66.8	28.2	6.8	71.8
#30	1.8	2.8	47.7	20.4	7.9	79.6
#50	1.7	2.5	23.3	10.5	9.9	89.5
#100	1.5	2.3	7.2	3.9	6.6	96.1
LBW	1.1	2.0	1.3	1.2	2.6	98.8

*Maximum % Retained must be above the 3/8" sieve.
 *Any two adjacent sieves must equal 10% except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 4% for each sieve except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 8% for the 1" sieve when a 2" max. size (nom. Max. 1.5") aggregate is used.

Production Gradation Batch Plant Gradations Aggregate Supplier Gradations

Coarseness Factor: **65** **Workability Factor:** **35**

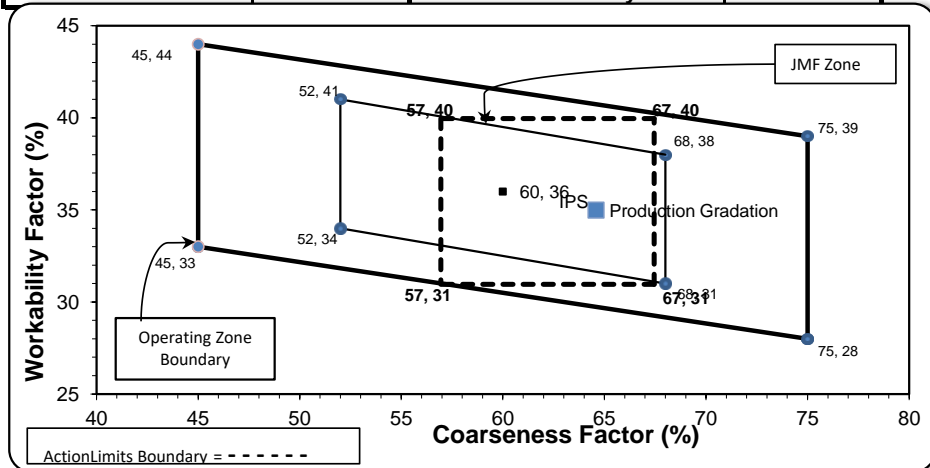

Initial Production Sample (IPS)

Coarseness Factor: 62		Workability Factor: 35	
Sieve	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	0.0	0.0
1.5"	100.0	0.0	0.0
1"	100.0	0.0	0.0
3/4"	94.0	6.0	6.0
1/2"	70.2	23.7	29.8
3/8"	59.9	10.4	40.1
#4	42.7	17.2	57.3
#8	35.5	7.2	64.5
#16	28.4	7.0	71.6
#30	19.2	9.2	80.8
#50	8.9	10.3	91.1
#100	3.1	5.9	96.9
LBW	1.4	1.7	98.6

PREPARED BY:
 SM, LLC Technical Service

Approved By:

Aggregate Optimization Chart

PLANT #: **P-35**

Sample Date: 8/1/22

Concrete Grade: **S2M, 3500HP**

Dates Test Represents: 8/2/2022 through 8/8/2022

Contractor: _____

MDOT No.: _____

Agg. Class	Pit #	Source	Weight (SSD)	ft ³	Specific Gravity	% Contribution
6AA	58-003	Stoneco	1650	9.83	2.69	53.2
26A	58-003	Stoneco	250	1.49	2.69	8.1
2NS	81-019	Pleasant Lake	1200	7.26	2.65	38.7
Total Wt			3100	18.58		100.0

<----- Verify this number is 100%




Superior Materials, LLC
 30701 W. 10 Mile Rd.
 Suite 500
 Farmington Hills, MI 48336

Sieve	6AA	26A	2NS	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	100.0	100.0	100.0	0.0	0.0
1.5"	100.0	100.0	100.0	100.0	0.0	0.0
1"	100.0	100.0	100.0	100.0	0.0	0.0
3/4"	79.7	100.0	100.0	89.2	10.8	10.8
1/2"	46.8	99.5	100.0	71.6	17.6	28.4
3/8"	17.8	84.0	100.0	55.0	16.7	45.0
#4	1.3	14.3	99.1	40.2	14.8	59.8
#8	0.9	4.6	85.3	33.9	6.3	66.1
#16	0.6	2.9	68.1	26.9	7.0	73.1
#30	0.5	2.2	51.0	20.2	6.7	79.8
#50	0.4	2.0	27.0	10.8	9.4	89.2
#100	0.4	1.9	8.8	3.8	7.1	96.2
LBW	0.4	1.6	1.6	1.0	2.8	99.0

*Maximum % Retained must be above the 3/8" sieve.
 *Any two adjacent sieves must equal 10% except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 4% for each sieve except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 8% for the 1" sieve when a 2" max. size (nom. Max. 1.5") aggregate is used.

Production Gradation Batch Plant Gradations Aggregate Supplier Gradations

Coarseness Factor:	68	Workability Factor:	34
---------------------------	-----------	----------------------------	-----------

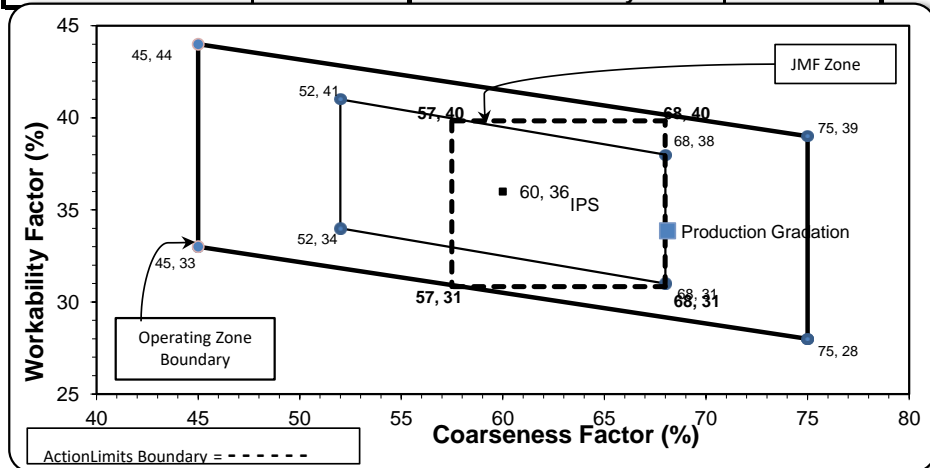

Initial Production Sample (IPS)

Sieve	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	0.0	0.0
1.5"	100.0	0.0	0.0
1"	99.2	0.8	0.8
3/4"	90.9	8.3	9.1
1/2"	71.3	19.6	28.7
3/8"	59.4	11.9	40.6
#4	43.0	16.5	57.0
#8	35.3	7.6	64.7
#16	28.2	7.1	71.8
#30	21.6	6.6	78.4
#50	9.1	12.5	90.9
#100	1.7	7.4	98.3
LBW	1.1	0.6	98.9

PREPARED BY:
 SM, LLC Technical Service

Approved By:

Aggregate Optimization Chart

PLANT #: **P-36**

Sample Date: 8/1/22

Concrete Grade: **S2M, 3500HP**

Contractor: _____

Dates Test Represents: 8/2/2022 through 8/8/2022

MDOT No.: _____

Agg. Class	Pit #	Source	Weight (SSD)	ft ³	Specific Gravity	% Contribution
6AA	71-47	Presque Isle	1550	9.48	2.62	50.8
26A	71-47	Presque Isle	300	1.83	2.62	9.8
2NS	63-92	Grange Hall	1200	7.26	2.65	39.3
Total Wt			3050	18.57		100.0

<----- Verify this number is 100%




Superior Materials, LLC
 30701 W. 10 Mile Rd.
 Suite 500
 Farmington Hills, MI 48336

Sieve	6AA	26A	2NS	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	100.0	100.0	100.0	0.0	0.0
1.5"	100.0	100.0	100.0	100.0	0.0	0.0
1"	98.5	100.0	100.0	99.2	0.8	0.8
3/4"	82.3	100.0	100.0	91.0	8.2	9.0
1/2"	39.5	95.5	100.0	68.8	22.2	31.2
3/8"	20.2	85.9	100.0	58.1	10.8	41.9
#4	2.2	28.8	94.7	41.2	16.8	58.8
#8	1.3	8.1	83.2	34.2	7.0	65.8
#16	1.1	3.7	68.4	27.8	6.4	72.2
#30	1.1	2.8	49.4	20.3	7.6	79.7
#50	1.0	2.5	19.2	8.3	12.0	91.7
#100	1.0	2.3	3.4	2.1	6.2	97.9
LBW	0.8	2.0	0.4	0.8	1.3	99.2

*Maximum % Retained must be above the 3/8" sieve.
 *Any two adjacent sieves must equal 10% except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 4% for each sieve except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 8% for the 1" sieve when a 2" max. size (nom. Max. 1.5") aggregate is used.

Production Gradation Batch Plant Gradations Aggregate Supplier Gradations

Coarseness Factor:	64	Workability Factor:	34
---------------------------	-----------	----------------------------	-----------

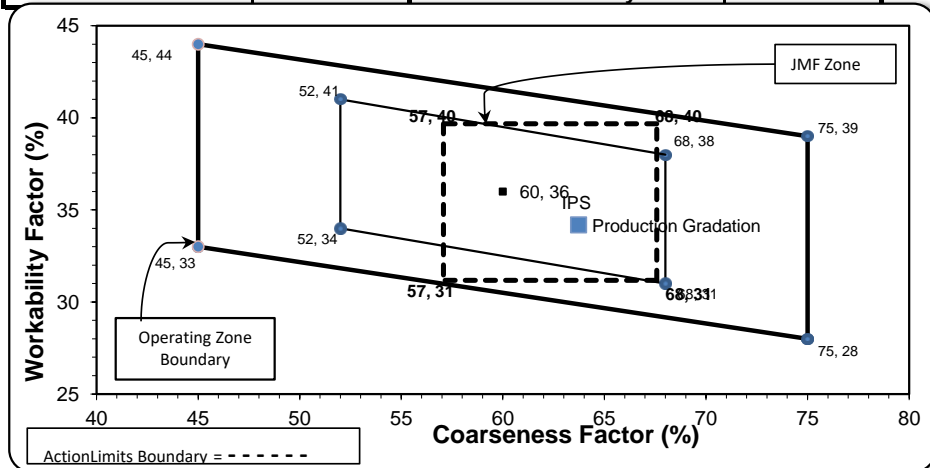

Initial Production Sample (IPS)

Coarseness Factor:	62
Workability Factor:	35

Sieve	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	0.0	0.0
1.5"	100.0	0.0	0.0
1"	99.1	0.9	0.9
3/4"	90.5	8.6	9.5
1/2"	69.8	20.7	30.2
3/8"	59.8	10.0	40.2
#4	42.2	17.6	57.8
#8	35.4	6.7	64.6
#16	28.8	6.7	71.2
#30	21.4	7.4	78.6
#50	8.8	12.6	91.2
#100	1.8	7.0	98.2
LBW	0.7	1.0	99.3

PREPARED BY:
 SM, LLC Technical Service

Approved By:

Aggregate Optimization Chart

PLANT #: **P-39**

Sample Date: 8/1/22

Concrete Grade: **S2M, 3500HP**

Dates Test Represents: 8/2/2022 through 8/8/2022

Contractor: _____

MDOT No.: _____

Agg. Class	Pit #	Source	Weight (SSD)	ft ³	Specific Gravity	% Contribution
6AA	71-47	Presque Isle	1600	9.79	2.62	52.5
26A	71-47	Presque Isle	200	1.22	2.62	6.6
2NS	44-051	Krake Willis Rd	1250	7.56	2.65	41.0
Total Wt			3050	18.57		100.0

<----- Verify this number is 100%




Superior Materials, LLC
 30701 W. 10 Mile Rd.
 Suite 500
 Farmington Hills, MI 48336

Sieve	6AA	26A	2NS	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	100.0	100.0	100.0	0.0	0.0
1.5"	100.0	100.0	100.0	100.0	0.0	0.0
1"	97.8	100.0	100.0	98.8	1.2	1.2
3/4"	85.3	100.0	100.0	92.3	6.6	7.7
1/2"	43.6	98.2	100.0	70.3	22.0	29.7
3/8"	21.9	86.2	100.0	58.1	12.2	41.9
#4	3.3	24.6	96.2	42.8	15.4	57.2
#8	2.0	5.8	80.2	34.3	8.5	65.7
#16	1.8	3.2	66.2	28.3	6.0	71.7
#30	1.6	2.6	50.4	21.7	6.6	78.3
#50	1.5	2.3	24.8	11.1	10.6	88.9
#100	1.4	2.1	6.4	3.5	7.6	96.5
LBW	1.3	1.8	0.4	1.0	2.5	99.0

*Maximum % Retained must be above the 3/8" sieve.
 *Any two adjacent sieves must equal 10% except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 4% for each sieve except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 8% for the 1" sieve when a 2" max. size (nom. Max. 1.5") aggregate is used.

Production Gradation Batch Plant Gradations Aggregate Supplier Gradations

Coarseness Factor:	64	Workability Factor:	34
---------------------------	-----------	----------------------------	-----------

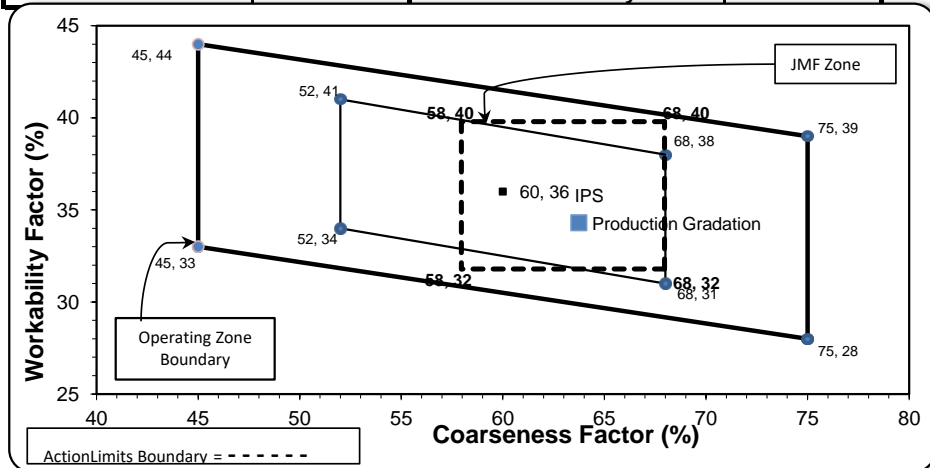

Initial Production Sample (IPS)

Coarseness Factor:	63		
Workability Factor:	36		
Sieve	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	0.0	0.0
1.5"	100.0	0.0	0.0
1"	100.0	0.0	0.0
3/4"	89.8	10.2	10.2
1/2"	70.7	19.1	29.3
3/8"	59.6	11.1	40.4
#4	43.2	16.4	56.8
#8	35.8	7.4	64.2
#16	29.2	6.6	70.8
#30	21.4	7.8	78.6
#50	9.8	11.6	90.2
#100	3.7	6.1	96.3
LBW	1.2	2.5	98.8

PREPARED BY:
 SM, LLC Technical Service

Approved By:

Aggregate Optimization Chart

PLANT #: P-02

Sample Date: 8/1/22

Concrete Grade: **S2M, 3500HP**

Dates Test Represents: 8/2/2022 through 8/8/2022

Contractor: _____

MDOT No.: _____



Superior Materials, LLC
30701 W. 10 Mile Rd.
Suite 500
Farmington Hills, MI 48336

Agg. Class	Pit #	Source	Weight (SSD)	ft ³	Specific Gravity	% Contribution
6AA	71-47	Presque Isle	1700	10.40	2.62	55.7
26A	71-47	Presque Isle	120	0.73	2.62	3.9
2NS	63-115	Ray Rd	1230	7.44	2.65	40.3
Total Wt			3050	18.57		100.0


<----- Verify this number is 100%

Sieve	6AA	26A	2NS	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	100.0	100.0	100.0	0.0	0.0
1.5"	100.0	100.0	100.0	100.0	0.0	0.0
1"	98.5	100.0	100.0	99.2	0.8	0.8
3/4"	82.3	100.0	100.0	90.1	9.0	9.9
1/2"	39.5	95.5	100.0	66.1	24.0	33.9
3/8"	20.2	85.9	100.0	55.0	11.1	45.0
#4	2.2	28.8	96.2	41.2	13.8	58.8
#8	1.3	8.1	76.6	31.9	9.2	68.1
#16	1.1	3.7	59.7	24.8	7.1	75.2
#30	1.1	2.8	43.9	18.4	6.4	81.6
#50	1.0	2.5	25.4	10.9	7.5	89.1
#100	1.0	2.3	7.6	3.7	7.2	96.3
LBW	0.8	2.0	1.5	1.1	2.6	98.9

*Maximum % Retained must be above the 3/8" sieve.
*Any two adjacent sieves must equal 10% except max., nom. max., #100 and #200 sieves.
*% Retained must be at least 4% for each sieve except max., nom. max., #100 and #200 sieves.
*% Retained must be at least 8% for the 1" sieve when a 2" max. size (nom. Max. 1.5") aggregate is used.

Production Gradation Batch Plant Gradations Aggregate Supplier Gradations

Coarseness Factor:	66	Workability Factor:	32
---------------------------	-----------	----------------------------	-----------

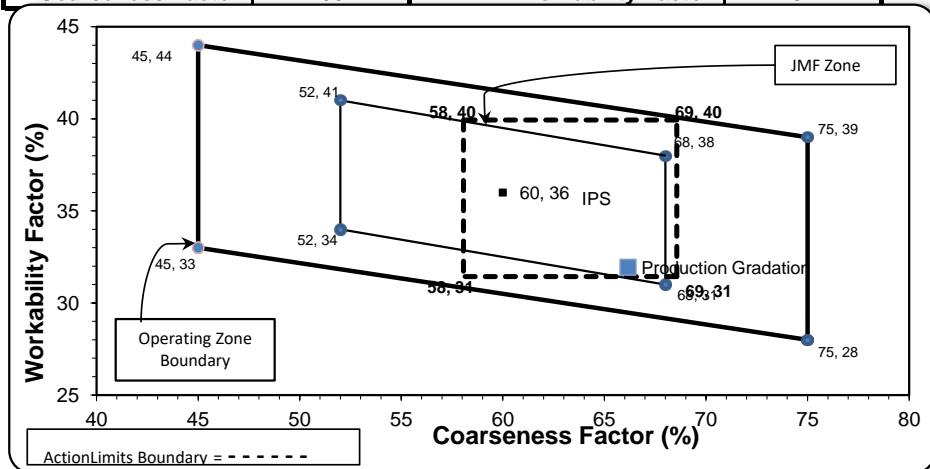

Initial Production Sample (IPS)

Coarseness Factor:	63		
Workability Factor:	36		
Sieve	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	0.0	0.0
1.5"	100.0	0.0	0.0
1"	100.0	0.0	0.0
3/4"	95.6	4.4	4.4
1/2"	73.1	22.6	26.9
3/8"	59.3	13.8	40.7
#4	42.8	16.5	57.2
#8	35.7	7.1	64.3
#16	28.9	6.8	71.1
#30	20.7	8.2	79.3
#50	9.9	10.8	90.1
#100	2.1	7.8	97.9
LBW	0.9	1.2	99.1

PREPARED BY:
SM, LLC Technical Service

Approved By:
