

Aggregate Optimization Chart

PLANT #: **P-32**

Sample Date: 12/28/20

Concrete Grade: **S2M**

Contractor: _____

Dates Test Represents: 12/29/2020 through 1/4/2021

MDOT No.: _____

Agg. Class	Pit #	Source	Weight (SSD)	ft ³	Specific Gravity	% Contribution
6AA	71-47	Presque Isle	1620	9.91	2.62	53.1
26A	71-47	Presque Isle	200	1.22	2.62	6.6
2NS	95-013	Smelter Bay	1230	7.44	2.65	40.3
Total Wt			3050	18.57		100.0

<---- Verify this number is 100%




Superior Materials, LLC
 30701 W. 10 Mile Rd.
 Suite 500
 Farmington Hills, MI 48336

Sieve	6AA	26A	2NS	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	100.0	100.0	100.0	0.0	0.0
1.5"	100.0	100.0	100.0	100.0	0.0	0.0
1"	98.3	100.0	100.0	99.1	0.9	0.9
3/4"	81.4	100.0	100.0	90.1	9.0	9.9
1/2"	45.3	98.1	100.0	70.8	19.3	29.2
3/8"	23.3	90.5	100.0	58.6	12.2	41.4
#4	6.9	19.9	96.1	43.7	14.9	56.3
#8	3.5	4.8	83.3	35.8	8.0	64.2
#16	2.6	2.8	66.9	28.5	7.2	71.5
#30	2.3	2.5	42.9	18.7	9.9	81.3
#50	2.1	2.4	22.1	10.2	8.5	89.8
#100	2.0	2.2	6.4	3.8	6.4	96.2
LBW	1.7	1.6	1.0	1.4	2.4	98.6

*Maximum % Retained must be above the 3/8" sieve.
 *Any two adjacent sieves must equal 10% except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 4% for each sieve except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 8% for the 1" sieve when a 2" max. size (nom. Max. 1.5") aggregate is used.

Production Gradation Batch Plant Gradations Aggregate Supplier Gradations

Coarseness Factor: **64** **Workability Factor:** **36**

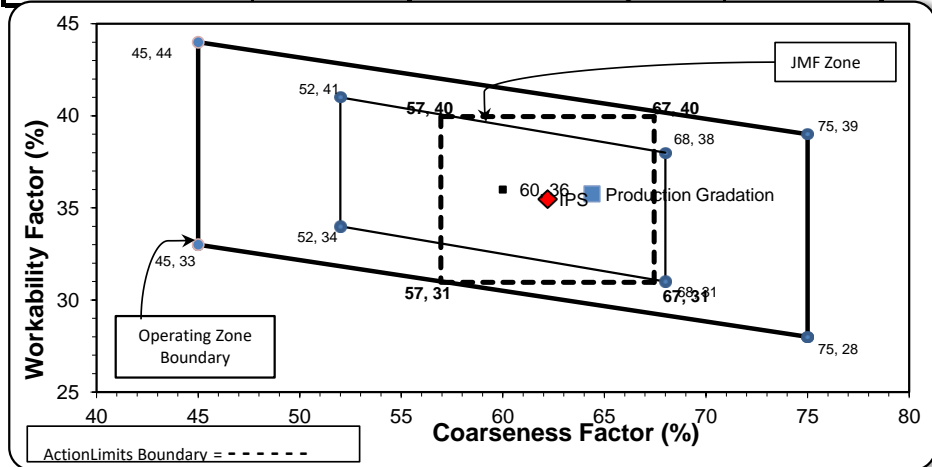

Initial Production Sample (IPS)

Coarseness Factor: **62**
Workability Factor: **35**

Sieve	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	0.0	0.0
1.5"	100.0	0.0	0.0
1"	100.0	0.0	0.0
3/4"	94.0	6.0	6.0
1/2"	70.2	23.7	29.8
3/8"	59.9	10.4	40.1
#4	42.7	17.2	57.3
#8	35.5	7.2	64.5
#16	28.4	7.0	71.6
#30	19.2	9.2	80.8
#50	8.9	10.3	91.1
#100	3.1	5.9	96.9
LBW	1.4	1.7	98.6

PREPARED BY:
 SM, LLC Technical Service

Approved By:

Aggregate Optimization Chart

PLANT #: **P-02**

Sample Date: 12/28/20

Concrete Grade: **S2M**

Contractor: _____

Dates Test Represents: 12/29/2020 through 1/4/2021

MDOT No.: _____

Agg. Class	Pit #	Source	Weight (SSD)	ft ³	Specific Gravity	% Contribution
6AA	71-47	Presque Isle	1650	10.09	2.62	54.1
26A	71-47	Presque Isle	100	0.61	2.62	3.3
2NS	63-115	Ray Rd	1300	7.86	2.65	42.6
Total Wt			3050	18.57		100.0

<----- Verify this number is 100%




Superior Materials, LLC
 30701 W. 10 Mile Rd.
 Suite 500
 Farmington Hills, MI 48336

Sieve	6AA	26A	2NS	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	100.0	100.0	100.0	0.0	0.0
1.5"	100.0	100.0	100.0	100.0	0.0	0.0
1"	98.6	100.0	100.0	99.2	0.8	0.8
3/4"	82.3	100.0	100.0	90.4	8.8	9.6
1/2"	49.3	98.1	100.0	72.5	17.9	27.5
3/8"	29.0	90.5	100.0	61.3	11.2	38.7
#4	6.1	19.9	95.6	44.7	16.6	55.3
#8	2.9	4.8	77.0	34.5	10.2	65.5
#16	2.4	2.8	59.7	26.8	7.7	73.2
#30	2.1	2.5	43.9	19.9	6.9	80.1
#50	1.9	2.4	20.5	9.8	10.1	90.2
#100	1.8	2.2	4.4	2.9	6.9	97.1
LBW	1.4	1.6	0.8	1.2	1.8	98.8

*Maximum % Retained must be above the 3/8" sieve.
 *Any two adjacent sieves must equal 10% except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 4% for each sieve except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 8% for the 1" sieve when a 2" max. size (nom. Max. 1.5") aggregate is used.

Production Gradation Batch Plant Gradations Aggregate Supplier Gradations

Coarseness Factor:	59	Workability Factor:	35
---------------------------	-----------	----------------------------	-----------

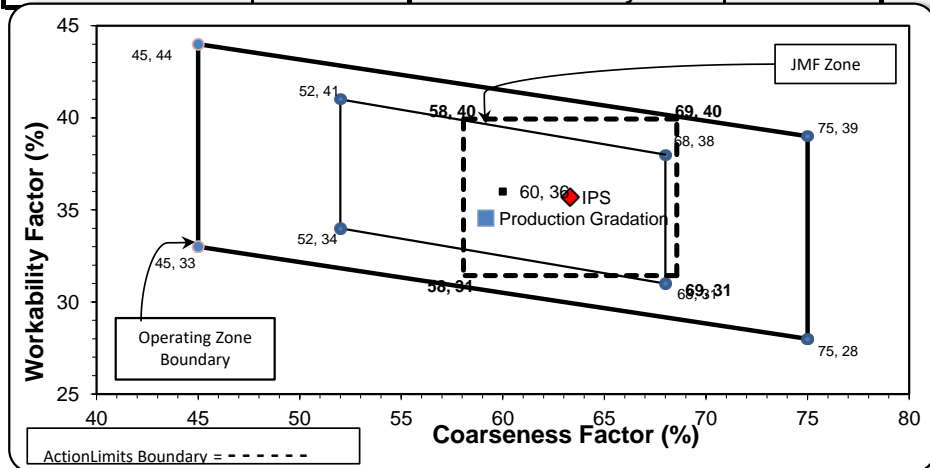

Initial Production Sample (IPS)

Coarseness Factor:	63		
Workability Factor:	36		
Sieve	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	0.0	0.0
1.5"	100.0	0.0	0.0
1"	100.0	0.0	0.0
3/4"	95.6	4.4	4.4
1/2"	73.1	22.6	26.9
3/8"	59.3	13.8	40.7
#4	42.8	16.5	57.2
#8	35.7	7.1	64.3
#16	28.9	6.8	71.1
#30	20.7	8.2	79.3
#50	9.9	10.8	90.1
#100	2.1	7.8	97.9
LBW	0.9	1.2	99.1

PREPARED BY:
 SM, LLC Technical Service

Approved By:
