

# Aggregate Optimization Chart

**PLANT #:** **P-20**

Sample Date: 6/14/21 Concrete Grade: **S2M**  
 Dates Test Represents: 6/15/2021 through 6/21/2021

Contractor: \_\_\_\_\_

MDOT No.: \_\_\_\_\_

Agg. Class	Pit #	Source	Weight (SSD)	ft <sup>3</sup>	Specific Gravity	% Contribution
6AA	71-47	Presque Isle	1600	9.79	2.62	52.5
26A	71-47	Presque Isle	200	1.22	2.62	6.6
2NS	63-92	Grange Hall	1250	7.56	2.65	41.0
<b>Total Wt</b>			<b>3050</b>	<b>18.57</b>		<b>100.0</b>

<----- Verify this number is 100%




**Superior Materials, LLC**  
 30701 W. 10 Mile Rd.  
 Suite 500  
 Farmington Hills, MI 48336

Sieve	6AA	26A	2NS	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	100.0	100.0	100.0	0.0	0.0
1.5"	100.0	100.0	100.0	100.0	0.0	0.0
1"	99.1	100.0	100.0	99.5	0.5	0.5
3/4"	83.3	100.0	100.0	91.2	8.3	8.8
1/2"	48.4	96.9	100.0	72.7	18.5	27.3
3/8"	27.9	88.9	100.0	61.4	11.3	38.6
#4	6.7	25.8	98.1	45.4	16.0	54.6
#8	2.9	6.0	85.5	37.0	8.5	63.0
#16	2.4	2.8	71.0	30.5	6.4	69.5
#30	2.2	2.4	50.8	22.1	8.4	77.9
#50	2.1	2.2	22.4	10.4	11.7	89.6
#100	2.0	2.0	2.4	2.2	8.3	97.8
LBW	1.8	1.8	0.5	1.3	0.9	98.7

\*Maximum % Retained must be above the 3/8" sieve.  
 \*Any two adjacent sieves must equal 10% except max., nom. max., #100 and #200 sieves.  
 \*% Retained must be at least 4% for each sieve except max., nom. max., #100 and #200 sieves.  
 \*% Retained must be at least 8% for the 1" sieve when a 2" max. size (nom. Max. 1.5") aggregate is used.

Production Gradation  Batch Plant Gradations  Aggregate Supplier Gradations

<b>Coarseness Factor:</b>	<b>61</b>	<b>Workability Factor:</b>	<b>37</b>
---------------------------	-----------	----------------------------	-----------

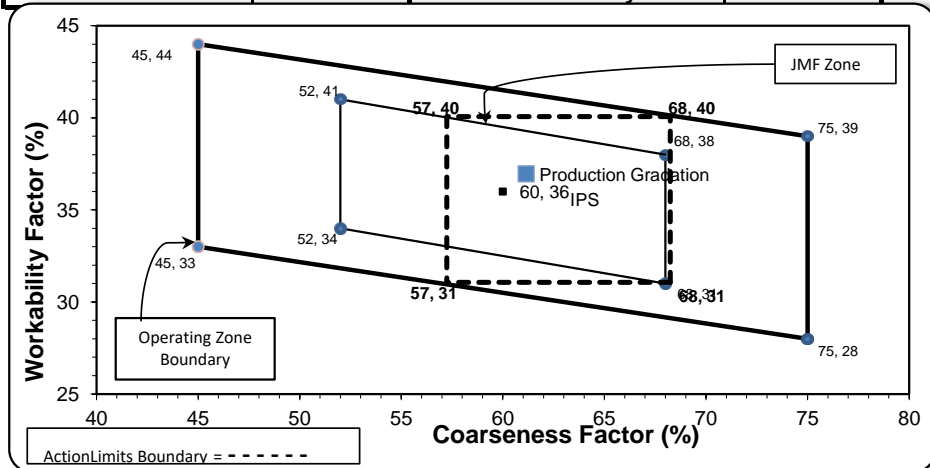

Initial Production Sample (IPS)

<b>Coarseness Factor:</b>	<b>63</b>		
<b>Workability Factor:</b>	<b>36</b>		
Sieve	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	0.0	0.0
1.5"	100.0	0.0	0.0
1"	100.0	0.0	0.0
3/4"	93.3	6.7	6.7
1/2"	70.6	22.6	29.4
3/8"	59.6	11.0	40.4
#4	43.9	15.7	56.1
#8	35.6	8.4	64.4
#16	28.4	7.2	71.6
#30	19.4	9.0	80.6
#50	7.5	11.9	92.5
#100	0.9	6.6	99.1
LBW	0.9	0.1	99.1

PREPARED BY:  
 SM, LLC Technical Service

Approved By:

# Aggregate Optimization Chart

**PLANT #:** **P-32**

Sample Date: 6/14/21 Concrete Grade: **S2M**  
 Dates Test Represents: 6/15/2021 through 6/21/2021

Contractor: \_\_\_\_\_

MDOT No.: \_\_\_\_\_

Agg. Class	Pit #	Source	Weight (SSD)	ft <sup>3</sup>	Specific Gravity	% Contribution
6AA	71-47	Presque Isle	1500	9.17	2.62	49.2
26A	71-47	Presque Isle	320	1.96	2.62	10.5
2NS	95-013	Smelter Bay	1230	7.44	2.65	40.3
<b>Total Wt</b>			<b>3050</b>	<b>18.57</b>		<b>100.0</b>

<----- Verify this number is 100%




**Superior Materials, LLC**  
 30701 W. 10 Mile Rd.  
 Suite 500  
 Farmington Hills, MI 48336

Sieve	6AA	26A	2NS	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	100.0	100.0	100.0	0.0	0.0
1.5"	100.0	100.0	100.0	100.0	0.0	0.0
1"	99.7	100.0	100.0	99.9	0.1	0.1
3/4"	86.4	100.0	100.0	93.3	6.5	6.7
1/2"	47.8	97.5	100.0	74.1	19.2	25.9
3/8"	24.1	89.4	100.0	61.6	12.5	38.4
#4	3.8	27.5	96.4	43.6	17.9	56.4
#8	2.7	9.3	83.6	36.0	7.6	64.0
#16	2.2	4.7	66.5	28.4	7.6	71.6
#30	2.1	3.3	45.8	19.8	8.5	80.2
#50	1.9	2.5	23.7	10.8	9.1	89.2
#100	1.8	2.1	8.1	4.4	6.4	95.6
LBW	1.4	1.7	1.1	1.3	3.1	98.7

\*Maximum % Retained must be above the 3/8" sieve.  
 \*Any two adjacent sieves must equal 10% except max., nom. max., #100 and #200 sieves.  
 \*% Retained must be at least 4% for each sieve except max., nom. max., #100 and #200 sieves.  
 \*% Retained must be at least 8% for the 1" sieve when a 2" max. size (nom. Max. 1.5") aggregate is used.

Production Gradation  Batch Plant Gradations  Aggregate Supplier Gradations

**Coarseness Factor:** **60** **Workability Factor:** **36**

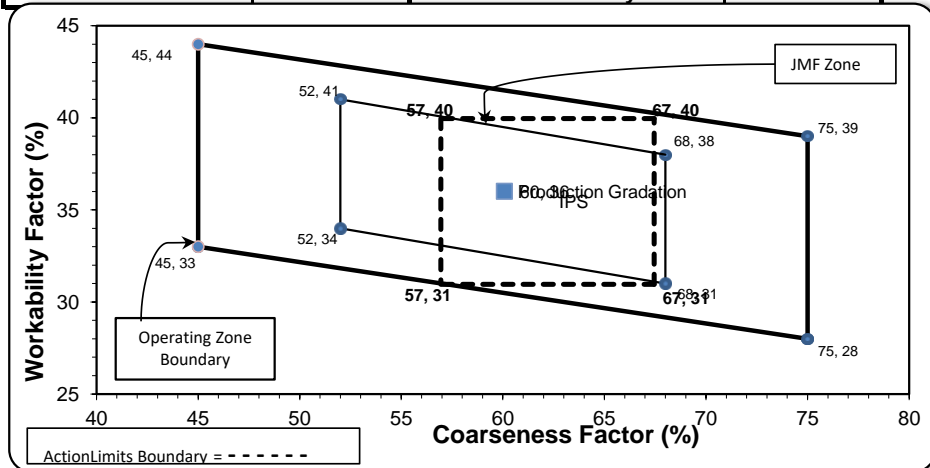

Initial Production Sample (IPS)

**Coarseness Factor:** **62**  
**Workability Factor:** **35**

Sieve	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	0.0	0.0
1.5"	100.0	0.0	0.0
1"	100.0	0.0	0.0
3/4"	94.0	6.0	6.0
1/2"	70.2	23.7	29.8
3/8"	59.9	10.4	40.1
#4	42.7	17.2	57.3
#8	35.5	7.2	64.5
#16	28.4	7.0	71.6
#30	19.2	9.2	80.8
#50	8.9	10.3	91.1
#100	3.1	5.9	96.9
LBW	1.4	1.7	98.6

PREPARED BY:  
 SM, LLC Technical Service

Approved By:

# Aggregate Optimization Chart

**PLANT #:** **P-35**

Sample Date: 6/14/21 Concrete Grade: **S2M**

Dates Test Represents: 6/15/2021 through 6/21/2021

Contractor: \_\_\_\_\_

MDOT No.: \_\_\_\_\_

Agg. Class	Pit #	Source	Weight (SSD)	ft <sup>3</sup>	Specific Gravity	% Contribution
6AA	58-003	Stoneco	1575	9.38	2.69	50.8
26A	58-003	Stoneco	325	1.94	2.69	10.5
2NS	81-093	Burmeister	1200	7.26	2.65	38.7
<b>Total Wt</b>			<b>3100</b>	<b>18.58</b>		<b>100.0</b>

<----- Verify this number is 100%




**Superior Materials, LLC**  
 30701 W. 10 Mile Rd.  
 Suite 500  
 Farmington Hills, MI 48336

Sieve	6AA	26A	2NS	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	100.0	100.0	100.0	0.0	0.0
1.5"	100.0	100.0	100.0	100.0	0.0	0.0
1"	99.1	100.0	100.0	99.5	0.5	0.5
3/4"	76.8	100.0	100.0	88.2	11.3	11.8
1/2"	39.9	99.4	100.0	69.4	18.8	30.6
3/8"	17.6	89.2	100.0	57.0	12.4	43.0
#4	3.1	6.6	97.4	40.0	17.0	60.0
#8	1.5	1.4	89.0	35.4	4.6	64.6
#16	1.3	1.0	69.6	27.7	7.7	72.3
#30	1.1	0.9	49.6	19.9	7.9	80.1
#50	1.0	0.8	18.1	7.6	12.3	92.4
#100	0.9	0.8	4.0	2.1	5.5	97.9
LBW	0.8	0.5	0.8	0.8	1.3	99.2

\*Maximum % Retained must be above the 3/8" sieve.  
 \*Any two adjacent sieves must equal 10% except max., nom. max., #100 and #200 sieves.  
 \*% Retained must be at least 4% for each sieve except max., nom. max., #100 and #200 sieves.  
 \*% Retained must be at least 8% for the 1" sieve when a 2" max. size (nom. Max. 1.5") aggregate is used.

Production Gradation  Batch Plant Gradations  Aggregate Supplier Gradations

<b>Coarseness Factor:</b>	<b>67</b>	<b>Workability Factor:</b>	<b>35</b>
---------------------------	-----------	----------------------------	-----------

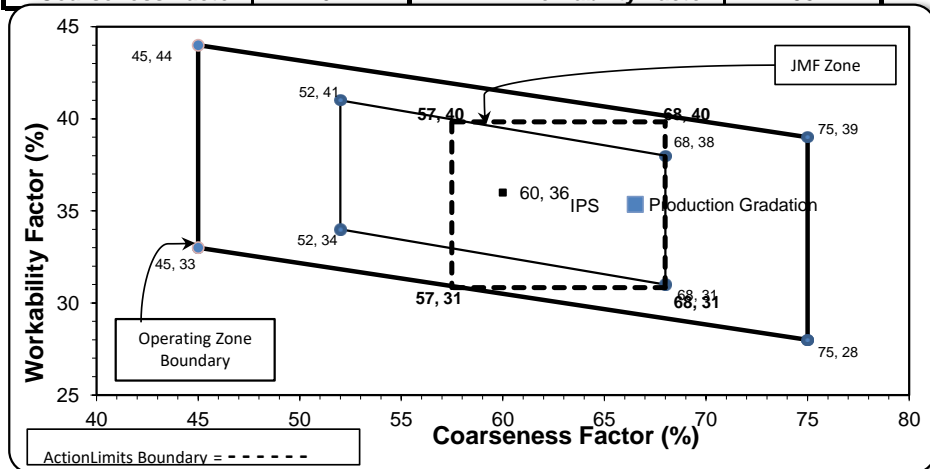

Intial Production Sample (IPS)

<b>Coarseness Factor:</b>	<b>63</b>
<b>Workability Factor:</b>	<b>35</b>

Sieve	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	0.0	0.0
1.5"	100.0	0.0	0.0
1"	99.2	0.8	0.8
3/4"	90.9	8.3	9.1
1/2"	71.3	19.6	28.7
3/8"	59.4	11.9	40.6
#4	43.0	16.5	57.0
#8	35.3	7.6	64.7
#16	28.2	7.1	71.8
#30	21.6	6.6	78.4
#50	9.1	12.5	90.9
#100	1.7	7.4	98.3
LBW	1.1	0.6	98.9

PREPARED BY:  
 SM, LLC Technical Service

Approved By:

# Aggregate Optimization Chart

**PLANT #:** **P-02**

Sample Date: 6/14/21 Concrete Grade: **S2M**  
 Dates Test Represents: 6/15/2021 through 6/21/2021

Contractor: \_\_\_\_\_

MDOT No.: \_\_\_\_\_

Agg. Class	Pit #	Source	Weight (SSD)	ft <sup>3</sup>	Specific Gravity	% Contribution
6AA	71-47	Presque Isle	1500	9.17	2.62	49.2
26A	71-47	Presque Isle	300	1.83	2.62	9.8
2NS	63-115	Ray Rd	1250	7.56	2.65	41.0
<b>Total Wt</b>			<b>3050</b>	<b>18.57</b>		<b>100.0</b>

<----- Verify this number is 100%




**Superior Materials, LLC**  
 30701 W. 10 Mile Rd.  
 Suite 500  
 Farmington Hills, MI 48336

Sieve	6AA	26A	2NS	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	100.0	100.0	100.0	0.0	0.0
1.5"	100.0	100.0	100.0	100.0	0.0	0.0
1"	98.1	100.0	100.0	99.1	0.9	0.9
3/4"	79.1	100.0	100.0	89.7	9.3	10.3
1/2"	37.0	97.5	100.0	68.8	21.0	31.2
3/8"	18.7	89.4	100.0	59.0	9.8	41.0
#4	4.6	27.5	96.9	44.7	14.3	55.3
#8	2.8	9.3	81.7	35.8	8.9	64.2
#16	2.4	4.7	66.8	29.0	6.8	71.0
#30	2.2	3.3	49.8	21.8	7.2	78.2
#50	2.0	2.5	24.9	11.4	10.4	88.6
#100	1.9	2.1	5.6	3.4	8.0	96.6
LBW	1.6	1.7	0.8	1.3	2.2	98.7

\*Maximum % Retained must be above the 3/8" sieve.  
 \*Any two adjacent sieves must equal 10% except max., nom. max., #100 and #200 sieves.  
 \*% Retained must be at least 4% for each sieve except max., nom. max., #100 and #200 sieves.  
 \*% Retained must be at least 8% for the 1" sieve when a 2" max. size (nom. Max. 1.5") aggregate is used.

Production Gradation  Batch Plant Gradations  Aggregate Supplier Gradations

<b>Coarseness Factor:</b>	<b>64</b>	<b>Workability Factor:</b>	<b>36</b>
---------------------------	-----------	----------------------------	-----------

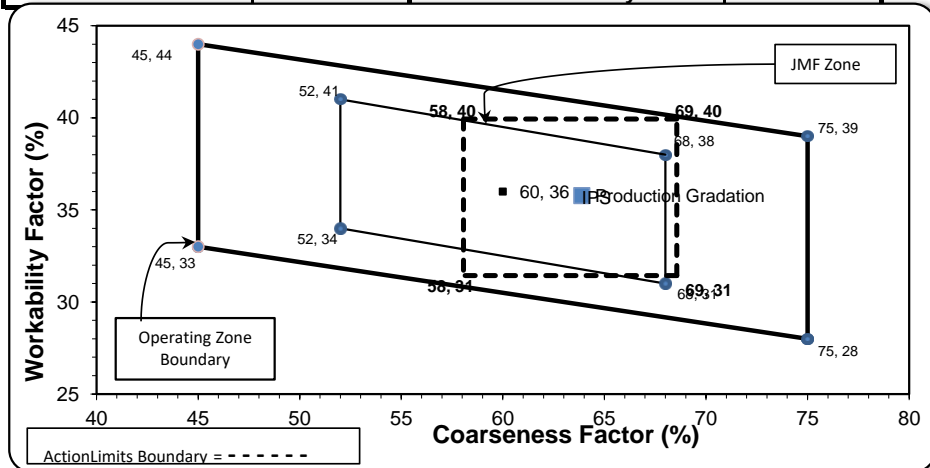

Initial Production Sample (IPS)

<b>Coarseness Factor:</b>	<b>63</b>
<b>Workability Factor:</b>	<b>36</b>

Sieve	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	0.0	0.0
1.5"	100.0	0.0	0.0
1"	100.0	0.0	0.0
3/4"	95.6	4.4	4.4
1/2"	73.1	22.6	26.9
3/8"	59.3	13.8	40.7
#4	42.8	16.5	57.2
#8	35.7	7.1	64.3
#16	28.9	6.8	71.1
#30	20.7	8.2	79.3
#50	9.9	10.8	90.1
#100	2.1	7.8	97.9
LBW	0.9	1.2	99.1

PREPARED BY:  
 SM, LLC Technical Service

Approved By:
