

Aggregate Optimization Chart

Production Gradation Report

PLANT #: **P-103**

Sample Date: 11/10/25

Concrete Grade: **S2M, 3500HP**

Dates Test Represents: 11/11/2025 through 11/17/2025

Contractor: _____

MDOT No.: _____

Agg. Class	Pit #	Source	Weight (SSD)	ft ³	Specific Gravity	% Contribution
6AA	58-003	Stoneco	1650	9.83	2.69	53.2
26A	58-003	Stoneco	250	1.49	2.69	8.1
2NS	63-114	Highland	1200	7.26	2.65	38.7
Total Wt			3100	18.58		100.0

<----- Verify this number is 100%

Sieve	6AA	26A	2NS	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	100.0	100.0	100.0	0.0	0.0
1.5"	100.0	100.0	100.0	100.0	0.0	0.0
1"	99.7	100.0	100.0	99.8	0.2	0.2
3/4"	84.7	100.0	100.0	91.9	8.0	8.1
1/2"	41.4	99.7	100.0	68.8	23.1	31.2
3/8"	24.4	80.6	100.0	58.2	10.6	41.8
#4	4.2	5.8	99.0	41.0	17.2	59.0
#8	1.9	2.0	84.2	33.8	7.3	66.2
#16	1.7	1.6	65.0	26.2	7.6	73.8
#30	1.6	1.4	43.3	17.7	8.5	82.3
#50	1.4	1.2	19.7	8.5	9.3	91.5
#100	1.3	1.0	3.6	2.2	6.3	97.8
LBW	1.1	0.8	0.6	0.9	1.3	99.1

*Maximum % Retained must be above the 3/8" sieve.

*Any two adjacent sieves must equal 10% except max.,

nom. max., #100 and #200 sieves.

*% Retained must be at least 4% for each sieve except max.,

nom. max., #100 and #200 sieves.

*% Retained must be at least 4% for the 3/4" sieve when

a 1.5" max. size (nom. Max. 1.0") aggregate is used.



Superior Materials, LLC


30701 W. 10 Mile Rd.

Suite 500

Farmington Hills, MI 48336

Production Gradation ☐ Batch Plant Gradations ☒ Aggregate Supplier Gradations

Coarseness Factor:	63	Workability Factor:	34
---------------------------	-----------	----------------------------	-----------

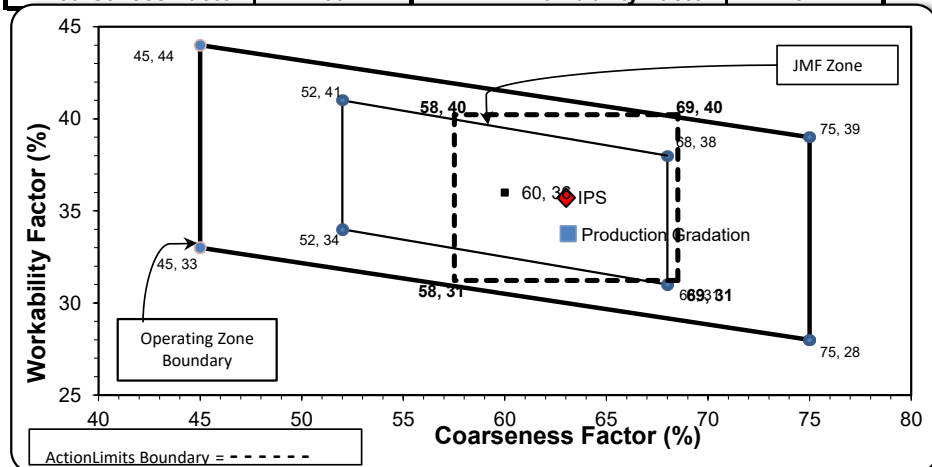

Initial Production Sample (IPS)

Coarseness Factor:		63	
Workability Factor:		36	
Sieve	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	0.0	0.0
1.5"	100.0	0.0	0.0
1"	99.2	0.8	0.8
3/4"	90.9	8.3	9.1
1/2"	71.3	19.6	28.7
3/8"	59.5	11.8	40.5
#4	43.8	15.7	56.2
#8	35.7	8.1	64.3
#16	27.0	8.7	73.0
#30	18.6	8.4	81.4
#50	6.8	11.8	93.2
#100	1.4	5.4	98.6
LBW	0.6	0.8	99.4

PREPARED BY:
SM, LLC Technical Service

Approved BY:

Aggregate Optimization Chart

Production Gradation Report

PLANT #: **p11**

Sample Date: 11/10/25

Concrete Grade: **S2M, 3500HP**

Dates Test Represents: 11/11/2025 through 11/17/2025

Contractor: _____

MDOT No.: _____

Agg. Class	Pit #	Source	Weight (SSD)	ft ³	Specific Gravity	% Contribution
6AA	71-47	Presque Isle	1520	9.30	2.62	49.8
26A	71-47	Presque Isle	300	1.83	2.62	9.8
2NS	63-115	Ray Rd	1230	7.44	2.65	40.3
Total Wt			3050	18.57		100.0

<----- Verify this number is 100%

Sieve	6AA	26A	2NS	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	100.0	100.0	100.0	0.0	0.0
1.5"	100.0	100.0	100.0	100.0	0.0	0.0
1"	97.4	100.0	100.0	98.7	1.3	1.3
3/4"	79.0	100.0	100.0	89.5	9.2	10.5
1/2"	37.9	98.8	100.0	68.9	20.6	31.1
3/8"	20.3	86.8	100.0	59.0	10.0	41.0
#4	3.4	17.7	97.5	42.8	16.2	57.2
#8	2.0	4.7	83.1	35.0	7.8	65.0
#16	1.8	2.5	62.7	26.4	8.5	73.6
#30	1.6	2.1	43.6	18.6	7.8	81.4
#50	1.6	2.0	20.0	9.1	9.5	90.9
#100	1.5	1.9	4.2	2.6	6.4	97.4
LBW	1.2	1.8	0.9	1.1	1.5	98.9

*Maximum % Retained must be above the 3/8" sieve.

*Any two adjacent sieves must equal 10% except max.,

nom. max., #100 and #200 sieves.

*% Retained must be at least 4% for each sieve except max.,

nom. max., #100 and #200 sieves.

*% Retained must be at least 4% for the 3/4" sieve when

a 1.5" max. size (nom. Max. 1.0") aggregate is used.



Superior Materials, LLC


30701 W. 10 Mile Rd.

Suite 500

Farmington Hills, MI 48336

Production Gradation ☐ Batch Plant Gradations ☒ Aggregate Supplier Gradations

Coarseness Factor:	63	Workability Factor:	35
---------------------------	-----------	----------------------------	-----------

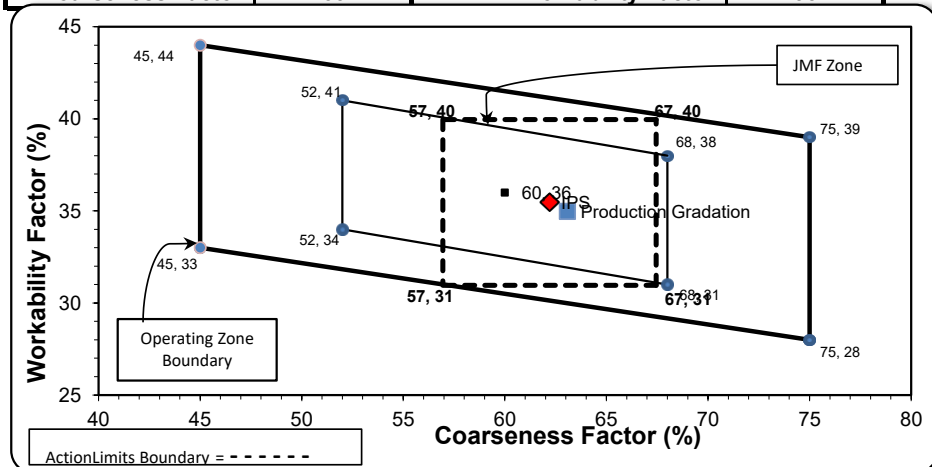

Initial Production Sample (IPS)

Coarseness Factor:		62	
Workability Factor:		35	
Sieve	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	0.0	0.0
1.5"	100.0	0.0	0.0
1"	100.0	0.0	0.0
3/4"	94.0	6.0	6.0
1/2"	70.2	23.7	29.8
3/8"	59.9	10.4	40.1
#4	42.7	17.2	57.3
#8	35.5	7.2	64.5
#16	28.4	7.0	71.6
#30	19.2	9.2	80.8
#50	8.9	10.3	91.1
#100	3.1	5.9	96.9
LBW	1.4	1.7	98.6

PREPARED BY:
SM, LLC Technical Service

Approved By:

Aggregate Optimization Chart

Production Gradation Report

PLANT #: **P-O2**

Sample Date: 11/10/25

Concrete Grade: **S2M, 3500HP**

Dates Test Represents: 11/11/2025 through 11/17/2025

Contractor: _____

MDOT No.: _____

Agg. Class	Pit #	Source	Weight (SSD)	ft ³	Specific Gravity	% Contribution
6AA	71-47	Presque Isle	1520	9.30	2.62	49.8
26A	71-47	Presque Isle	300	1.83	2.62	9.8
2NS	63-115	Ray Rd	1230	7.44	2.65	40.3
Total Wt			3050	18.57		100.0

<----- Verify this number is 100%

Sieve	6AA	26A	2NS	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	100.0	100.0	100.0	0.0	0.0
1.5"	100.0	100.0	100.0	100.0	0.0	0.0
1"	97.4	100.0	100.0	98.7	1.3	1.3
3/4"	79.0	100.0	100.0	89.5	9.2	10.5
1/2"	37.9	98.8	100.0	68.9	20.6	31.1
3/8"	20.3	86.8	100.0	59.0	10.0	41.0
#4	3.4	17.7	97.5	42.8	16.2	57.2
#8	2.0	4.7	83.1	35.0	7.8	65.0
#16	1.8	2.5	62.7	26.4	8.5	73.6
#30	1.6	2.1	43.6	18.6	7.8	81.4
#50	1.6	2.0	20.0	9.1	9.5	90.9
#100	1.5	1.9	4.2	2.6	6.4	97.4
LBW	1.2	1.8	0.9	1.1	1.5	98.9

*Maximum % Retained must be above the 3/8" sieve.

*Any two adjacent sieves must equal 10% except max.,

nom. max., #100 and #200 sieves.

*% Retained must be at least 4% for each sieve except max.,

nom. max., #100 and #200 sieves.

*% Retained must be at least 4% for the 3/4" sieve when

a 1.5" max. size (nom. Max. 1.0") aggregate is used.



Superior Materials, LLC


30701 W. 10 Mile Rd.

Suite 500

Farmington Hills, MI 48336

Production Gradation ☐ Batch Plant Gradations ☒ Aggregate Supplier Gradations

Coarseness Factor:	63	Workability Factor:	35
---------------------------	-----------	----------------------------	-----------

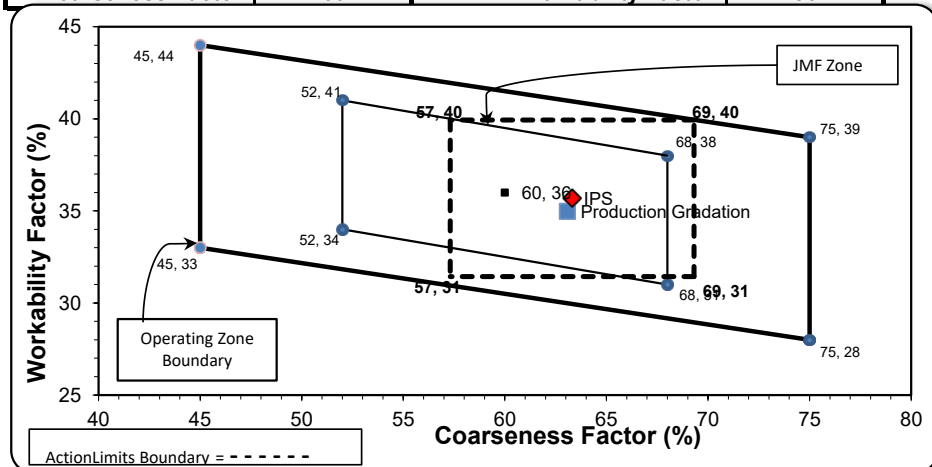

Initial Production Sample (IPS)

Coarseness Factor:		63	
Workability Factor:		36	
Sieve	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	0.0	0.0
1.5"	100.0	0.0	0.0
1"	100.0	0.0	0.0
3/4"	95.6	4.4	4.4
1/2"	73.1	22.6	26.9
3/8"	59.3	13.8	40.7
#4	42.8	16.5	57.2
#8	35.7	7.1	64.3
#16	28.9	6.8	71.1
#30	20.7	8.2	79.3
#50	9.9	10.8	90.1
#100	2.1	7.8	97.9
LBW	0.9	1.2	99.1

PREPARED BY:
SM, LLC Technical Service

Approved By:

[Signature]
